



KARACHI WATER & SEWERAGE BOARD

OFFICE OF THE EXECUTIVE ENGINEER (SEW) GULSHAN-E-IQBAL (TOWN)
ST-2, BLOCK-14, SCHEME-24, MAIN UNIVERSITY ROAD NEAR CIVIC CENTER

NO.EE/GIT/SEW/KW&SB/2013-14/ 39

DATED: 07-4-2014

M/S FAKHAR & BROTHERS
Government Contractor
Karachi

WORK ORDER / L.O.C.

SUBJECT:

REHABILITATION / REPLACEMENT OF 15", 12" AND 8" DIA SUNK DOWN / BROKEN SEWERAGE LINES AT DIFFERENT LOCATIONS IN UNION COUNCIL NOS. 05, 09 & 11 OF GULSHAN-E-IQBAL TOWN.

Your tender dated: 13-02-2014, has been approved by the Competent Authority, KW&SB on item rate basis for amounting to **Rs.9,95,141/= (Rupees Nine lac Ninety five thousand one hundred and forty one Only)**. You are therefore requested to start the above mentioned work as per design and specification.

The work is to be completed with (20) days, failing which penalty of Rs.500/= per day will be imposed/recovered as per terms and conditions of the contract.

You are further requested to contact the concerned A.E.E., in connection with commencement of supervision for necessary instruction of the work.


EXECUTIVE ENGINEER (SEW)
GULSHAN-E-IQBAL TOWN
KW&SB

Copy to:-

1. The Chief Engineer (East), KW&SB.
2. Superintending Engineer, (Gulshan Town), KW&SB.
3. Accountant Officer, (Gulshan Town), KW&SB.
4. A.O. (Budget)
5. Office Copy.

SINDH PUBLIC PROCUREMENT REGULATORY AUTHORITY

CONTRACT EVALUATION FORM

TO BE FILLED IN BY ALL PROCURING AGENCIES FOR PUBLIC CONTRACTS OF WORKS, SERVICES & GOODS

- 1) NAME OF THE ORGANIZATION / DEPT. I. KARACHI WATER & SEWERAGE BOARD
- 2) PROVINCIAL / LOCAL GOVT / OTHER -----
- 3) TITLE OF CONTRACT REPLACEMENT OF 15", 12 & 8" DIA IN UC-05-09&11 G.I.T
- 4) TENDER NUMBER SPPRA Sr No.18744 I.D No
- 5) BRIEF DESCRIPTION OF CONTRACT REPLACEMENT OF 15", 12 & 8" DIA IN UC-05-09&11 G.I.T
- 6) FORUM THAT APPROVED THE SCHEME Managing Director KW&SB
- 7) TENDER ESTIMATED VALUE Rs.9,95,141/=
- 8) ENGINEER'S ESTIMATE (For civil works only) Rs.9,95,210/=
- 9) ESTIMATED COMPLETION PERIOD (AS PER CONTRACT) 20 days
- 10) TENDER OPENED ON (DATE & TIME) 13-02-2014
- 11) NUMBER OF TENDER DOCUMENTS SOLD (Attach list of buyers) 3 (THREE)
- 12) NUMBER OF BIDS RECEIVED 3 (THREE)
- 13) NUMBER OF BIDDERS PRESENT AT THE TIME OF OPENING OF BIDS 3 (THREE)
- 14) BID EVALUATION REPORT (Enclose a copy) Copy Attached
- 15) NAME AND ADDRESS OF THE SUCCESSFUL BIDDER M/S FAKHAR & BROTHERS
- 16) CONTRACT AWARD PRICE Rs.9,95,141/=
- 17) RANKING OF SUCCESSFUL BIDDER IN EVALUATION REPORT (i.e. 1st, 2nd, 3rd EVALUATION BID).
M/S FAKHAR & BROTHERS
M/S BEHZAD ENTERPRISES
M/S UNIVERSAL ENTERPRISES
- 18) METHOD OF PROCUREMENT USED : - (Tick one)
- a) SINGLE STAGE - ONE ENVELOPE PROCEDURE Domestic/ Local
- b) SINGLE STAGE - TWO ENVELOPE PROCEDURE
- c) TWO STAGE BIDDING PROCEDURE
- d) TWO STAGE - TWO ENVELOPE BIDDING PROCEDURE

PLEASE SPECIFY IF ANY OTHER METHOD OF PROCUREMENT WAS ADOPTED i.e. EMERGENCY, DIRECT CONTRACTING ETC WITH BRIEF REASONS

19) APPROVING AUTHORITY FOR AWARD OF CONTRACT _____

20) WHETHER THE PROCUREMENT WAS INCLUDED IN ANNUAL PROCUREMENT PLAN?

Yes	<input checked="" type="checkbox"/>	No	<input type="checkbox"/>
-----	-------------------------------------	----	--------------------------

21) ADVERTISEMENT :

i) SPPRA Website
(If yes, give date and SPPRA Identification No.)

Yes	Serial No 17494
<input checked="" type="checkbox"/>	
No	

ii) News Papers
(If yes, give names of newspapers and dates)

Yes	
<input type="checkbox"/>	
No	<input checked="" type="checkbox"/>

22) NATURE OF CONTRACT

Domestic / Local	<input checked="" type="checkbox"/>	Int.	<input type="checkbox"/>
------------------	-------------------------------------	------	--------------------------

23) WHETHER QUALIFICATION CRITERIA WAS INCLUDED IN BIDDING / TENDER DOCUMENTS?
(If yes, enclose a copy)

Yes	<input type="checkbox"/>	No	<input checked="" type="checkbox"/>
-----	--------------------------	----	-------------------------------------

24) WHETHER BID EVALUATION CRITERIA WAS INCLUDED IN BIDDING / TENDER DOCUMENTS?
(If yes, enclose a copy)

Yes	<input type="checkbox"/>	No	<input checked="" type="checkbox"/>
-----	--------------------------	----	-------------------------------------

25) WHETHER APPROVAL OF COMPETENT AUTHORITY WAS OBTAINED FOR USING A METHOD OTHER THAN OPEN COMPETITIVE BIDDING?

Yes	<input type="checkbox"/>	No	<input checked="" type="checkbox"/>
-----	--------------------------	----	-------------------------------------

26) WAS BID SECURITY OBTAINED FROM ALL THE BIDDERS?

Yes	<input checked="" type="checkbox"/>	No	<input type="checkbox"/>
-----	-------------------------------------	----	--------------------------

27) WHETHER THE SUCCESSFUL BID WAS LOWEST EVALUATED BID / BEST EVALUATED BID (in case of Consultancies)

Yes	<input checked="" type="checkbox"/>	No	<input type="checkbox"/>
-----	-------------------------------------	----	--------------------------

28) WHETHER THE SUCCESSFUL BIDDER WAS TECHNICALLY COMPLIANT?

Yes	<input checked="" type="checkbox"/>	No	<input type="checkbox"/>
-----	-------------------------------------	----	--------------------------

29) WHETHER NAMES OF THE BIDDERS AND THEIR QUOTED PRICES WERE READ OUT AT THE TIME OF OPENING OF BIDS?

Yes	<input checked="" type="checkbox"/>	No	<input type="checkbox"/>
-----	-------------------------------------	----	--------------------------

30) WHETHER EVALUATION REPORT GIVEN TO BIDDERS BEFORE THE AWARD OF CONTRACT?
(Attach copy of the bid evaluation report)

Yes	<input checked="" type="checkbox"/>	No	<input type="checkbox"/>
-----	-------------------------------------	----	--------------------------

31) ANY COMPLAINTS RECEIVED
(If yes, result thereof)

Yes	
No	<input checked="" type="checkbox"/>

32) ANY DEVIATION FROM SPECIFICATIONS GIVEN IN THE TENDER NOTICE / DOCUMENTS
(If yes, give details)

Yes	
No	<input checked="" type="checkbox"/>

33) WAS THE EXTENSION MADE IN RESPONSE TIME?
(If yes, give reasons)

Yes	
No	<input checked="" type="checkbox"/>

34) DEVIATION FROM QUALIFICATION CRITERIA
(If yes, give detailed reasons.)

Yes	
No	<input checked="" type="checkbox"/>

35) WAS IT ASSURED BY THE PROCURING AGENCY THAT THE SELECTED FIRM IS NOT BLACK LISTED?

Yes	<input checked="" type="checkbox"/>	No	<input type="checkbox"/>
-----	-------------------------------------	----	--------------------------

36) WAS A VISIT MADE BY ANY OFFICER/OFFICIAL OF THE PROCURING AGENCY TO THE SUPPLIER'S PREMISES IN CONNECTION WITH THE PROCUREMENT? IF SO, DETAILS TO BE ASCERTAINED REGARDING FINANCING OF VISIT, IF ABROAD:
(If yes, enclose a copy)

Yes	<input type="checkbox"/>	No	<input checked="" type="checkbox"/>
-----	--------------------------	----	-------------------------------------

37) WERE PROPER SAFEGUARDS PROVIDED ON MOBILIZATION ADVANCE PAYMENT IN THE CONTRACT (BANK GUARANTEE ETC.)?

Yes	<input type="checkbox"/>	No	<input checked="" type="checkbox"/>
-----	--------------------------	----	-------------------------------------

38) SPECIAL CONDITIONS, IF ANY
(If yes, give Brief Description)

Yes	
No	<input checked="" type="checkbox"/>

39) Date of Award of Contract: _____

Signature & Official Stamp of
Authorized Officer

Pyed Ejaz Ahmad
EXECUTIVE ENGINEER (SEW)

FOR OFFICE USE ONLY Gulshan-e-Iqbal (Town) K.W. & S.B.

SPPRA, Block. No.8, Sindh Secretariat No.4-A, Court Road, Karachi
Tele: 021-9205356; 021-9205369 & Fax: 021-9206291

Print

Save

Reset

2

OFFICE OF THE EXECUTIVE ENGINEER (S&W) GULSHAN-E-IQBAL (TOWN)
KARACHI WATER AND SEWERAGE BAOR

SCHEDULE "B"

NAME OF WORK:- **REHABILITATION / REPLACEMENT OF 15", 12" AND 8" DIA SUNK DOWN / BROKEN SEWERAGE LINES AT DIFFERENT LOCATIONS IN UNION COUNCIL NOS. 05, 09 & 11 OF GULSHAN-E-IQBAL TOWN.**

Estimated Cost: On Item Rate
Earnest Money: 2% of Bidding Cost
Tender Cost: Rs. 1000/-
Time Limit: 120 Days
Penalty: K. W. Rs. 500/- per day.

Quotation Issued to M/S M/S. Fakhar & Brothers.

Vide Receipt No. 100 Dated: 10-2-2014

S NO	DESCRIPTION	QUANTITY	RATE	PER	AMOUNT
1.	Scarifying the existing road surface.	3770 Sft.	116	%Sft	4373
2.	Dismantling and removal road matting.	3770 Cft.	605	%Cft	22809
3.	Excavation for pipe line in trenches and pits in all kinds of soils of murum i.c trimming and dressing sides to true alignment and shape, leveling of beds of trenches to correct level and grade, cutting joint holes and disposal of surplus earth within one chain as directed by Engineering In charge, providing fence guards, lights, flags and temporary crossing for non vehicular traffic where ever required lift up to 5 ft and lead up to one chain. Lift 00'- 05'	10935 Cft.	4550	%0Cft	50848
4.	Excavation for pipe line in trench and pits in wet soils. clay or mud i/c trimming & dressing sides to true alignment and shape, leveling of beds of tranches to correct level and grade, cutting joint holes and disposal of surplus earth in one chain as directed by Engineer In-charge, providing fence guards, lights, flags, and temporary crossing for non vehicular traffic where ever required lift up to 5ft and lead up to one chain. Lift 00'- 05' Lift 05'- 08' Lift 08'- 11'	3020 Cft.	5400	%0Cft	16308
		4650 Cft.	5950	%0Cft	27668
		280 Cft.	6500	%0Cft	1820
5.	Providing & Laying of R.C.C. pipe with Rubber ring joint and fitting in trench including cutting, fitting and jointing with rubber ring i/c testing with water to specified pressure. 15" dia pipe 12" dia pipe 08" dia pipe	80 Rft.	436	Rft.	34880
		715 Rft.	367	Rft.	262405
		300 Rft.	206	Rft.	61800
6.	Providing manhole 4ft dia (inside) and 5ft clear depth, with C.I. Frame (15 kg) cast in situ with 1:2:4 C.C in 9" thick wall, 1:4:8 C.C. in 6ft dia and 6" inch thick in foundation 1:2:4 C.C. in benching, 1/2" thick cement plastering with 1:3 C.M. on all inside wall surfaces, channel and benching i/c making required Nos of main and branch channels, 3/4" dia M.S footrest @ 12" c/c i/c cost of excavation in all kinds of soil, backfilling and disposal of excavated stuff etc complete as per design and instruction of the Engineer In-charge.	13 Nos.	14529	Each	188877

	Add or deduct for extra / less depth than 5ft c/c of 4ft dia manholes i/c footrest.	(+) 26.0 Ft.	2538	P/Rft	65988
	Full hire charges of the pumping set per day i/c of wages of driver and Assistant fuel or Electric Energy plate form required for placing pumps etc at lower depth with suction and delivery pipes for pumping out water found at various depth from trenches i/c the cost of erection and dismantling after completion of the job. Hire charges of pumping set upto 10 HP pumping out water from 10 feet deep trench.	40 Days	1500	Day	6000
9.	Making connection with the existing manhole i.c the cost of cutting hole in wall, making them good in C.C 1:2:4 and making required channel etc complete.	20 Nos	180	Each	3600
10.	Manufacturing and Supplying of R.C.C manhole covers cast in 1:2:4 cement concrete ratio 3" deep at center, reinforced with 1/2" dia tor steel bars @ 4" c/c welded to a 3/16" thick 2" wide M.S plate and two hook of 3/8" dia tor bars including compacting, curing and transportation within 10 miles. 21" dia.	13 Nos.	913	Each	11869
11	Sand Haro or any other source sand of same modulus of the fineness (Hill Sand).	3473 Cft.	2425	%Cft	84220
12.	Refilling the excavated stuff in trenches 6" thick layer i.c watering, ramming to full compaction etc complete.	15998 Cft.	2760	%0Cft	44154
13.	Carriage of 100 Cft/ 5 tons of all materials like stone aggregate, spawl, coal, lime, surkhi etc; B.G. Rail fastening points and crossing bridges, Girders, pipes sheets Rail, M.S. Bars etc; or 1000 Nos: bricks, 10"x5"x3" or 1000 Nos: tiles, 12"x6"x2" or 150 Cft of timber or 100 Maunds of fuel wood by trucks or any other means owned by the contractors. <u>Carriage for 07 Miles</u> (407.00 + 95.52 + 76.89 + 70.45 + 64.43 + 57.67 + 32.56 = 804.52)	6657 Cft.	804	%Cft	53522

995141/

Executive Engineer (Sew)
Gulshan-e-Iqbal (Town), KW&SB

Bidder Quoted Amount Rs. 995141/- Rupees Nine Lacs Ninety Five Thousands
One hundred forty one and p

Sign/Stamp of Bidder Fajr

Address of Bidder C-23/1 H-10/14

Gulistan B. Jochen

1. Tender RECEIVED
2. Rate Quoted 9,95,141/2 Nine Lacs Ninety Five thousand one hundred
3. Cutting or over
4. Pay Order

P.O. No. 9038208 12-02-14 HBL Roshid minhas road

AO (EWS) ADD. I/A (KMC) S.E. (IP&D) C.E. (IP&D)



KARACHI WATER & SEWERAGE BOARD
OFFICE OF THE CHIEF ENGINEER (DISTRICT EAST)
1ST Floor Old Annexe Building, Gulshan-e-Iqbal, Karachi.

No:CE/DE/LOAW&S/KW&SB/2014/ 477

Dated: 27-11-2014

M/s. Fakhar & Brothers,
C-25/1 Block No.14, Gulistan-e-Jauhar,
Karachi,

LETTER OF ACCEPTANCE / SANCTION ORDER

SUBJECT:- **REHABILITATION / REPLACEMENT OF 15" DIA, 12" DIA & 8" DIA SUNK DOWN / BROKEN SEWERAGE LINE AT DIFFERENT LOCATIONS IN UNION COUNCIL NOS. 05, 09 & 11 OF GULSHAN-E-IQBAL TOWN.**

On behalf of the employer, it is notified that following the approval of the Managing Director, Karachi Water & Sewerage Board, vide para-68/N, dated: 10-03-2014, tender called upon through **Authority's Website of SPPRA Rule-2010 under Serial NO.18744,** as recommended by the Procurement Committee-I, KW&SB, vide para-38(01)/N to 43(06)/N, your bid for the subject is hereby accepted for the sum of **Rs.9,95,141/= (Rupees Nine Lacs Ninety Five Thousand One Hundred Forty One Only),** duly concurred by the Finance Department, vide para-55/N to para-64/N. The expenditure will be charged from the Head of Account **B.G.No. H-023-18, after Re-Appropriation of Funds through Form B-20 from B.G.No.7444-16 to B.G.No.H-023-18,** for the financial year 2013-2014.


There is now binding contract between KW&SB and **M/s. Fakhar & Brothers.**

In accordance with the General Condition of Contract, you are required to enter in to and execute a contract agreement. This agreement shall be signed by the employer and **M/s. Fakhar & Brothers.**

Please be noted that 8% Security Deposit will be deducted from your bill for due fulfillment of defect liability.

All correspondence onward shall be carried out through Superintending Engineer, Gulshan-e-Iqbal Town, District East, KW&SB.


(**GHULAM QADIR ABBAS**)
CHIEF ENGINEER DISTRICT EAST


K.W.&S.B

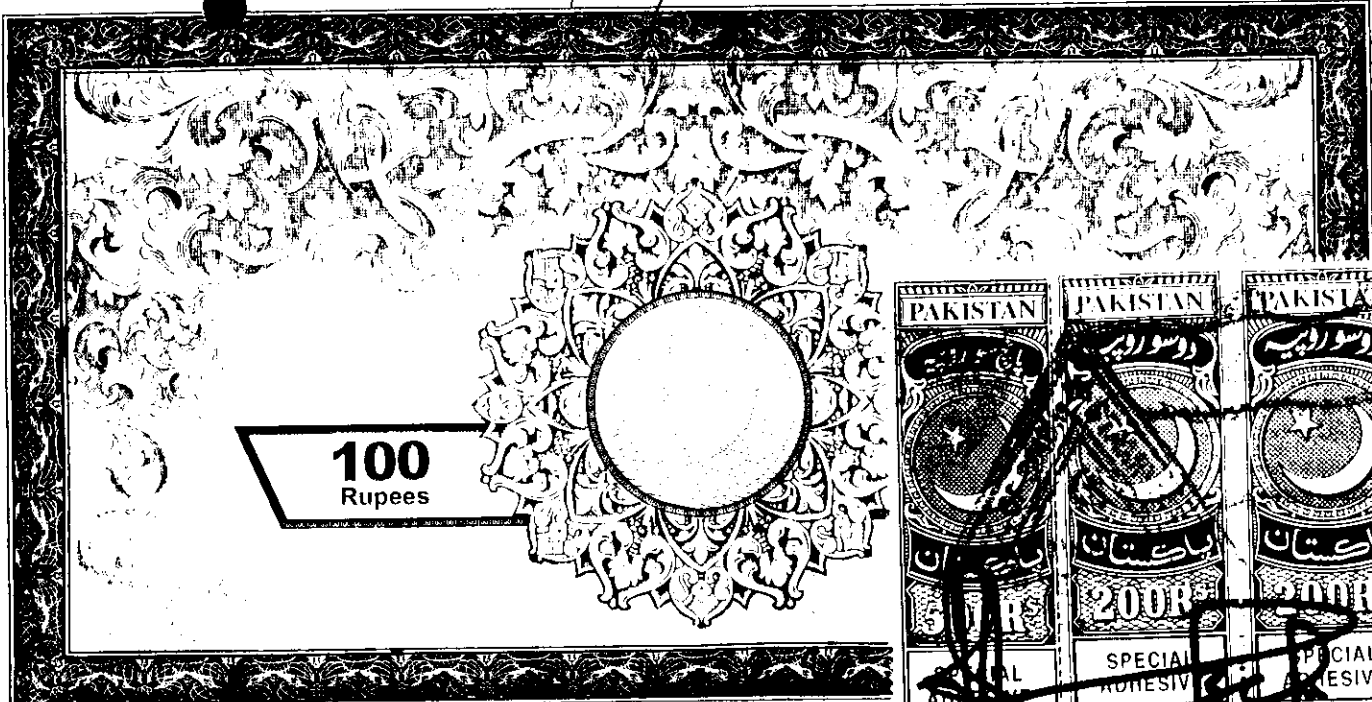
Copy to :-

1. The DMD(T/S), KW&SB.
2. S.E Gulshan-e-Iqbal Town, District East, KW&SB.
3. XEN (Sew) Gulshan-e-Iqbal Town, KW&SB.
4. Office Copy.

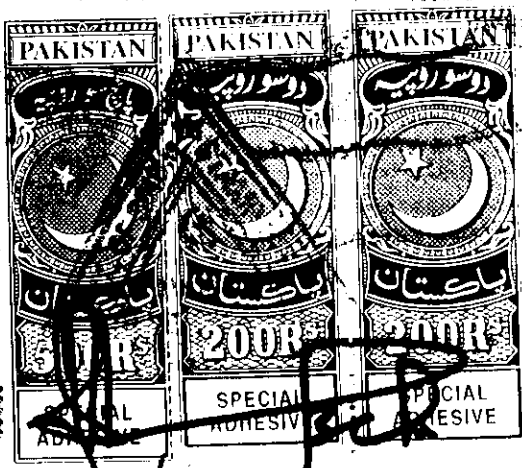
10827



10/9/14



100 Rupees




AGRICULTURE
Licence No. 091240
Karnal
15/03/2014
10/9/14
10/9/14
10/9/14
10/9/14

IN WITNESS WHEREOF, the parties hereto have set their respective hands and seals the day and year first above written.

091240

Signed, Sealed and Delivered by the
ZAHID AHMED QADIR
Advocate
For and on behalf of
EMPLOYER


10 MAR 2014
For and on behalf of
CONTRACTOR



GHULAM QADIR ABBAS
CHIEF ENGINEER DISTRICT EAST
KW&SB.


FAHAD AHMED SIDDIQUI
MANAGING PARTNER
M/S. FAKHAR & BROTHERS.


WITNESS OF EMPLOYER

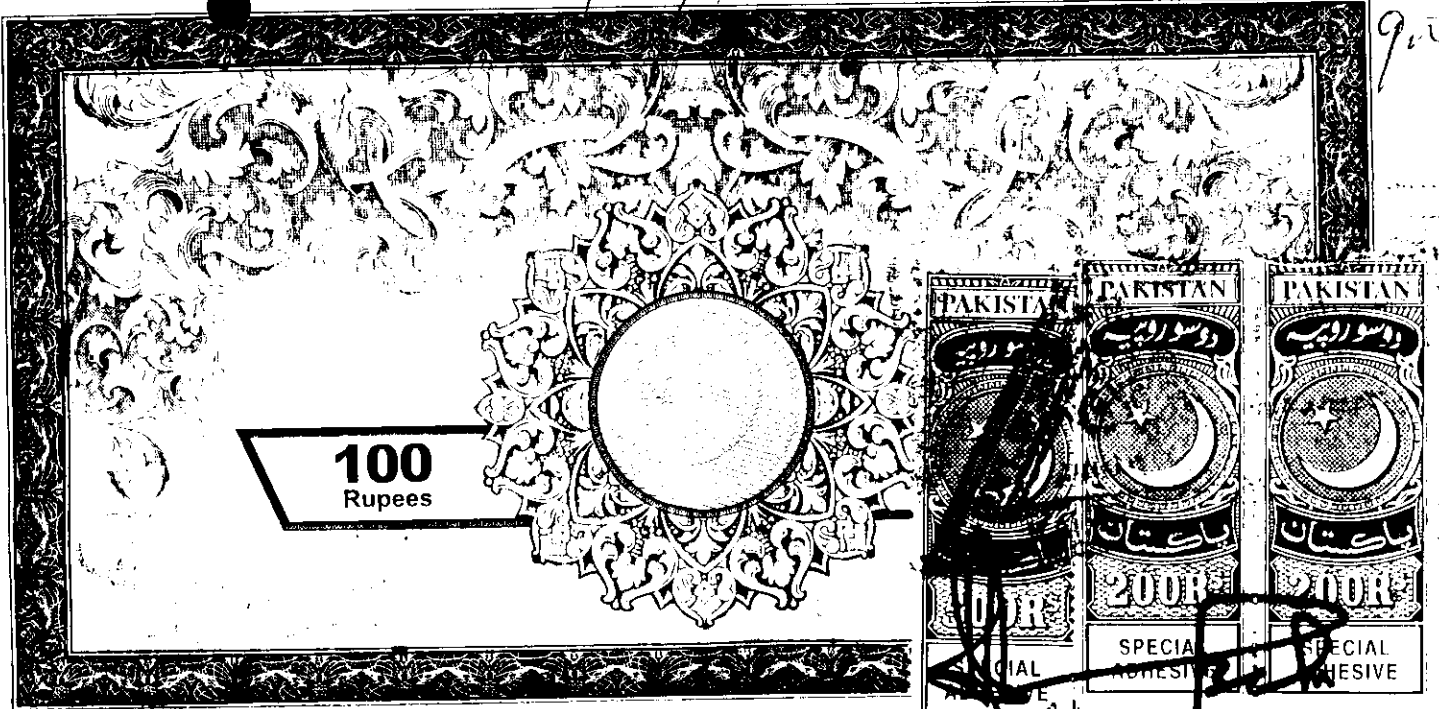
WITNESS OF CONTRACTOR


MUHAMMAD RIAZ KHAN GHORI
SUPERINTENDING ENGINEER
GULSHAN-E-IQBAL TOWN, DISTRICT EAST
K.W.&S.B.


PROJECT COORDINATOR

(B.C.C) Elegant Const & Co.

P.M. ZAYYAN Const. Co.


EJAZ AHMED
EXECUTIVE ENGINEER (SEW)
GULSHAN-E-IQBAL TOWN, DISTRICT EAST
K.W.&S.B.



28 MAR 2014

091239

ZAHID MEHMOOD

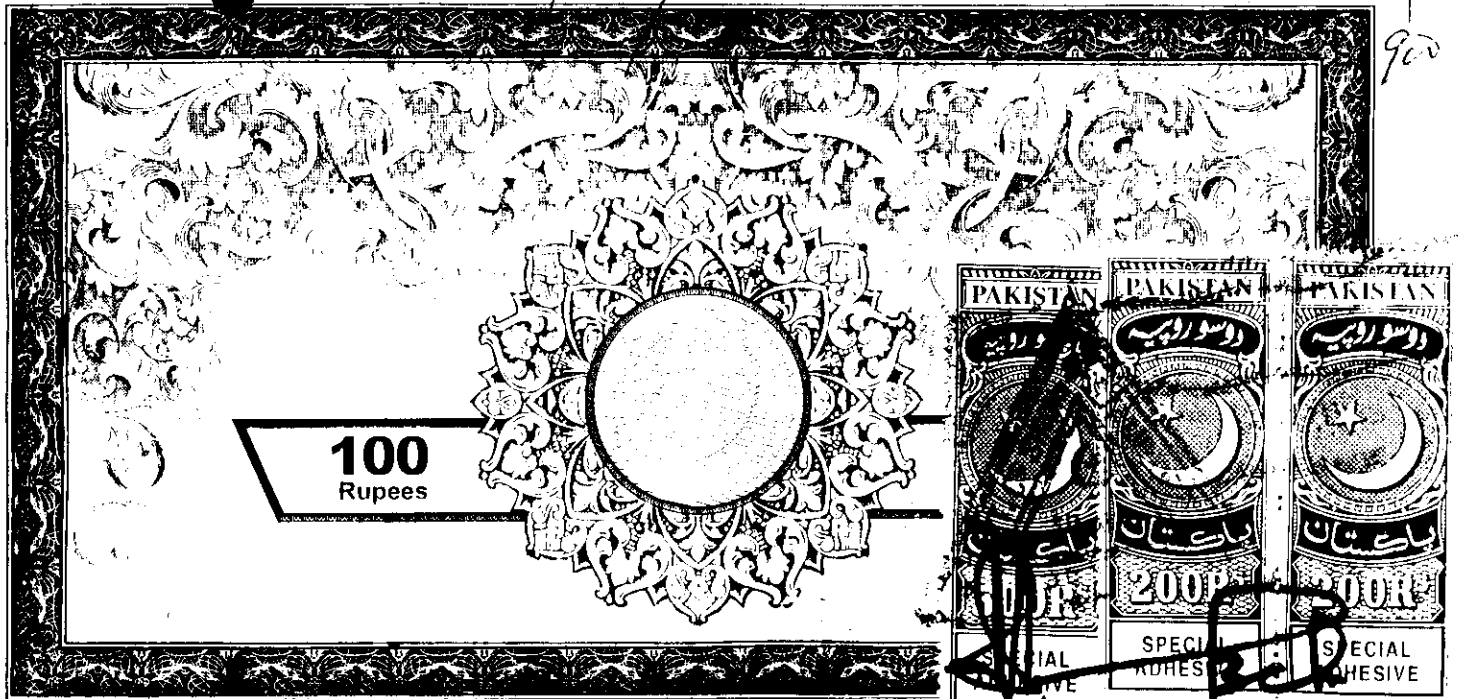
NOW this Agreement Witnesses as follows:-

1. In this Agreement words and expression shall have the same meanings as are respectively assigned to them in the conditions of Contract hereinafter referred to.
2. The following documents which for the purpose of identification have been signed by **MR. FAHAD AHMED SIDDIQUI** on behalf of the contractor and by **MR. GHULAM QADIR ABBAS, CHIEF ENGINEER, DISTRICT EAST, KW&SB**, on behalf the EMPLOYER all of which shall be deemed to form and be read and construed as part of this Agreement.
 - a). This Form of Agreement.
 - b). Employer letter of Acceptance No.CE/DE/W&S/LOA/KW&SB/2014/471 dated: 27-4-2014.
 - c). The Tender.
 - d). The conditions of the Particular Application - Part-II-A & II-B.
 - e). The General Conditions - Part-I.
 - f). The Drawings.
 - g). The specifications and
 - h). The Priced Bill of Quantities.
3. In consideration of the payments to be made by the EMPLOYER to the CONTRACTOR has hereinafter mentioned, the CONTRACTOR hereby covenants with the EMPLOYER to execute and complete the WORK and to remedy any defects therein and maintaining the same in conformity in all respects with the provisions of the CONTRACT.
4. THE EMPLOYER hereby covenants to pay to the CONTRACT in the manner prescribed by the CONTRACT.

CHIEF ENGINEER
District East, City Cantt
Karachi.

10/10/14

10/10/14



CONTRACT AGREEMENT

28 MAR 2014

U911239 CONTRACT AGREEMENT made the 07 day of April 2014, between the **Karachi Water & Sewerage Board (KW&SB)**, Government of Sindh, Represented by its Chief Engineer, District East, KW&SB, (hereinafter called the "Employer" which expression shall wherever the context so admits or required to deemed to include their successor) on the one part as first Party **M/S. FAKHAR & BROTHERS**, having their office at **C-25/1, Block-14, Gulistan-e-Jauhar Karachi**, Represented by the **MR. FAHAD AHMED SIDDIQUI** hereinafter called the "Contractor" (which expression shall wherever the context so admit or required be deemed to include their Executors. Administrators. Successors and permitted Assignees) on other part as second party.

WHEREAS the Employer is desirous to execute the work By **"REHABILITATION / REPLACEMENT OF 15" DIA, 12" DIA & 8" DIA SUNK DOWN / BROKEN SEWERAGE LINE AT DIFFERENT LOCATIONS IN UNION COUNCIL NOS. 05, 09 & 11 OF GULSHAN-E-IQBAL TOWN"** Under KW&SB'S OWN FUNDED PROGRAMME and has accepted the Tender of the CONTRACTOR for **Rs.9,95,141/= (RUPEES NINE LACS NINETY FIVE THOUSAND ONE HUNDRED FORTY ONE ONLY)** for the construction and completion of such WORKS and the remedying of an defects therein.

AND WHEREAS THE CONTRACTOR has already deposited 2% Pay Order for amounting to **Rs.20,000/=** vide Pay Order No. **9038208**, dated: **12-02-2014**, issued from **Habib Bank Limited, Rashid Minhas Road, Karachi**, deposited by the contractor and remaining amount **Rs.79,514/=** will be deducted from his bill, the same will be kept with the EMPLOYER till the maintenance period of the work for the due fulfillment of the CONTRACTOR. Further 1% Water Charges will also be deducted from his bill as per Standard Operating Procedure (SOP).



KARACHI WATER & SEWERAGE BOARD

OFFICE OF THE CHIEF ENGINEER (IP&D)

BID EVALUATION REPORT


1	Name of Procuring Agency :	KARACHI WATER & SEWERAGE BOARD
2	Tender Reference No:	SPPRA Serial No.18744 I.D No. _____/2014
3	Tender Description/Name of Work/Item:	REHABILITATION / REPLACEMENT OF 15", 12" AND 8" DIA SUNK DOWN / BROKEN SEWERAGE LINE AT DIFFERENT LOCATIONS IN UNION COUNCIL NOS. 05,09 & 11 OF GULSHAN-E-IQBAL
4	Method of Procurement:	Single Stage (One Envelop)
5	Tender Published:	Through Web Site
6	Total Bid Documents Sold:	3 Nos
7	Total Bid Received:	3 Nos
8	Technical Bid Opening Date (if applicable):	N/A
9	No. of Bid Technically Qualified (if applicable)	N/A
10	Bid (s) Rejected:	01 No
11	Financial Bid Opening Date:	13-02-2014

12 BID EVALUATION REPORT


S #	Name of Firm / Bidder	COST OFFERED BY THE BIDDER	RANKING IN TERMS OF COST	COMPARISON WITH ESTIMATED COST	REASON FOR ACCEPTANCE/ REJECTION	REMARKS
1.	M/s.Fakhar & Brothers	Rs.9,95,141/-	1 st Lowest	@0.007%Below	Substantially Responsive	P.O # 9038208 dt:12-02-2014 from HBL Rashid Minhas Road Branch Karachi Rs.20,000/-
2.	M/s.Behzad Enterprises	Rs.9,95,666/-	2 nd Lowest	@0.046%Above	Substantially Responsive	P.O # 8968727 dt:04-02-2014 from HBL Gulistan-e-Jauhar, Ruffi Lake Drive Branch Karachi Rs.20,500/-
3	M/s.Universal Enterprises	Rs.9,97,401/-	-	@0.220%Above	Un-Responsive	P.O not Attached.


The all concerned bidder are being informed accordingly.


M/s. **Fakhar & Brothers** declared as the lowest responsive bidder by the Committee and recommended for sanction from Competent Authority.


(Nadeem Ahmed Khan)
Accounts Officer (District East)
Member / Secretary


(Saif-ul-Haque)
Additional Director Internal
Audit – KMC Member


(Maqsood Ahmed Shaikh)
Superintending Engineer (KMC)
Member






(Ghulam Qadir Abbas)
Chief Engineer (District East)
Member


(Abdul Rahim Khattai)
Chief Engineer (IPD)
Convener

COMPARATIVE STATEMENT

Name of Work: REHABILITATION / REPLACEMENT OF 15", 12" AND 8" DIA SUNK DOWN / BROKEN SEWERAGE LINE
AT DIFFERENT LOCATIONS IN UNION COUNCIL NOS. 05,09 & 11 OF GULSHAN-E-IQBAL+A21

Item No	Description of Work	Estimated Cost				M/s. Fakhar & Brothers		M/s. Behzad Enterprises		
		Quantity	Rate	Per	Amount	Rate	Amount	Rate	Amount	
1	Scarifying the Existing road Surface.	3770	Sft	116.16	%Sft	4,379.23	116.00	4,373.20	117.00	4,410.90
2	Dismantling and removal road matting	3770	Cft	605.00	%Cft	22,808.50	605.00	22,808.50	605.00	22,808.50
3	Excavation for pipe line in trenches and pits in all kind of soils of murum i/c trimming and dressing sides to true alignment and shape leveling of beds of trenches to correct level and grade cutting joints holes and disposal of surplus earth within one chain as directed by Engineer Incharge providing fence guards, lights, flags sand temporary crossing for non-vehicular traffic wherever required lift upto 5 ft (1.52 m) and lead upto one chain (30.5m). Lift 00' - 05'ft	10935	Cft	4650.00	%0Cft	50,847.75	4650.00	50,847.75	4650.00	50,847.75
4	Excavation for pipe line in trenches, pits in wet silt clay or mud i/c trimming and dressing sides to true alignment and shape, leveling of beds of trenches to correct level and grade, cutting joint holes and disposal of surplus earth within one chain as directed by Engineering Incharge. Providing fence guard, light, flags and temporary crossing for non vehicular traffic where ever required lift upto 5' ft and lead upto one chain. Lift 00' - 05'	3020.00	Cft	5400.00	%0Cft	16,308.00	5400.00	16,308.00	5500.00	16,610.00
5	Lift 05' - 08'	4650.00	Cft	5950.00	%0Cft	27,667.50	5950.00	27,667.50	5950.00	27,667.50
	Lift 08' - 11'	280.00	Cft	6500.00	%0Cft	1,820.00	6500.00	1,820.00	6500.00	1,820.00
	Providing, & Laying of RCC Pipes with Rubber Ring Joint and fitting in trench including cutting, fitting, jointing with rubber ring i/c testing with water to specified pressure. 15" Dia Pipe	80	Rft	436.00	P/Rft	34,880.00	436.00	34,880.00	437.00	34,960.00
12" Dia Pipe	715	Rft	367.00	P/Rft	262,405.00	367.00	262,405.00	367.00	262,405.00	
08" Dia Pipe	300	Rft	206.00	P/Rft	61,800.00	206.00	61,800.00	206.00	61,800.00	

**Name of Work: REHABILITATION / REPLACEMENT OF 15", 12" AND 8" DIA SUNK DOWN / BROKEN SEWERAGE LINE
AT DIFFERENT LOCATIONS IN UNION COUNCIL NOS. 05,09 & 11 OF GULSHAN-E-IQBAL+A21**

Item No	Description of Work	Estimated Cost				M/s.Fakhar & Brothers		M/s.Behzad Enterprises		
		Quantity	Rate	Per	Amount	Rate	Amount	Rate	Amount	
6	Providing manhole 4' feet (inside) and 5 feet clear depth with C.I Frame (15 Kg) cast in situ with 1:2:4 CC in 9" thick wall, 1:4:8: C.C in 6ft dia and 6" inch thick in foundation 1:2:4 C.C in benching 12" thick cement plastering with 1:3 C.M on all inside wall surfaces, channel and benching i/c making required nos of main and branch channels, 3/4" dia m.s foot rest @12" c/c i/c cost of excavation in all kinds of soil, backfilling and disposal of excavated stuff etc complete as per design and instruction of engineer incharge.	13	Nos	14529.29	Each	188,880.77	14529.00	188,877.00	14529.00	188,877.00
7	Add or deduct for extra / less depth then 5ft to 4ft dia manhole i.e footrest.	26	(+)Ft	2538.62	P/ft	66,004.12	2538.00	65,988.00	2539.00	66,014.00
8	Full hire charges of pumping set per day i/c of wages of driver and assistant fuel or electric energy platform for placing the pump etc at lower depth with suction and delivery pipes for pumping out water found at various depth from trenches including the cost of erection and dismantling after completion of the job.	40	Days	1500.00	P/Day	60,000.00	1500.00	60,000.00	1500.00	60,000.00
9	(i) Hire charges of pumping set upto 10 HP pumping out water from 10 ft deep trench Making connection with the existing manhole including the cost of cutting hole in wall, making them good in C.C 1:2:4 and making the required channel etc. complete	20	Nos	180.00	Each	3,600.00	180.00	3,600.00	180.00	3,600.00











Name of Work: REHABILITATION / REPLACEMENT OF 15", 12" AND 8" DIA SUNK DOWN / BROKEN SEWERAGE LINE
AT DIFFERENT LOCATIONS IN UNION COUNCIL NOS. 05,09 & 11 OF GULSHAN-E-IQBAL+A21

Item No	Description of Work	Estimated Cost			M/s. Fakhar & Brothers		M/s. Behzad Enterprises		
		Quantity	Rate	Per	Amount	Rate	Amount	Rate	Amount
10	Manufacturing and supplying of RCC Manhole covers cast in situ 1:2:4 concrete ratio 3" deep at centre, reinforced with 1/2" dia tor steel bars at 4" C/C welded to a 3/16" thick 2" wide M.S plate two hook of 3/8" dia for bar including compacting i/c cutting and transportation with in 10 miles. 21" dia.	13 Nos	913.63	Each	11,877.19	913.00	11,869.00	914.00	11,882.00
11	Sand Haro or any other source sand of same modules of the fineness (Hill Sand)	3473.00 Cft	2425.00	%Cft	84,220.25	2425.00	84,220.25	2425.00	84,220.25
12	Refilling the excavated stuff in trenches 6" thick layer i/c watering ramming to full compaction etc complete.	15998.00 Cft	2760.00	%0Cft	44,154.48	2760.00	44,154.48	2760.00	44,154.48
13	Carriage of 100 Cft / 5 Tons of all materials like stone aggregate, spawl, coal, lime, surkhi etc B.G Rail fastening points and crossing bridges, Girders, pipes sheet Rail, M.S Bars etc. or 1000 Nos bricks, 10"x 5"x3" or 1000 Nos: tiles, 12" x6"x2" or 150 Cft of timber or 100 Maunds of fuel wood by trucks or any other means owned by the Contractors. Carriage for 07 Miles (407.00 + 95.52 + 76.89 + 70.45 + 64.43 + 57.67 + 32.56 = 804.52)	6657.00 Cft	804.52	%Cft	53,556.90	804	53,522.28	805	53,588.85
	TOTAL QUOTED / CORRECTED COST				995,209.69		995,140.96		995,666.23
	SAY				995,210		995,141		995,666


(Nadeem Ahmed Khan)
Accounts Officer (Distt. East)
Member / Secretary


(Saif-ul-Haque)
Addl. Director Internal
Audit KMC - Member


(Maqsood Ahmed Shaikh)
Superintending Engineer (K.M.C.)
Member


(Ghulam Qadir Abbas)
Chief Engineer (Distt. East)
Member


(Abdul Rahim Khan)
Chief Engineer (IPD)
Comptroller

2nd

1st



KARACHI WATER & SEWERAGE BOARD

OFFICE OF THE CHIEF ENGINEER (IP&D)

BID EVALUATION REPORT


1	Name of Procuring Agency :	KARACHI WATER & SEWERAGE BOARD
2	Tender Reference No:	SPPRA Serial No.18744 I.D No. /2014
3	Tender Description/Name of Work/Item:	REHABILITATION / REPLACEMENT OF 12" AND 8" DIA SUNK DOWN SEWERAGE LINE AT DIFFERENT LOCATIONS IN UC-10 MAIN ROAD BLOCK 3 & 14, A-222 BLOCK-03 OF GULISTAN-E-JOHAR GULSHAN-E-IQBAL
4	Method of Procurement:	Single Stage (One Envelop)
5	Tender Published:	Through Web Site
6	Total Bid Documents Sold:	3 Nos
7	Total Bid Received:	3 Nos
8	Technical Bid Opening Date (if applicable):	N/A
9	No. of Bid Technically Qualified (if applicable)	N/A
10	Bid (s) Rejected:	NIL
11	Financial Bid Opening Date:	13-02-2014

12 BID EVALUATION REPORT


S #	Name of Firm / Bidder	COST OFFERED BY THE BIDDER	RANKING IN TERMS OF COST	COMPARISON WITH ESTIMATED COST	REASON FOR ACCEPTANCE/ REJECTION	REMARKS
1.	M/s. Universal Enterprises	Rs.9,84,677/-	1 st Lowest	@0.007%Below	Substantially Responsive	P.O # 8968763 dt:07-02-2014 from HBL Gulistan-e-Jauhar, Ruffi Lake Drive Branch Karachi Rs.20,500/-
2.	M/s.Fakhar & Brothers	Rs.9,85,099/-	2 nd Lowest	@0.036%Above	Substantially Responsive	P.O # 9038207 dt:12-02-2014 from HBL Rashid Minhas Road Branch Karachi Rs.20,000/-
3	M/s.Behzad Enterprises	Rs.9,85,717/-	3 rd Lowest	@0.099%Above	Substantially Responsive	P.O # 8968760 dt:06-02-2014 from HBL Gulistan-e-Jauhar, Ruffi Lake Drive Branch Karachi Rs.20,500/-


The all concerned bidder are being informed accordingly.


M/s. Universal Enterprises declared as the lowest responsive bidder by the Committee and recommended for sanction from Competent Authority.


(Nadeem Ahmed Khan)
Accounts Officer (District East)
Member / Secretary


(Saif-ul-Haqq)
Additional Director Internal
Audit – KMC Member


(Maqsood Ahmed Shaikh)
Superintending Engineer (KMC)
Member



(Ghulam Qadir Abbas)
Chief Engineer (District East)
Member


(Abdul Rahim Khattai)
Chief Engineer (IPD)
Convener

COMPARATIVE STATEMENT

Name of Work: REHABILITATION / REPLACEMENT OF 12" AND 8" DIA SUNK DOWN SEWERAGE LINE AT DIFFERENT LOCATIONS IN UC-10 MAIN ROAD BLOCK 3 & 14, A-222 BLOCK-03 OF GULISTAN-E-JOHAR GULSHAN-E-IQBAL.

Item No	Description of Work	Estimated Cost			M/s. Universal Enterprises			M/s. Fakhar & Brothers			M/s. Behzad Enterprises		
		Quantity	Rate	Per	Rate	Amount	Rate	Amount	Rate	Amount	Rate	Amount	
1	Scarifying the Existing road Surface.	3830	Sft	116.16	%Sft	4,448.93	116.00	4,442.80	117.00	4,481.10	120.00	4,596.00	
2	Dismantling and removal road matting	3830	Cft	605.00	%Cft	23,171.50	605.00	23,171.50	605.00	23,171.50	605.00	23,171.50	
3	Excavation for pipe line in trenches and pits in all kind of soils of murum i/c trimming and dressing sides to true alignment and shape leveling of beds of trenches to correct level and grade cutting joints holes and disposal of surplus earth within one chain as directed by Engineer Incharge providing fence guards, lights, flags sand temporary crossing for non-vehicular traffic wherever required lift upto 5 ft (1.52 m) and lead upto one chain (30.5m). Lift 00' - 05'	10500	Cft	4650.00	%0Cft	48,825.00	4650.00	48,825.00	4650.00	48,825.00	4650.00	48,825.00	
4	Excavation for pipe line in trenches, pits in wet silt clay or mud i/c trimming and dressing sides to true alignment and shape, leveling of beds of trenches to correct level and grade, cutting joint holes and disposal of surplus earth within one chain as directed by Engineering Incharge. Providing fence guard, light, flags and temporary crossing for non vehicular traffic where ever required lift upto 5' ft and lead upto one chain.	4280.00	Cft	5400.00	%0Cft	23,112.00	5400.00	23,112.00	5400.00	23,112.00	5500.00	23,540.00	
	Lift 00' - 05'	4770.00	Cft	5950.00	%0Cft	28,381.50	5950.00	28,381.50	6000.00	28,620.00	6000.00	28,620.00	
	Lift 08' - 11'	300.00	Cft	6500.00	%0Cft	1,950.00	6500.00	1,950.00	6500.00	1,950.00	6500.00	1,950.00	
5	Providing, & Laying of RCC Pipes with Rubber Ring Joint and fitting in trench including cutting, fitting, jointing with rubber ring i/c testing with water to specified pressure. 12" Dia	920	Rft	367.00	P/Rft	337,640.00	367.00	337,640.00	367.00	337,640.00	367.00	337,640.00	
	08" Dia Pipe	144	Rft	206.00	P/Rft	29,664.00	206.00	29,664.00	206.00	29,664.00	206.00	29,664.00	



 June 14/12

Name of Work: REHABILITATION / REPLACEMENT OF 12" AND 8" DIA SUNK DOWN SEWERAGE LINE AT DIFFERENT LOCATIONS IN UC-10 MAIN ROAD BLOCK 3 & 14, A-222 BLOCK-03 OF GULISTAN-E-JOHAR GULSHAN-E-IQBAL

Item No	Description of Work	Estimated Cost			M/s. Universal Enterprises		M/s. Fakhar & Brothers		M/s. Behzad Enterprises			
		Quantity	Rate	Per	Amount	Rate	Amount	Rate	Amount	Rate	Amount	
6	Providing manhole 4' feet (inside) and 5 feet clear depth with C.I Frame (15 Kg) cast in situ with 1:2:4 CC in 9" thick wall, 1:4:8: C.C in 6ft dia and 6" inch thick in foundation 1:2:4 C.C in benching 12" thick cement plastering with 1:3 C.M on all inside wall surfaces, channel and benching i/c making required nos of main and branch channels, 3/4" dia m.s foot rest @12" c/c i/c cost of excavation in all kinds of soil, backfilling and disposal of excavated stuff etc complete as per design and instruction of engineer incharge (prepared R.A on Sch.12).	15	Nos	Each	217,939.35	14529.29	14529.00	217,935.00	14530.00	217,950.00	14535.00	218,025.00
7	Add or deduct for extra / less depth then 5ft to 4ft dia manhole i/c footrest.	29	(+)	P/ft	73,619.98	2538.62	2538.00	73,602.00	2540.00	73,660.00	2540.00	73,660.00
8	Full hire charges of pumping set per day i/c of wages of driver and assistant fuel or electric energy platform for placing the pump etc at lower depth with suction and delivery pipes for pumping out water found at various depth from trenches including the cost of erection and dismantling after completion of the job. (i) Hire charges of pumping set upto 10 HP pumping out water from 10 ft deep trench	20	Days	P/Day	30,000.00	1500.00	1500.00	30,000.00	1500.00	30,000.00	1500.00	30,000.00
9	Making connection with the existing manhole including the cost of cutting hole in wall, making them good in C.C 1:2:4 and making the required channel etc. complete	20	Nos	Each	3,600.00	180.00	180.00	3,600.00	180.00	3,600.00	180.00	3,600.00
10	Manufacturing and supplying of RCC Manhole covers cast in situ 1:2:4 concrete ratio 3" deep at centre, reinforced with 1/2" dia tor steel bars at 4" C/C welded to a 3/16" thick 2" wide M.S plate two hook of 3/8" dia tor bar including compacting i/c cutting and transportation with in 10 miles. 21" dia.	15	Nos	Each	13,704.45	913.63	913.00	13,695.00	914.00	13,710.00	914.00	13,710.00



 14/12

Name of Work: REHABILITATION / REPLACEMENT OF 12" AND 8" DIA SUNK DOWN SEWERAGE LINE AT DIFFERENT LOCATIONS IN UC-10 MAIN ROAD BLOCK 3 & 14, A-222 BLOCK-03 OF GULISTAN-E-JOHAR GULSHAN-E-IQBAL

Item No	Description of Work	Estimated Cost			M/s. Universal Enterprises		M/s. Fakhar & Brothers		M/s. Behzad Enterprises	
		Quantity	Rate	Per	Rate	Amount	Rate	Amount	Rate	Amount
11	Sand Haro or any other source sand of same modules of the fineness (Hill Sand)	2196.00	Cft	2425.00	%Cft	53,253.00	2425.00	53,253.00	2425.00	53,253.00
12	Refilling the excavated stuff in trenches 6" thick layer i/c watering ramming to full compaction etc complete.	17989.00	Cft	2760.00	%0Cft	49,649.64	2760.00	49,649.64	2760.00	49,649.64
13	Carriage of 100 Cft / 5 Tons of all materials like stone aggregate, spawl, coal, lime, surkhi etc B.G Rail fastening points and crossing bridges, Girders, pipes sheet Rail, M.S Bars etc. or 1000 Nos bricks, 10" x 5" x 3" or 1000 Nos: tiles, 12" x 6" x 2" or 150 Cft of timber or 100 Maunds of fuel wood by trucks or any other means owned by the Contractors.	5691.00	Cft	804.52	%Cft	45,785.00	804	45,755.64	805	45,812.55
	Carriage for 07 Miles (407.00 + 95.52 + 76.89 + 70.45 + 64.43 + 57.67 + 32.56 = 804.52)					984,744.35		984,677.08		985,098.79
	TOTAL QUOTED / CORRECTED COST					984,744		984,677		985,099
	SAY					1st		2nd		3rd

(Nadeem Ahmed Khan) 14/12
Accounts Officer (Distt. East)
Member / Secretary

(Maqsood Ahmed Shaikh)
Superintending Engineer (K.M.C)
Member

(Ghulam Qadir Abbas)
Chief Engineer (Distt. East)
Member

(Abdul Khaliq Khattak)
Chief Engineer (PPD)
Contractor

SINDH PUBLIC PROCUREMENT REGULATORY AUTHORITY

CONTRACT EVALUATION FORM

TO BE FILLED IN BY ALL PROCURING AGENCIES FOR PUBLIC CONTRACTS OF WORKS, SERVICES & GOODS

- KARACHI WATER & SEWERAGE BOARD
- 1) NAME OF THE ORGANIZATION / DEPTT. _____
 - 2) PROVINCIAL / LOCAL GOVT./ OTHER _____
 - 3) TITLE OF CONTRACT Replacement of 12" & 8" Dia in UC-10 G.J Gulshan Town.
 - 4) TENDER NUMBER SPPRA Sr No.18744 I.D No
 - 5) BRIEF DESCRIPTION OF CONTRACT Replacement of 12" & 8" Dia in UC-10 G.J Gulshan Town.
 - 6) FORUM THAT APPROVED THE SCHEME Managing Director KW&SB
 - 7) TENDER ESTIMATED VALUE Rs.9,84,677/=
 - 8) ENGINEER'S ESTIMATE Rs.9,85,528/=
(For civil works only)
 - 9) ESTIMATED COMPLETION PERIOD (AS PER CONTRACT) 20 days
 - 10) TENDER OPENED ON (DATE & TIME) 13-02-2014
 - 11) NUMBER OF TENDER DOCUMENTS SOLD 3 (Three)
(Attach list of buyers)
 - 12) NUMBER OF BIDS RECEIVED 3 (Three)
 - 13) NUMBER OF BIDDERS PRESENT AT THE TIME OF OPENING OF BIDS 3 (Three)
 - 14) BID EVALUATION REPORT Copy Attached
(Enclose a copy)
 - 15) NAME AND ADDRESS OF THE SUCCESSFUL BIDDER M/S UNIVERSAL ENTERPRISES
 - 16) CONTRACT AWARD PRICE Rs.9,84,677/=
 - 17) RANKING OF SUCCESSFUL BIDDER IN EVALUATION REPORT
(i.e. 1st, 2nd, 3rd EVALUATION BID).
M/S Universal Enterprises
M/S Fakhar & Brothers
M/S Behzad Enterprises
 - 18) METHOD OF PROCUREMENT USED :- (Tick one)

- a) SINGLE STAGE – ONE ENVELOPE PROCEDURE Domestic/ Local
- b) SINGLE STAGE – TWO ENVELOPE PROCEDURE
- c) TWO STAGE BIDDING PROCEDURE
- d) TWO STAGE – TWO ENVELOPE BIDDING PROCEDURE

PLEASE SPECIFY IF ANY OTHER METHOD OF PROCUREMENT WAS ADOPTED i.e. EMERGENCY, DIRECT CONTRACTING ETC. WITH BRIEF REASONS:

19) APPROVING AUTHORITY FOR AWARD OF CONTRACT _____

20) WHETHER THE PROCUREMENT WAS INCLUDED IN ANNUAL PROCUREMENT PLAN?

Yes	<input type="checkbox"/>	No	<input type="checkbox"/>
-----	--------------------------	----	--------------------------

21) ADVERTISEMENT :

i) SPPRA Website
(If yes, give date and SPPRA Identification No.)

Yes	Serial No 18744
<input checked="" type="checkbox"/>	
No	

ii) News Papers
(If yes, give names of newspapers and dates)

Yes	
<input type="checkbox"/>	
No	<input checked="" type="checkbox"/>

22) NATURE OF CONTRACT

Domestic/ Local	<input checked="" type="checkbox"/>	Int.	<input type="checkbox"/>
--------------------	-------------------------------------	------	--------------------------

23) WHETHER QUALIFICATION CRITERIA
WAS INCLUDED IN BIDDING / TENDER DOCUMENTS?
(If yes, enclose a copy)

Yes	<input type="checkbox"/>	No	<input checked="" type="checkbox"/>
-----	--------------------------	----	-------------------------------------

24) WHETHER BID EVALUATION CRITERIA
WAS INCLUDED IN BIDDING / TENDER DOCUMENTS?
(If yes, enclose a copy)

Yes	<input type="checkbox"/>	No	<input checked="" type="checkbox"/>
-----	--------------------------	----	-------------------------------------

25) WHETHER APPROVAL OF COMPETENT AUTHORITY WAS OBTAINED FOR USING A
METHOD OTHER THAN OPEN COMPETITIVE BIDDING?

Yes	<input type="checkbox"/>	No	<input checked="" type="checkbox"/>
-----	--------------------------	----	-------------------------------------

26) WAS BID SECURITY OBTAINED FROM ALL THE BIDDERS?

Yes	<input checked="" type="checkbox"/>	No	<input type="checkbox"/>
-----	-------------------------------------	----	--------------------------

27) WHETHER THE SUCCESSFUL BID WAS LOWEST EVALUATED
BID / BEST EVALUATED BID (in case of Consultancies)

Yes	<input checked="" type="checkbox"/>	No	<input type="checkbox"/>
-----	-------------------------------------	----	--------------------------

28) WHETHER THE SUCCESSFUL BIDDER WAS TECHNICALLY
COMPLIANT?

Yes	<input checked="" type="checkbox"/>	No	<input type="checkbox"/>
-----	-------------------------------------	----	--------------------------

29) WHETHER NAMES OF THE BIDDERS AND THEIR QUOTED PRICES WERE READ OUT AT
THE TIME OF OPENING OF BIDS?

Yes	<input checked="" type="checkbox"/>	No	<input type="checkbox"/>
-----	-------------------------------------	----	--------------------------

30) WHETHER EVALUATION REPORT GIVEN TO BIDDERS BEFORE THE AWARD OF
CONTRACT?
(Attach copy of the bid evaluation report)

Yes	<input checked="" type="checkbox"/>	No	<input type="checkbox"/>
-----	-------------------------------------	----	--------------------------

31) ANY COMPLAINTS RECEIVED
(If yes, result thereof)

Yes	
No	<input checked="" type="checkbox"/>

32) ANY DEVIATION FROM SPECIFICATIONS GIVEN IN THE TENDER NOTICE / DOCUMENTS
(If yes, give details)

Yes	
No	<input checked="" type="checkbox"/>

33) WAS THE EXTENSION MADE IN RESPONSE TIME?
(If yes, give reasons)

Yes	
No	<input checked="" type="checkbox"/>

34) DEVIATION FROM QUALIFICATION CRITERIA
(If yes, give detailed reasons.)

Yes	
No	<input checked="" type="checkbox"/>

35) WAS IT ASSURED BY THE PROCURING AGENCY THAT THE SELECTED FIRM IS NOT
BLACK LISTED?

Yes	<input checked="" type="checkbox"/>	No	<input type="checkbox"/>
-----	-------------------------------------	----	--------------------------

36) WAS A VISIT MADE BY ANY OFFICER/OFFICIAL OF THE PROCURING AGENCY TO THE
SUPPLIER'S PREMISES IN CONNECTION WITH THE PROCUREMENT? IF SO, DETAILS TO
BE ASCERTAINED REGARDING FINANCING OF VISIT, IF ABROAD:
(If yes, enclose a copy)

Yes	<input type="checkbox"/>	No	<input checked="" type="checkbox"/>
-----	--------------------------	----	-------------------------------------

37) WERE PROPER SAFEGUARDS PROVIDED ON MOBILIZATION ADVANCE PAYMENT IN
THE CONTRACT (BANK GUARANTEE ETC.)?

Yes	<input type="checkbox"/>	No	<input checked="" type="checkbox"/>
-----	--------------------------	----	-------------------------------------

38) SPECIAL CONDITIONS, IF ANY
(If yes, give Brief Description)

Yes	
No	<input checked="" type="checkbox"/>

39) Date of Award of Contract: _____

Signature & Official Stamp of
Authorized Officer

[Handwritten Signature]
[Official Stamp]

FOR OFFICE USE ONLY

[Official Stamp]

SPPRA, Block. No.8, Sindh Secretariat No.4-A, Court Road, Karachi

Tele: 021-9205356; 021-9205369 & Fax: 021-9206291



KARACHI WATER & SEWERAGE BOARD

OFFICE OF THE CHIEF ENGINEER (DISTRICT EAST)

1st Floor Old Annexe Building, Gulshan-e-Iqbal, Karachi.

No:CE/DE/W&S/LOA/KW&SB/2014/ 44

Dated: 20-3-2014

M/s. Universal Enterprises,
B-146, Block No.3, Gulistan-e-Jauhar,
Karachi.

LETTER OF ACCEPTANCE / SANCTION ORDER

SUBJECT:- **REHABILITATION / REPLACEMENT OF 12" DIA & 8" DIA SUNK DOWN SEWERAGE LINE AT DIFFERENT LOCATIONS IN UC-10 MAIN ROAD BLOCK-3 & 14, A-222 BLOCK-03 OF GULISTAN-E-JAUHAR, GULSHAN-E-IQBAL TOWN.**


On behalf of the employer, it is notified that following the approval of the Managing Director, Karachi Water & Sewerage Board, vide para-55/N, dated: 03-03-2014, the tender called upon through **Authority's Website of SPPRA Rule-2010 under Serial NO.18744**, as recommended by the Procurement Committee-I, KW&SB, vide para-28(1)/N to 33(6)/N, your bid for the subject is hereby accepted for the sum of **Rs.9,84,677/= (Rupees Nine Lacs Eighty Four Thousand Six Hundred Seventy Seven Only)**, duly concurred by the Finance Department, vide para-42/N to 51/N. The expenditure will be charged from the Head of Account **B.G.No. H-023-18, after Re-Appropriation of funds through Form B-20 from B.G.No.7444-16 to B.G.No.H-023-18**, for the year 2013-2014.

There is now binding contract between KW&SB and **M/s. Universal Enterprises.**

In accordance with the General Condition of Contract, you are required to enter in to and execute a contract agreement. This agreement shall be signed by the employer and **M/s. Universal Enterprises.**

Please be noted that 8% Security Deposit will be deducted from your bill for due fulfillment of defect liability.

All correspondence onward shall be carried out through Superintending Engineer, Gulshan-e-Iqbal Town, District East, KW&SB.


(**GHULAM QADIR ABBAS**)
CHIEF ENGINEER, DISTRICT EAST
K.W.&S.B

Copy to :-

1. The DMD(T/S), KW&SB.
2. S.E Gulshan-e-Iqbal Town, District South, KW&SB.
3. XEN, (Sew), Gulshan-e-Iqbal Town, District East KW&SB.
4. Office Copy.



KARACHI WATER & SEWERAGE BOARD

OFFICE OF THE EXECUTIVE ENGINEER (SEW) GULSHAN-E-IQBAL (TOWN)
ST-2, BLOCK-14, SCHEME-24, MAIN UNIVERSITY ROAD NEAR CIVIC CENTER

NO.EE/GIT/SEW/KW&SB/2013-14/34

DATED:- 20-3-2014

M/S UNIVERSAL ENTERPRISES
Government Contractor
Karachi

WORK ORDER / L.O.C.

SUBJECT:

REHABILITATION / REPLACEMENT OF 12" AND 8" DIA
SUNK DOWN SEWERAGE LINES AT DIFFERENT
LOCATIONS IN UC-10 MAIN ROAD BLOCK 3 & 14 , A-222
BLOCK-03 OF GULISTAN-E-JOHAR GULSHAN-E-IQBAL
TOWN.

Your tender dated: 13-02-2014, has been approved by the Competent Authority, KW&SB on item rate basis for amounting to **Rs.9,84,677/= (Rupees Nine lac eighty four thousand six hundred and seventy seven Only)**. You are therefore, requested to start the above mentioned work as per design and specification.

The work is to be completed with (20) days, failing which penalty of Rs.500/= per day will be imposed/recovered as per terms and conditions of the contract.

You are further requested to contact the concerned A.E.E., in connection with commencement of supervision for necessary instruction of the work.


EXECUTIVE ENGINEER (SEW)
GULSHAN-E-IQBAL TOWN
KW&SB

Copy to:-

1. The Chief Engineer (East), KW&SB.
2. Superintending Engineer, (Gulshan Town), KW&SB.
3. Accountant Officer, (Gulshan Town), KW&SB.
4. A.O. (Budget)
5. Office Copy.

**OFFICE OF THE EXECUTIVE ENGINEER (SEW) GULSHAN-E-IQBAL (TOWN)
KARACHI WATER AND SEWERAGE BAOR**

SCHEDULE "B"

NAME OF WORK:- **REHABILITATION / REPLACEMENT OF 12" AND 8" DIA SUNK
DOWN SEWERAGE LINES AT DIFFERENT LOCATIONS IN UC-
10 MAIN ROAD BLOCK 3 & 14 , A-222 BLOCK-03 OF GULISTAN-
E-JOHAR GULSHAN-E-IQBAL TOWN.**

Estimated Cost: On Item Rate Quotation Issued to M/S M/S. Universal Enterprise
Earnest Money 2% of Biding Cost
Tender Cost: Rs. 1000/-
Time Limit: 15 Days Vide Receipt No. 16 Dated: 11-02-2014
Penalty: Rs. 500/- per day
**Finance Department
K. W. & S.B.**

S NO	DESCRIPTION	QUANTITY	RATE	PER	AMOUNT	
1.	Scarifying the existing road surface.	3830 Sft.	116/-	%Sft	4443/-	
2.	Dismantling and removal road matting.	3830 Cft.	605/-	%Cft	23172/-	
3.	Excavation for pipe line in trenches and pits in all kinds of soils of murum i.c trimming and dressing sides to true alignment and shape, leveling of beds of trenches to correct level and grade, cutting joint holes and disposal of surplus earth within one chain as directed by Engineering In charge, providing fence guards, lights, flags and temporary crossing for non vehicular traffic where ever required lift up to 5 ft and lead up to one chain. Lift 00'- 05'	10500 Cft.	4650	%0Cft	48825/-	
4.	Excavation for pipe line in trench and pits in wet soils, clay or mud i/c trimming & dressing sides to true alignment and shape, leveling of beds of tranches to correct level and grade, cutting joint holes and disposal of surplus earth in one chain as directed by Engineer In-charge, providing fence guards, lights, flags, and temporary crossing for non vehicular traffic where ever required lift up to 5ft and lead up to one chain. Lift 00'- 05'	4280 Cft.	5400/-	%0Cft	23112/-	
		Lift 05'- 08'	4770 Cft.	5950/-	%0Cft	28381/50
		Lift 08'- 11'	300 Cft.	6500/-	%0Cft	1950/-
5.	Providing & Laying of R.C.C. pipe with Rubber ring joint and fitting in trench including cutting, fitting and jointing with rubber ring i/c testing with water to specified pressure. 12" dia pipe 08" dia pipe	920 Rft.	367/-	Rft.	337640/-	
		144 Rft.	206/-	Rft.	29664/-	
6.	Providing manhole 4ft dia (inside) and 5ft clear depth, with C.I. Frame (15 kg) cast in situ with 1:2:4 C.C in 9" thick wall, 1:4:8 C.C. in 6ft dia and 6" inch thick in foundation 1:2:4 C.C. in benching, 1/2" thick cement plastering with 1:3 C.M. on all inside wall surfaces, channel and benching i/c making required Nos of main and branch channels, 3/4" dia M.S footrest @ 12" c/c i/c cost of excavation in all kinds of soil, backfilling and disposal of excavated stuff etc complete as per design and instruction of the Engineer In-charge.(prepared R.A. on Sch;12)	15 Nos.	14529/-	Each	217935/-	

7.	Add or deduct for extra / less depth than 5ft of dia manholes i/c footrest.	2538/-	P/Rft	73602/-
8.	Full hire charges of the pumping set per day i/c of wages of driver and Assistant fuel or Electric Energy plate form required for placing pumps etc at lower depth with suction and delivery pipes for pumping out water found at various depth from trenches i/c the cost of erection and dismantling after completion of the job. Hire charges of pumping set upto 10 HP pumping out water from 10 feet deep trench.	20 Days	2500/- Day	30000/-
9.	Making connection with the existing manhole i.c the cost of cutting hole in wall, making them good in C.C 1:2:4 and making required channel etc complete.	20 Nos	180/- Each	3600/-
10.	Manufacturing and Supplying of R.C.C manhole covers cast in 1:2:4 cement concrete ratio 3" deep at center, reinforced with 1/2" dia tor steel bars @ 4" c/c welded to a 3/16" thick 2" wide M.S plate and two hook of 3/8" dia tor bars including compacting, curing and transportation within 10 miles. 21" dia.	15 Nos.	913/- Each	13695/-
11.	Sand Haro or any other source sand of same modulus of the fineness (Hill Sand).	2196 Cft.	2425/- %Cft	53253/-
12.	Refilling the excavated stuff in trenches 6" thick layer i.c watering, ramming to full compaction etc complete.	17989 Cft.	2760/- %0Cft	69650/-
13.	Carriage of 100 Cft/ 5 tons of all materials like stone aggregate, spawl, coal, lime, surkhi etc; B.G. Rail fastening points and crossing bridges, Girders, pipes sheets Rail, M.S. Bars etc; or 1000 Nos: bricks, 10"x5"x3" or 1000 Nos: tiles, 12"x6"x2" or 150 Cft of timber or 100 Maunds of fuel wood by trucks or any other means owned by the contractors. <u>Carriage for 07 Miles</u> (407.00 + 95.52 + 76.89 + 70.45 + 64.43 + 57.67 + 32.56 = 804.52)	5691 Cft.	804/- %Cft	45756/-

984,678/50

[Signature]
Executive Engineer (Sew)
Gulshan-e-Iqbal (Town), KW&SB


Bidder Quoted Amount Rs. 984678/50 Rupees Nine Lacs eighty four thousand six hundred seventy eight and paise fifty

Sign: / Stamp of Bidder *[Signature]*

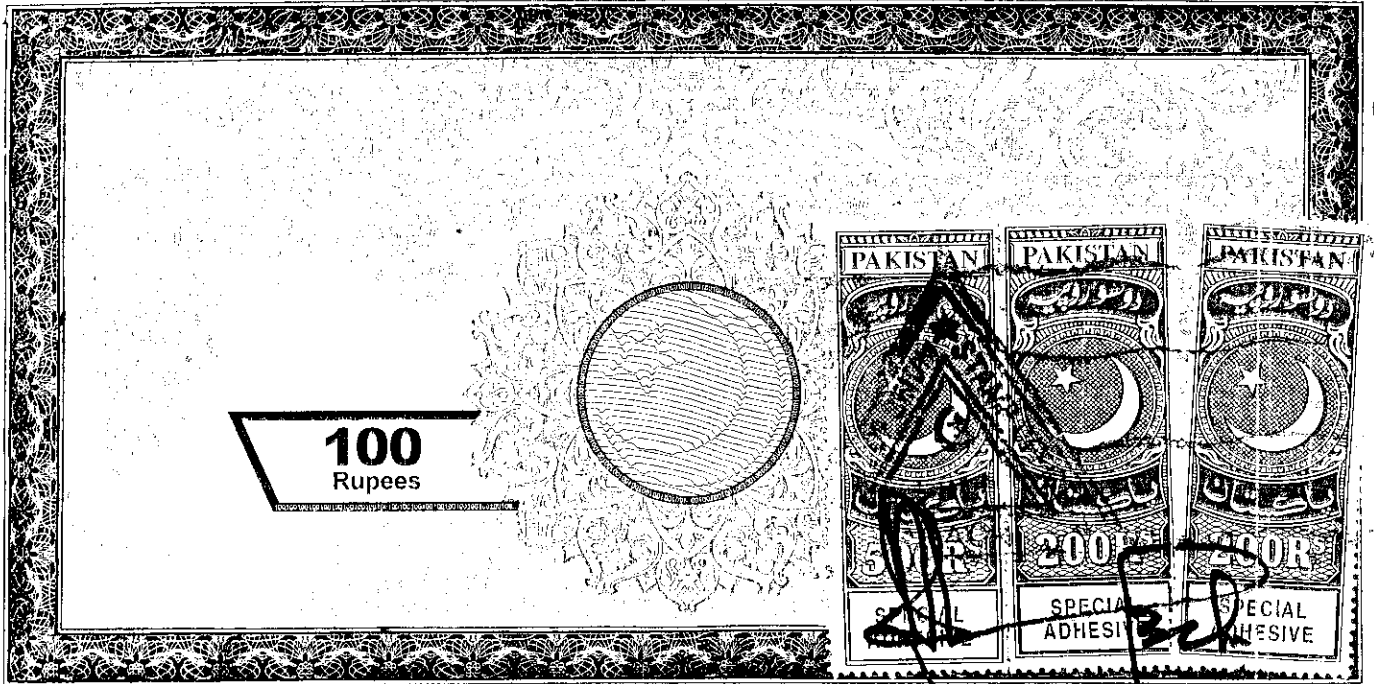
Address of Bidder B-146 Pk No 3 Gulistan B. Jular

1. Tender RECEIVED
2. Rate Quoted 9,84,678/50 Nine Lac eighty four thousand six hundred
3. Seventy eight and Paise fifty only
4. Pay Order No. 8968763 S.No. (8) 07-02-10 20,500/- HBL Ruffi Lake Drive

[Signatures]
A.O. (KMS) ADD. IV (KMC) S.E. (KMC) C.E. (KMS) C.E. (IP&D)



218
900



IN WITNESS WHEREOF, the parties hereto have set their respective hands and seals the day and year first above written.

76539
Signed, Sealed and Delivered by the.

For and on behalf of
EMPLOYER

For and on behalf of
CONTRACTOR

[Signature]
GHULAM QADIR ABBAS
CHIEF ENGINEER DISTRICT EAST
KW&SB.

[Signature]
ZAFAR MEHMOOD SIDDIQUI
MANAGING PARTNER
M/S. UNIVERSAL ENTERPRISES.

WITNESS OF EMPLOYER

WITNESS OF CONTRACTOR

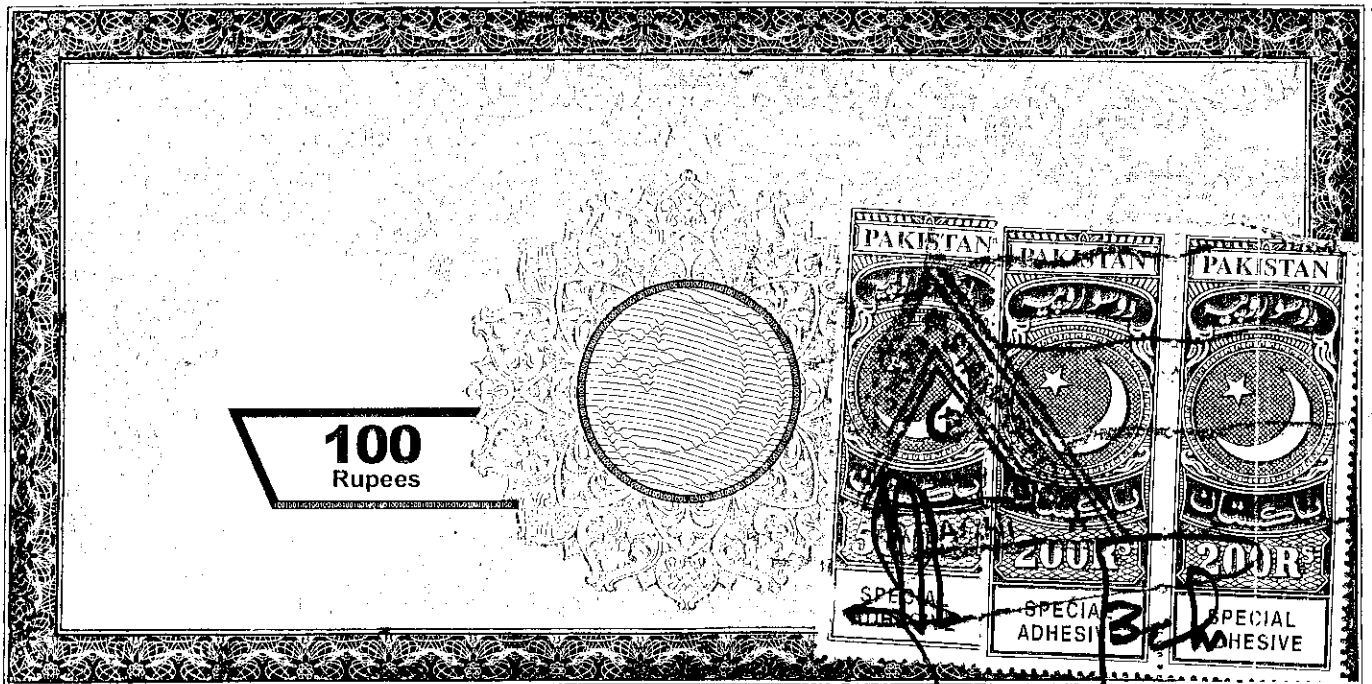
[Signature]
MUHAMMAD RIAZ KHAN GHORI
SUPERINTENDING ENGINEER
GULSHAN-E-IQBAL TOWN, DISTRICT EAST
K.W.&.S.B.

[Signature]
PROJECT COORDINATOR
[Signature] Ms. Farhan Assoad

[Signature]
EJAZ AHMED
EXECUTIVE ENGINEER (SEW)
GULSHAN-E-IQBAL TOWN, DISTRICT EAST
K.W.&.S.B.



218
900



REHMAN SULTAN Stamp Vendor
 Location No 129 Shop No 16 Block 14,
 Kream Plaza, Gulshan-e-Iqbal, Karachi
 S.No.

DATE 17 MAR 2014 76538

[Handwritten signature]

BASED UPON THE ABOVE NOW this Agreement witnesses as follows:-

1. In this Agreement words and expression shall have the same meanings as are respectively assigned to them in the conditions of Contract hereinafter referred to.


2. The following documents which for the purpose of identification have been signed by **MR. ZAFAR MEHMOOD SIDDIQUI** on behalf of the contractor and by **MR. GHULAM QADIR ABBAS, CHIEF ENGINEER, DISTRICT EAST, KW&SB**, on behalf the EMPLOYER all of which shall be deemed to form and be read and construed as part of this Agreement.

- a). This Form of Agreement.
- b). Employer letter of Acceptance No.CE/DE/W&S/KW&SB/2014/22/ dated: 20-03-2014.
- c). The Tender.
- d). The conditions of the Particular Application – Part-II-A & II-B.
- e). The General Conditions – Part-I.
- f). The Drawings.
- g). The specifications and
- h). The Priced Bill of Quantities.

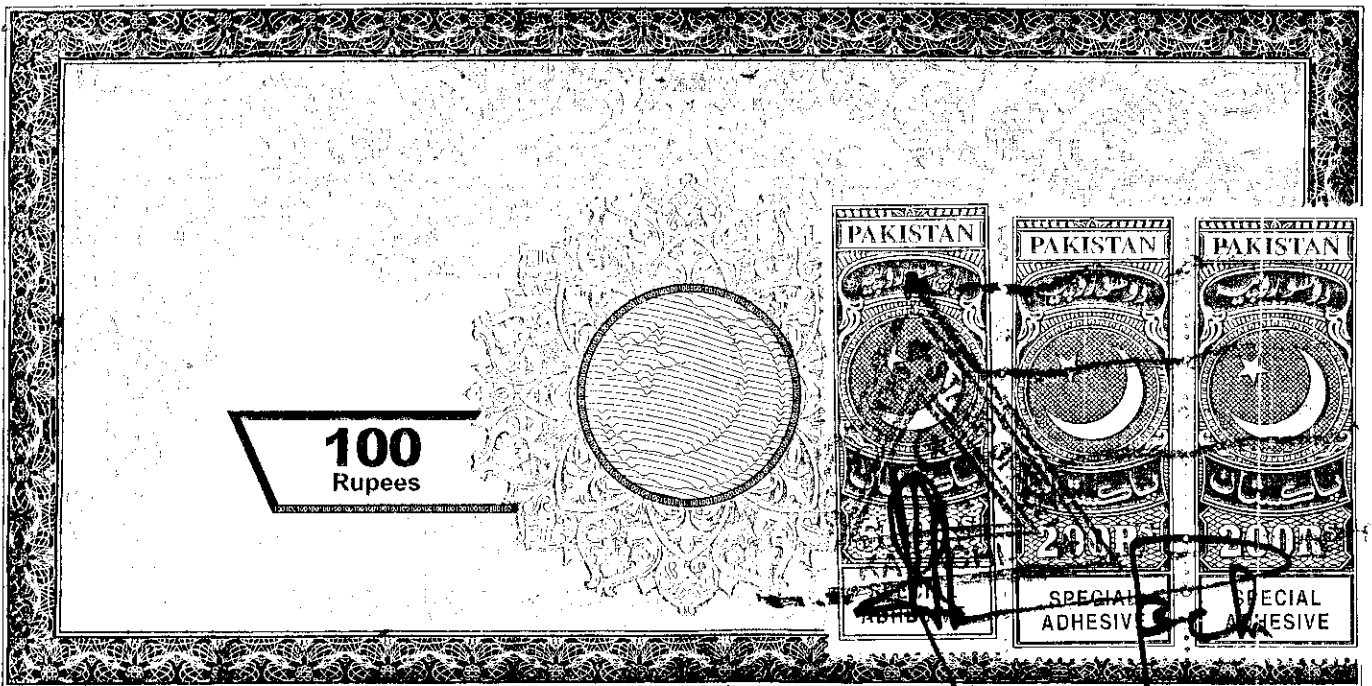
3. In consideration of the payments to be made by the EMPLOYER to the CONTRACTOR has hereinafter mentioned, the CONTRACTOR hereby covenants with the EMPLOYER to execute and complete the WORK and to remedy any defects therein and maintaining the same in conformity in all respects with the provisions of the CONTRACT.

4. THE EMPLOYER hereby covenants to pay to the CONTRACT in the manner prescribed by the CONTRACT.

[Handwritten signature]



218
Jaw



REMANI MONTAN Stamp Vendor
Location No 129 Shop No 16 Block 14
Karnal Ghara, Gulshan-e-Iqbal, Karachi
S No.

CONTRACT AGREEMENT

76537

Date: 17 MAR 2014

This CONTRACT AGREEMENT made the 20th day of March 2014, between the **Karachi Water & Sewerage Board (KW&SB)**, Government of Sindh, Represented by its Chief Engineer, District East, KW&SB, (hereinafter called the "Employer" which expression shall wherever the context so admits or required to include their successor) on the one part as first Party **M/S. UNIVERSAL ENTERPRISES**, having their office at **B-146, Block-3, Gulistan-e-Jauhar, Karachi**, Represented by the **MR. ZAFAR MEHMOOD SIDDIQUI** hereinafter called the "Contractor" (which expression shall wherever the context so admit or required be deemed to include their Executors. Administrators. Successors and permitted Assignees) on other part as second party.

WHEREAS the Employer is desirous to execute the work By **"REHABILITATION / REPLACEMENT OF 12" DIA & 8" DIA SUNK DOWN SEWERAGE LINE AT DIFFERENT LOCATIONS IN UC-10 MAIN ROAD BLOCK-3 & 14, A-222 BLOCK-03 OF GULISTAN-E-JAUHAR, GULSHAN-E-IQBAL TOWN."** Under KW&SB'S OWN FUNDED PROGRAMME and has accepted the Tender of the CONTRACTOR for **Rs.9,84,677/= (RUPEES NINE LACS EIGHTY FOUR THOUSAND SIX HUNDRED SEVENTY SEVEN ONLY)** for the construction and completion of such WORKS and the remedying of an defects therein.

AND WHEREAS THE CONTRACTOR has already deposited 2% Pay Order for amounting to **Rs.20,500/=** vide Pay Order No. **8968763**, dated: **07-02-2014**, issued from **HBL- Gulistan-e-Jauhar, Ruffi Lake Drive Branch Karachi**, deposited by the contractor and remaining amount **Rs.77,968/=** will be deducted from his bill, the same will be kept with the EMPLOYER till the maintenance period of the work for the due fulfillment of the CONTRACTOR. Further 1% Water Charges will also be deducted from his bill as per Standard Operating Procedure (SOP).

[Handwritten signature]



KARACHI WATER & SEWERAGE BOARD

OFFICE OF THE CHIEF ENGINEER (IP&D)

BID EVALUATION REPORT


1	Name of Procuring Agency :	KARACHI WATER & SEWERAGE BOARD
2	Tender Reference No:	SPPRA Serial No.18744 I.D No. _____/2014
3	Tender Description/Name of Work/Item:	REHABILITATION / REPLACEMENT OF 12" AND 8" DIA SUNK DOWN SEWERAGE LINE AT DIFFERENT LOCATIONS IN UC-10 MAIN ROAD BLOCK 3 & 14, A-222 BLOCK-03 OF GULISTAN-E-JOHAR GULSHAN-E-IQBAL
4	Method of Procurement:	Single Stage (One Envelop)
5	Tender Published:	Through Web Site
6	Total Bid Documents Sold:	3 Nos
7	Total Bid Received:	3 Nos
8	Technical Bid Opening Date (if applicable):	N/A
9	No. of Bid Technically Qualified (if applicable)	N/A
10	Bid (s) Rejected:	NIL
11	Financial Bid Opening Date:	13-02-2014

12 BID EVALUATION REPORT


S #	Name of Firm / Bidder	COST OFFERED BY THE BIDDER	RANKING IN TERMS OF COST	COMPARISON WITH ESTIMATED COST	REASON FOR ACCEPTANCE/ REJECTION	REMARKS
1.	M/s. Universal Enterprises	Rs.9,84,677/-	1 st Lowest	@0.007%Below	Substantially Responsive	P.O # 8968763 dt:07-02-2014 from HBL Gulistan-e-Jauhar, Ruffi Lake Drive Branch Karachi Rs.20,500/-
2.	M/s.Fakhar & Brothers	Rs.9,85,099/-	2 nd Lowest	@0.036%Above	Substantially Responsive	P.O # 9038207 dt:12-02-2014 from HBL Rashid Minhas Road Branch Karachi Rs.20,000/-
3	M/s.Behzad Enterprises	Rs.9,85,717/-	3 rd Lowest	@0.099%Above	Substantially Responsive	P.O # 8968760 dt:06-02-2014 from HBL Gulistan-e-Jauhar, Ruffi Lake Drive Branch Karachi Rs.20,500/-


The all concerned bidder are being informed accordingly.


M/s. **Universal Enterprises** declared as the lowest responsive bidder by the Committee and recommended for sanction from Competent Authority.


(Nadeem Ahmed Khan)
Accounts Officer (District East)
Member / Secretary


(Saif-ul-Haque)
Additional Director Internal
Audit – KMC Member


(Maqsood Ahmed Shaikh)
Superintending Engineer (KMC)
Member


(Ghulam Qadir Abbas)
Chief Engineer (District East)
Member


(Abdul Rahim Khattai)
Chief Engineer (IPD)
Convener

COMPARATIVE STATEMENT

Name of Work: REHABILITATION / REPLACEMENT OF 12" AND 8" DIA SUNK DOWN SEWERAGE LINE AT DIFFERENT LOCATIONS IN UC-10 MAIN ROAD BLOCK 3 & 14, A-222 BLOCK-03 OF GULISTAN-E-JOHAR GULSHAN-E-IQBAL

Sl. No	Description of Work	Estimated Cost			M/s. Universal Enterprises		M/s. Fakhar & Brothers		M/s. Bclizad Enterprises	
		Quantity	Rate	Per %Sft / %Cft	Rate	Amount	Rate	Amount	Rate	Amount
1	Scarifying the Existing road Surface.	3830	116.16	%Sft	4,448.93	4,442.80	117.00	4,481.10	120.00	4,596.00
2	Dismantling and removal road matting	3830	605.00	%Cft	23,171.50	23,171.50	605.00	23,171.50	605.00	23,171.50
3	Excavation for pipe line in trenches and pits in all kind of soils of murum i/c trimming and dressing sides to true alignment and shape leveling of beds of trenches to correct level and earth within one chain as directed by Engineer Incharge providing fence guards, lights, flags and temporary crossing for non-vehicular traffic wherever required lift upto 5 ft (1.52 m) and lead upto one chain (30.5m). Lift 00' - 05"ft	10500	4650.00	%0Cft	48,825.00	48,825.00	4650.00	48,825.00	4650.00	48,825.00
4	Excavation for pipe line in trenches, pits in wet silt clay or mud i/c trimming and dressing sides to true alignment and shape, leveling of beds of trenches to correct level and grade, cutting joint holes and disposal of surplus earth within one chain as directed by Engineering Incharge. Providing fence guard, light, flags and temporary crossing for non vehicular traffic where ever required lift upto 5' ft and lead upto one chain. Lift 00' - 05'	4280.00	5400.00	%0Cft	23,112.00	23,112.00	5400.00	23,112.00	5500.00	23,540.00
	Lift 05' - 08'	4770.00	5950.00	%0Cft	28,381.50	28,381.50	6000.00	28,620.00	6000.00	28,620.00
	Lift 08' - 11'	300.00	6500.00	%0Cft	1,950.00	1,950.00	6500.00	1,950.00	6500.00	1,950.00
5	Providing, & Laying of RCC Pipes with Rubber Ring joint and fitting in trench including cutting, fitting, jointing with rubber ring i/c testing with water to specified pressure. 12" Dia 08" Dia Pipe	920	367.00	P/Rft	337,640.00	337,640.00	367.00	337,640.00	367.00	337,640.00
		144	206.00	P/Rft	29,664.00	29,664.00	206.00	29,664.00	206.00	29,664.00

Handwritten signature and date:
19/12

Handwritten signature and date:
19/12


Name of Work: REHABILITATION / REPLACEMENT OF 12" AND 8" DIA SUNK DOWN SEWERAGE LINE AT DIFFERENT LOCATIONS IN UC-10 MAIN ROAD BLOCK 3 & 14, A-222 BLOCK-03 OF GULISTAN-E-JOHAR GULSHAN-E-IQBAL


Description of Work	Estimated Cost			M/s. Universal Enterprises		M/s. Fakhar & Brothers		M/s. Behzad Enterprises		
	Quantity	Rate	Per	Amount	Rate	Amount	Rate	Amount	Rate	Amount
6 Providing manhole 4" feet (inside) and 5 feet clear depth with C.I Frame (15 Kg) cast in situ with 1:2:4 CC in 9" thick wall, 1:4:8: C.C in 6ft dia and 6" inch thick in foundation 1:2:4 C.C in benching 12" thick cement plastering with 1:3 C.M on all inside wall surfaces, channel and benching i/c making required nos of main and branch channels, 3/4" dia m.s foot rest @12" c/c i/c cost of excavation in all kinds of soil, backfilling and disposal of excavated stuff etc complete as per design and instruction of engineer incharge (prepared R.A on Sch.12).	15 Nos	14529.29	Each	217,939.35	14529.00	217,935.00	14530.00	217,950.00	14535.00	218,025.00
7 Add or deduct for extra / less depth then 5ft to 4ft dia manhole i.e footrest.	29 (+) Ft	2538.62	P/Ft	73,619.98	2538.00	73,602.00	2540.00	73,660.00	2540.00	73,660.00
8 Full hire charges of pumping set per day i/c of wages of driver and assistant fuel or electric energy platform for placing the pump etc at lower depth with suction and delivery pipes for pumping out water found at various depth from trenches including the cost of erection and dismantling after completion of the job. (i) Hire charges of pumping set upto 10 HP pumping out water from 10 ft deep trench	20 Days	1500.00	P/Day	30,000.00	1500.00	30,000.00	1500.00	30,000.00	1500.00	30,000.00
9 Making connection with the existing manhole including the cost of cutting hole in wall, making them good in C.C 1:2:4 and making the required channel etc. complete	20 Nos	180.00	Each	3,600.00	180.00	3,600.00	180.00	3,600.00	180.00	3,600.00
10 Manufacturing and supplying of RCC Manhole covers cast in situ 1:2:4 concrete ratio 3" deep at centre, reinforced with 1/2" dia tor steel bars at 4" C/C welded to a 3/16" thick 2" wide M.S plate two hook of 3/8" dia tor bar including compacting i/c cutting and transportation with in 10 miles. 21" dia.	15 Nos	913.63	Each	13,704.45	913.00	13,695.00	914.00	13,710.00	914.00	13,710.00


[Handwritten signatures and initials]


Name of Work: REHABILITATION / REPLACEMENT OF 12" AND 8" DIA SUNK DOWN SEWERAGE LINE AT DIFFERENT LOCATIONS IN UC-10 MAIN ROAD BLOCK 3 & 14, A-222 BLOCK-03 OF GULISTAN-E-JOHAR GULSHAN-E-IQBAL


Sl. No.	Description of Work	Estimated Cost			M/s. Universal Enterprises		M/s. Fakhar & Brothers		M/s. Behzad Enterprises	
		Quantity	Rate	Per	Rate	Amount	Rate	Amount	Rate	Amount
11	Sand Haro or any other source sand of same modulus of the fineness (Hill Sand)	2196.00	Cft	2425.00	%Cft	53,253.00	2425.00	53,253.00	2425.00	53,253.00
12	Refilling the excavated stuff in trenches 6" thick layer i/c watering ramming to full compaction etc complete.	17989.00	Cft	2760.00	%0Cft	49,649.64	2760.00	49,649.64	2760.00	49,649.64
13	Carriage of 100 Cft / 5 Tons of all materials like stone aggregate, spawl, coal, lime, surkhi etc B.G Rail fastening points and crossing bridges, Girders, pipes sheet Rail, M.S Bars etc. or 1000 Nos bricks. 10"x 5"x3" or 1000 Nos: tiles, 12"x6"x2" or 150 Cft of timber or 100 Maunds of fuel wood by trucks or any other means owned by the Contractors. Carriage for 07 Miles +437.00 + 95.52 + 76.89 + 70.45 + 64.43 +57.67 = 32.56= 804.52)	5691.00	Cft	804.52	%Cft	45,785.00	805	45,812.55	805	45,812.55
	TOTAL QUOTED / CORRECTED COST					984,744.35		985,098.79		985,716.69
	SAY					984,744		985,099		985,717


(Nadeem Ahmed Khan) (4/12)
Accounts Officer (Distt. East)
Member / Secretary


(Saif-ul-Haque)
Addl. Director Internal
Audit KMC - Member


(Maqsood Ahmed Shaikh)
Superintending Engineer (K.M.C)
Member


(Ghulam Qadir Abbas)
Chief Engineer (Distt. East)
Member


(Ghulam Rabbani Khalid)
Chief Engineer (P.D)
Co-optee

2nd
1st
3rd



KARACHI WATER & SEWERAGE BOARD

OFFICE OF THE CHIEF ENGINEER (IP&D)

BID EVALUATION REPORT


1	Name of Procuring Agency :	KARACHI WATER & SEWERAGE BOARD
2	Tender Reference No:	SPPRA Serial No.18744 I.D No. _____/2014
3	Tender Description/Name of Work/Item:	REHABILITATION / REPLACEMENT OF 15", 12" AND 8" DIA SUNK DOWN / BROKEN SEWERAGE LINE AT DIFFERENT LOCATIONS IN UNION COUNCIL NOS. 05,09 & 11 OF GULSHAN-E-IQBAL
4	Method of Procurement:	Single Stage (One Envelop)
5	Tender Published:	Through Web Site
6	Total Bid Documents Sold:	3 Nos
7	Total Bid Received:	3 Nos
8	Technical Bid Opening Date (if applicable):	N/A
9	No. of Bid Technically Qualified (if applicable)	N/A
10	Bid (s) Rejected:	01 No
11	Financial Bid Opening Date:	13-02-2014

12 BID EVALUATION REPORT


S #	Name of Firm / Bidder	COST OFFERED BY THE BIDDER	RANKING IN TERMS OF COST	COMPARISON WITH ESTIMATED COST	REASON FOR ACCEPTANCE/ REJECTION	REMARKS
1.	M/s.Fakhar & Brothers	Rs.9,95,141/-	1 st Lowest	@0.007%Below	Substantially Responsive	P.O # 9038208 dt:12-02-2014 from HBL Rashid Minhas Road Branch Karachi Rs.20,000/-
2.	M/s.Behzad Enterprises	Rs.9,95,666/-	2 nd Lowest	@0.046%Above	Substantially Responsive	P.O # 8968727 dt:04-02-2014 from HBL Gulistan-e-Jauhar, Ruffi Lake Drive Branch Karachi Rs.20,500/-
3	M/s.Universal Enterprises	Rs.9,97,401/-	-	@0.220%Above	Un-Responsive	P.O not Attached.


The all concerned bidder are being informed accordingly.


M/s. **Fakhar & Brothers** declared as the lowest responsive bidder by the Committee and recommended for sanction from Competent Authority.


(Nadeem Ahmed Khan)
Accounts Officer (District East)
Member / Secretary


(Saif-ul-Haque)
Additional Director Internal
Audit – KMC Member


(Maqsood Ahmed Shaikh)
Superintending Engineer (KMC)
Member





(Ghulam Qadir Abbas)
Chief Engineer (District East)
Member


(Abdul Rahim Khattai)
Chief Engineer (IPD)
Convener

COMPARATIVE STATEMENT

Name of Work: REHABILITATION / REPLACEMENT OF 15", 12" AND 8" DIA SUNK DOWN / BROKEN SEWERAGE LINE
AT DIFFERENT LOCATIONS IN UNION COUNCIL NOS. 05,09 & 11 OF GULSHAN-E-IQBAL-A21


Item No	Description of Work	Estimated Cost				M/s. Fakhar & Brothers		M/s. Behzad Enterprises	
		Quantity	Rate	Per	Amount	Rate	Amount	Rate	Amount
		Sft	%Sft	%Cft					
1	Scarifying the Existing road Surface.	3770	116.16		4,379.23	116.00	4,373.20	117.00	4,410.90
2	Dismantling and removal road matting	3770	605.00		22,808.50	605.00	22,808.50	605.00	22,808.50
3	Excavation for pipe line in trenches and pits in all kind of soils of murum i/c trimming and dressing sides to true alignment and shape leveling of beds of trenches to correct level and grade cutting joints holes and disposal of surplus earth within one chain as directed by Engineer Incharge providing fence guards, lights, flags sand temporary crossing for non-vehicular traffic wherever required lift upto 5 ft (1.52 m) and lead upto one chain (30.5m). Lift 00' - 05'ft	10935	4650.00	%0Cft	50,847.75	4650.00	50,847.75	4650.00	50,847.75
4	Excavation for pipe line in trenches, pits in wet silt clay or mud i/c trimming and dressing sides to true alignment and shape, leveling of beds of trenches to correct level and grade, cutting joint holes and disposal of surplus earth within one chain as directed by Engineering Incharge. Providing fence guard, light, flags and temporary crossing for non vehicular traffic where ever required lift upto 5' ft and lead upto one chain. Lift 00' - 05'	3020.00	5400.00	%0Cft	16,308.00	5400.00	16,308.00	5500.00	16,610.00
5	Lift 05' - 08'	4650.00	5950.00	%0Cft	27,667.50	5950.00	27,667.50	5950.00	27,667.50
	Lift 08' - 11'	280.00	6500.00	%0Cft	1,820.00	6500.00	1,820.00	6500.00	1,820.00
	Providing, & Laying of RCC Pipes with Rubber Ring Joint and fitting in trench including cutting, fitting, jointing with rubber ring i/c testing with water to specified pressure. 15" Dia Pipe	80	436.00	P/Rft	34,880.00	436.00	34,880.00	437.00	34,960.00
	12" Dia Pipe	715	367.00	P/Rft	262,405.00	367.00	262,405.00	367.00	262,405.00
	08" Dia Pipe	300	206.00	P/Rft	61,800.00	206.00	61,800.00	206.00	61,800.00

M/s. Fakhar & Brothers declared as the lowest responsive bidder by the Committee and

Name of Work: REHABILITATION / REPLACEMENT OF 15", 12" AND 8" DIA SUNK DOWN / BROKEN SEWERAGE LINE
 AT DIFFERENT LOCATIONS IN UNION COUNCIL NOS. 05,09 & 11 OF GULSHAN-E-IQBAL+A21


S.No	Description of Work	Estimated Cost						M/s. Behzad Enterprises		
		Quantity	Rate	Per	Amount	M/s. Fakhar & Brothers		Rate		
						Rate	Amount	Rate	Amount	
6	Providing manhole 4' feet (inside) and 5 feet clear depth with C.I Frame (15 Kg) cast in situ with 1:2:4 CC in 9" thick wall, 1:4:8: C.C in 6ft dia and 6" inch thick in foundation 1:2:4 C.C in benching 12" thick cement plastering with 1:3 C.M on all inside wall surfaces, channel and benching i/c making required nos of main and branch channels, 3/4" dia m.s foot rest @12" c/c i/c cost of excavation in all kinds of soil, backfilling and disposal of excavated stuff etc complete as per design and instruction of engineer incharge.	13	Nos	14529.29	Each	188,880.77	14529.00	188,877.00	14529.00	188,877.00
7	Add or deduct for extra / less depth then 5ft to 4ft dia manhole i.c footrest.	26	(+)Ft	2538.62	P/ft	66,004.12	2538.00	65,988.00	2539.00	66,014.00
8	Full hire charges of pumping set per day i/c of wages of driver and assistant fuel or electric energy platform for placing the pump etc at lower depth with suction and delivery pipes for pumping out water found at various depth from trenches including the cost of erection and dismantling after completion of the job. (i) Hire charges of pumping set upto 10 HP pumping out water from 10 ft deep trench	40	Days	1500.00	P/Day	60,000.00	1500.00	60,000.00	1500.00	60,000.00
9	Making connection with the existing manhole including the cost of cutting hole in wall, making them good in C.C 1:2:4 and making the required channel etc. complete	20	Nos	180.00	Each	3,600.00	180.00	3,600.00	180.00	3,600.00


14/12



M/s. Fakhar & Brothers declared as the lowest responsive bidder by the Committee and recommended for sanction from Competent Authority.


Name of Work: REHABILITATION / REPLACEMENT OF 15", 12" AND 8" DIA SUNK DOWN / BROKEN SEWERAGE LINE
AT DIFFERENT LOCATIONS IN UNION COUNCIL NOS. 05,09 & 11 OF GULSHIAN-E-IQBAL+A21


Sl. No	Description of Work	Estimated Cost			M/s. Fakhar & Brothers		M/s. Behzad Enterprises		
		Quantity	Rate	Per	Amount	Rate	Amount	Rate	Amount
10	Manufacturing and supplying of RCC Manhole covers cast in situ 1:2:4 concrete ratio 3" deep at centre, reinforced with 1/2" dia for steel bars at 4" C/C welded to a 3/16" thick 2" wide M.S plate two hook of 3/8" dia for bar including compacting i/c cutting and transportation with in 10 miles. 21" dia.	13 Nos	913.63	Each	11,877.19	913.00	11,869.00	914.00	11,882.00
11	Sand Haro or any other source sand of same modules of the fineness (Hill Sand)	3473.00 Cft	2425.00	%Cft	84,220.25	2425.00	84,220.25	2425.00	84,220.25
12	Refilling the excavated stuff in trenches 6" thick layer i/c watering ramming to full compaction etc complete.	15998.00 Cft	2760.00	%0Cft	44,154.48	2760.00	44,154.48	2760.00	44,154.48
13	Carriage of 100 Cft / 5 Tons of all materials like stone aggregate, spawl, coal, lime, surkhi etc B.G Rail fastening points and crossing bridges, Girders, pipes sheet Rail, M.S Bars etc. or 1000 Nos bricks, 10"x 5"x3" or 1000 Nos: tiles, 12"x6"x2" or 150 Cft of timber or 100 Maunds of fuel wood by trucks or any other means owned by the Contractors.	6657.00 Cft	804.52	%Cft	53,556.90	804	53,522.28	805	53,588.85
	Carriage for 07 Miles (407.00 + 95.52 + 76.89 + 70.45 + 64.43 + 57.67 + 32.56 = 804.52)				995,209.69		995,140.96		995,666.23
	TOTAL QUOTED / CORRECTED COST				995,210		995,141		995,666
	SAY								


(Nadeem Ahmed Khan)
Accounts Officer (Distt. East)
Member / Secretary


(Saif-ul-Haque)
Addl. Director Internal
Audit KMC - Member


(Maqsood Ahmed Shaikh)
Superintending Engineer (K.M.C)
Member


(Ghulam Qadir Abbas)
Chief Engineer (Distt. East)
Member


(Abdul Rahim Khan)
Chief Engineer (IPD)
Contractor

M/s. Fakhar & Brothers declared as the lowest responsive bidder by the Committee and recommended for sanction from Competent Authority.
