

BID EVALUATION REPORT

1	Name of Procuring Agency	Executive Engineer Education Works Division Jacobabad
2	Tender Reference No.	NIT No. 1925 dated: 21.02.2018
3	Tender Description / Name of Work / Item	Rehabilitaion / Expansion of High Priority 4560-Schools @ District Jacobabad. (Primary & Elemt: Schools) at GBPS - POLICE HEAD QUARTER, GGPS - PHOOL BAGH, GGPS - JUMO DASTI TALUKA Jacobabad (Package No. 1)
4	Method of Procurement	Single Stage - One envelope procedure
5	Tender Published	News Papers & on SPPRA Website
6	Total bid documents Sold:	03 Nos
7	Total Bids Received	03 Nos
8	Technical Bid Opening Date (if applicable)	Not Applicables
9	No. of bid technically qualified (if applicable)	Not Applicable
10	Bids(s) Rejected	-
11	Financial Bid Opening Date	13.03.2018
13	Bid Evaluation Report	

S.No.	Name of Firm or Bidder	Name of Work	Ranking in Terms of cost	Ranking in Terms of cost	Comparison with Estimated Cost (if any)	Reasons for acceptance / Rejection	Remarks
1	M/s. Muhammad Ramzan & Co.	GBPS - POLICE HEAD QUARTER	24821902	1st	0.11% Below	Lowest	Recommended for award of work
		GGPS - PHOOL BAGH	2690418				
		GGPS - JUMO DASTI	9202838				
			36722944				
2	M/s. Abdul Khaliq Dayo	GBPS - POLICE HEAD QUARTER	24894985	2nd	0.29% Above	Higher	Responsive
		GGPS - PHOOL BAGH	2701191				
		GGPS - JUMO DASTI	9239683				
			36835859				
3	M/s. Muhammad Anwar Brohi	GBPS - POLICE HEAD QUARTER	25042839	3rd	0.79% Above	Highest	Responsive
		GGPS - PHOOL BAGH	2714858				
		GGPS - JUMO DASTI	9193175				
			36950872				

(Signature)
 ASSISTANT ENGINEER
 PUBLIC HEALTH ENGINEERING
 SUB-DIVISION JACOBABAD




(Signature)
 (ABDUL REHMAN MANGI)
 ASSISTANT ENGINEER
 EDUCATION WORKS SUB-DIVISION
 JACOBABAD


(Signature)
 (ALTAF HUSSAIN BHURGRI)
 EXECUTIVE ENGINEER
 EDUCATION WORKS DIVISION
 JACOBABAD


**ATTENDENCE SHEET OF PARTICIPATION IN
TENDER PROCESS IN EDUCATION WORKS DIVISION JACOBABAD**

Name of Work :- **Rehabilitaion / Expansion of High Priority 4560-Schools @ District Jacobabad. (Primary & Elemt: Schools) at GBPS - POLICE HEAD QUARTER, GGPS - PHOOL BAGH, GGPS - JUMO DASTI TALUKA Jacobabad (Package No. 1)**

Executive Engineer Education Works Division JACOBABAD held on 13.03.2018

Sr. No	Name of Contractor / Firm	Signature
1	M/s. Muhammad Ramzan & Co.	
2	M/s. Abdul Khaliq Dayo	
3	M/s. Muhammad Anwar Brohi	


ASSISTANT ENGINEER
PUBLIC HEALTH ENGINEERING
SUB-DIVISION JACOBABAD


(ABDUL REHMAN MANGI)
ASSISTANT ENGINEER
EDUCATION WORKS SUB-DIVISION
JACOBABAD


(ALTAF HUSSAIN BHURGRI)
EXECUTIVE ENGINEER
EDUCATION WORKS DIVISION
JACOBABAD

**OFFICE OF THE
EXECUTIVE ENGINEER EDUCATION WORKS DIVISION JACOBABAD**


COMPRATIVE STATEMENT


NIT NO. EE/EWD/TC/ 1925 DATED: 21.02.2018

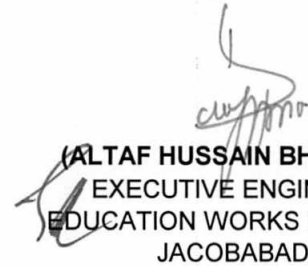
Name of Work :-

**Rehabilitaion / Expansion of High Priority 4560-Schools @
District Jacobabad. (Primary & Elemnt: Schools) at GBPS -
POLICE HEAD QUARTER, GGPS - PHOOL BAGH, GGPS -
JUMO DASTI TALUKA Jacobabad (Package No. 1)**

Sr. No	Name of Contractor	Rate Quoted	
1	M/s. Muhammad Ramzan & Co.	i) 10.45% Above ii) 6997456/- iii) 0.10% Below	(Part-A Schedule) (Part-A Non Schedule) (Part-B Schedule)
2	M/s. Abdul Khaliq Dayo	i) 10.85% Above ii) 7003456/- iii) At Par	(Part-A Schedule) (Part-A Non Schedule) (Part-B Schedule)
3	M/s. Muhammad Anwar Brohi	i) 11.25% Above ii) 7008456/- iii) 1.20% Above	(Part-A Schedule) (Part-A Non Schedule) (Part-B Schedule)


ASSISTANT ENGINEER
PUBLIC HEALTH ENGINEERING
SUB-DIVISION JACOBABAD


(ABDUL REHMAN MANGI)
ASSISTANT ENGINEER
EDUCATION WORKS SUB-DIVISION
JACOBABAD



(ALTAF HUSSAIN BHURGRI)
EXECUTIVE ENGINEER
EDUCATION WORKS DIVISION
JACOBABAD


GENERAL ABSTRACT

Name of Work :-

Rehabilitaion / Expansion of High Priority 4560-Schools @ District Jacobabad. (Primary & Elemt: Schools) at GBPS - POLICE HEAD QUARTER, GGPS - PHOOL BAGH, GGPS - JUMO DASTI TALUKA Jacobabad (Package No. 1)

Sr. No	Name of Contractor / Firm	Tender Amount
1	M/s. Muhammad Ramzan & Co.	36722944
2	M/s. Abdul Khalique Dayo	36835859
3	M/s. Muhammad Anwar Brohi	36950872


ASSISTANT ENGINEER
PUBLIC HEALTH ENGINEERING
SUB-DIVISION JACOBABAD


(ABDUL REHMAN MANGI)
ASSISTANT ENGINEER
EDUCATION WORKS SUB-DIVISION
JACOBABAD


(ALTAF HUSSAIN BHURGRI)
EXECUTIVE ENGINEER
EDUCATION WORKS DIVISION
JACOBABAD

Name of Work :-

Rehabilitaion / Expansion of High Priority 4560-Schools @ District Jacobabad. (Primary & Elemt: Schools) at GBPS - POLICE HEAD QUARTER, GGPS - PHOOL BAGH, GGPS - JUMO DASTI TALUKA Jacobabad (Package No. 1)


SUMMARY OF COST


Sr. No	Item of Work	Schedule B Amount	Contractor Rate	Amount
1	Civil Schedule Items	29873770	i) 10.45% Above	29444121
3	Non Schedule Items	6997456	ii) 6997456/-	6997456
3	W/S & S/F	281649	iii) 0.10% Below	281367


Total Amount of Bid

A + B + C =

36722944


ASSISTANT ENGINEER
PUBLIC HEALTH ENGINEERING
SUB-DIVISION JACOBABAD


(ABDUL REHMAN MANGI)
ASSISTANT ENGINEER
EDUCATION WORKS SUB-DIVISION
JACOBABAD



(ALTAF HUSSAIN BHURGRI)
EXECUTIVE ENGINEER
EDUCATION WORKS DIVISION
JACOBABAD


BIDDER QUALIFICATION REPORT

NIT NO. EE/EWD/TC/ 1925 DATED: 21.02.2018

EDUCATION WORKS DIVISION JACOBABAD

1 Name of Procuring Agency	<u>Executive Engineer Education Works Division JACOBABAD</u>
2 Tender Reference No.	<u>NIT No. 1925, dated: 21.02.2018</u>
3 Tender Description / Name of Work / Item	<u>Rehabilitaion / Expansion of High Priority 4560-Schools @ District Jacobabad. (Primary & Elemt: Schools) at GBPS - POLICE HEAD QUARTER, GGPS - PHOOL BAGH, GGPS - JUMO DASTI TALUKA Jacobabad (Package No. 1)</u>
4 Method of Procurement	<u>Single Stage - One envelope procedure</u>
5 Tender Published	<u>News Papers & on SPPRA Website</u>
6 N.T.N	<u>Available</u>
7 Registration with P.E.C	<u>Registered</u>
8 Sindh Board of Revenue	<u>Registered</u>
9 Relevant Experience	<u>Available</u>
10 Turnover of at least last three years	<u>Available</u>
11 Funds / Budget	<u>Available</u>
12 05% Earnest Money	<u>Available</u>
13 Tender Fee / Cost Bidding Document	<u>Deposited</u>


ASSISTANT ENGINEER
PUBLIC HEALTH ENGINEERING
SUB-DIVISION JACOBABAD


(ABDUL REHMAN MANGI)
ASSISTANT ENGINEER
EDUCATION WORKS SUB-DIVISION
JACOBABAD


(ALTAF HUSSAIN BHURGRI)
EXECUTIVE ENGINEER
EDUCATION WORKS DIVISION
JACOBABAD

Method and procedure of procurement: NATIONAL COMPETITIVE BIDDING (SINGLE STAGE-ONE ENVELOPE).

MINUTES OF BID OPENING MEETING


A meeting of the procurement committee of this department was held on dated: 13.03.2018. for opening the bids received in respect of subject NIT till the deadlines of submission. The meeting was attended by all following members of the procurement committee and the representative of bidders. (Attendance sheet is enclosed).

The bids were opened at **2:00 PM** in the presence of the above mentioned participants and the rates quoted by bidders were read aloud and encircled by Chairman of the Procurement Committee. All the members of the procurement committee signed each and every page of financial proposal/bids. The bids do not contain any over-writing or cutting. (Also mention cutting or over writing if any). Following is the details of bids announced.


The committee shall examine all the bids as per the Qualification/ eligibility criteria provided in the bidding documents, arithmetical checks and verify the documents and bid security submitted by the bidders.

The meeting ended with the note of thanks to and from the chair.


(MEMBER)


ASSISTANT ENGINEER
PUBLIC HEALTH ENGINEERING
SUB-DIVISION JACOBABAD

(MEMBER)


(ABDUL REHMAN MANGI)
ASSISTANT ENGINEER
EDUCATION WORKS SUB-DIVISION
JACOBABAD

(CHAIRMAN)


(ALTAF HUSSAIN BHURGRI)
EXECUTIVE ENGINEER
EDUCATION WORKS DIVISION
JACOBABAD

FINANCIAL REVIEW

NAME OF WORK:-

Rehabilitation / Expansion of High Priority 4560-Schools @ District Jacobabad. (Primary & Elemt: Schools) at GBPS - POLICE HEAD QUARTER, GGPS - PHOOL BAGH, GGPS - JUMO DASTI TALUKA Jacobabad (Package No. 1)

S #	Description	Estimated Cost	M/s. Muhammad Ramzan & Co.		M/s. Abdul Khaliq Dayo		M/s. Muhammad Anwar Brohi	
			Rate	Amount	Rate	Amount	Rate	Amount
1	2	3	4	5	6	7	8	9

PART-A CIVIL SCHEDULE ITEMS

1	Schedule Items	26,658,326		26,658,326		26,658,326		26,658,326
2	Carriage of Material	2,815,503	i) 10.45% Above	2,785,795	i) 10.85% Above	2,892,428	i) 11.25% Above	2,999,062
3	Contingency	399,941						
4	Total Part-A	29,873,770		29,444,121		29,550,754		29,657,388

PART-A NON SCHEDULE

1	Non Schedule Items	6,997,456		6,997,456		7,003,456		7,008,456
2	Total Part-C	6,997,456		6,997,456		7,003,456		7,008,456

PART-B W/S & S/F

1	Schedule Items	281,649		281,649		281,649		281,649
2			ii) 0.10% Below	282	iii) At Par		iii) 1.20% Above	3,380
3	Total Part-B	281,649		281,367		281,649		285,029
4	Total Part-A+B+C	37,152,875		36,722,944		36,835,859		36,950,872

The Lowest rate quoted by M/s. Muhammad Ramzan & Co. Government Contractor are :
 Part-A @ Rs. 29444121/- **10.45% Above** on Estimate (Rupees Two Crore, Ninety Four Lacs,
 Forty Four Thousand, One Hundred, Twenty One) Only
 Part-A @ Rs. 6997456/- **Lowest Quoted Rates**, on Estimate (Rupees Sixty Nine Lacs, Ninety Seven Thousand
 Four Hundred, Fifty Six) Only
 Part-B @ Rs. 281367/- **0.10% Below**, on Estimate (Rupees Two Lac, Eighty One Thousand, Three Hundred,
 Sixty Seven) Only

Abdul Rehman Mangi
 ASSISTANT ENGINEER
 PUBLIC HEALTH ENGINEERING
 SUB-DIVISION JACOBABAD

Abdul Rehman Mangi
 ASSISTANT ENGINEER
 EDUCATION WORKS SUB-DIVISION
 JACOBABAD

Altair Hussain Bhurgri
 EXECUTIVE ENGINEER
 EDUCATION WORKS DIVISION
 JACOBABAD

BID EVALUATION REPORT

1	Name of Procuring Agency	Executive Engineer Education Works Division JACOBABAD
2	Tender Reference No.	NIT No. 1925, dated: 21.02.2018
3	Tender Description / Name of Work / Item	Rehabilitaion / Expansion of High Priority 4560-Schools @ District Jacobabad. (Primary & Elemt: Schools) at GBPS - JACOBABAD (MAIN) GBPS - HAMIDIA TALUKA Jacobabad (Package No. 2)
4	Method of Procurement	Single Stage - One envelope procedure
5	Tender Published	News Papers & on SPPRA Website
6	Total bid documents Sold:	03 Nos
7	Total Bids Received	03 Nos
8	Technical Bid Opening Date (if applicable)	Not Applicable
9	No. of bid technically qualified (if applicable)	Not Applicable
10	Bids(s) Rejected	-
11	Financial Bid Opening Date	13.03.2018

13 Bid Evaluation Report

S.No.	Name of Firm or Bidder	Cost of offered by the Bidders	Ranking in Terms of cost	Comparison with Estimated Cost	Reasons for acceptance / Rejection	Remarks	
1	M/s. Abdul Khaliq Dayo	25225960	1st Lowest	i) 10.25% Above	Part-A	Quality as per evaluation criteria	Recommended for award of work
		7212884		ii) 7212884/-	N.S.I		
		137336		iii) 0.15% Below	Part-B		
		32576179					
2	M/s. Muhammad Anwar Brohi	25363244	2nd Lowest	i) 10.85% Above	Part-A	Rejected Being Hieghest	Responsive
		7222884		ii) 7222884/-	N.S.I		
		137542		iii) At Par	Part-B		
		32723670					
3	M/s. Zulfiqar Ali Buriro	25454767	3rd Lowest	i) 11.25% Above	Part-A	Rejected Being Hieghest	Responsive
		7224884		ii) 7224884/-	N.S.I		
		139193		iii) 1.20% Above	Part-B		
		32818843					

(Signature)
 ASSISTANT ENGINEER
 PUBLIC HEALTH ENGINEERING
 SUB-DIVISION JACOBABAD




(Signature)
 (ABDUL REHMAN MANGI)
 ASSISTANT ENGINEER
 EDUCATION WORKS SUB-DIVISION
 JACOBABAD


(Signature)
 (ALTAF HUSSAIN BHURGRI)
 EXECUTIVE ENGINEER
 EDUCATION WORKS DIVISION
 JACOBABAD


**ATTENDANCE SHEET OF PARTICIPATION IN
TENDER PROCESS IN EDUCATION WORKS DIVISION JACOBABAD**


Name of Work :- **Rehabilitaion / Expansion of High Priority 4560-Schools @ District Jacobabad. (Primary & Elemt: Schools) at GBPS - JACOBABAD (MAIN) GBPS - HAMIDIA TALUKA Jacobabad (Package No. 2)**

Executive Engineer Education Works Division JACOBABAD held on 13.03.2018

Sr. No	Name of Contractor / Firm	Signature
1	M/s. Abdul Khalique Dayo	
2	M/s. Muhammad Anwar Brohi	
3	M/s. Zulfiqar Ali Buriro	


ASSISTANT ENGINEER
PUBLIC HEALTH ENGINEERING
SUB-DIVISION JACOBABAD


(ABDUL REHMAN MANGI)
ASSISTANT ENGINEER
EDUCATION WORKS SUB-DIVISION
JACOBABAD


(ALTAF HUSSAIN BHURGRI)
EXECUTIVE ENGINEER
EDUCATION WORKS DIVISION
JACOBABAD

**OFFICE OF THE
EXECUTIVE ENGINEER EDUCATION WORKS DIVISION JACOBABAD**


COMPRATIVE STATEMENT


NIT NO. EE/EWD/TC/ 1925 DATED: 21.02.2018


Name of Work :-

**Rehabilitaion / Expansion of High Priority 4560-Schools @
District Jacobabad. (Primary & Elemt: Schools) at GBPS -
JACOBABAD (MAIN) GBPS - HAMIDIA TALUKA
Jacobabad (Package No. 2)**

Sr. No	Name of Contractor	Rate Quoted	
1	M/s. Abdul Khalique Dayo	i) 10.25% Above ii) 7212884/- iii) 0.15% Below	(Part-A Schedule) (Part-A Non Schedule) (Part-B Schedule)
2	M/s. Muhammad Anwar Brohi	i) 10.85% Above ii) 7222884/- iii) At Par	(Part-A Schedule) (Part-A Non Schedule) (Part-B Schedule)
3	M/s. Zulfiqar Ali Buriro	i) 11.25% Above ii) 7224884/- iii) 1.20% Above	(Part-A Schedule) (Part-A Non Schedule) (Part-B Schedule)


**ASSISTANT ENGINEER
PUBLIC HEALTH ENGINEERING
SUB-DIVISION JACOBABAD**


**(ABDUL REHMAN MANGI)
ASSISTANT ENGINEER
EDUCATION WORKS SUB-DIVISION
JACOBABAD**



**(ALTAF HUSSAIN BHURGRI)
EXECUTIVE ENGINEER
EDUCATION WORKS DIVISION
JACOBABAD**


GENERAL ABSTRACT


Name of Work :-

Rehabilitaion / Expansion of High Priority 4560-Schools @
District Jacobabad. (Primary & Elemt: Schools) at GBPS -
JACOBABAD (MAIN) GBPS - HAMIDIA TALUKA
Jacobabad (Package No. 2)

Sr. No	Name of Contractor / Firm	Tender Amount
1	M/s. Abdul Khaliq Dayo	32576179
2	M/s. Muhammad Anwar Brohi	32723670
3	M/s. Zulfiqar Ali Buriro	32818843


ASSISTANT ENGINEER
PUBLIC HEALTH ENGINEERING
SUB-DIVISION JACOBABAD


(ABDUL REHMAN MANGI)
ASSISTANT ENGINEER
EDUCATION WORKS SUB-DIVISION
JACOBABAD


(ALTAF HUSSAIN BHURGRI)
EXECUTIVE ENGINEER
EDUCATION WORKS DIVISION
JACOBABAD

Name of Work :-

Rehabilitaion / Expansion of High Priority 4560-Schools @ District Jacobabad. (Primary & Elemt: Schools) at GBPS - JACOBABAD (MAIN) GBPS - HAMIDIA TALUKA Jacobabad (Package No. 2)


SUMMARY OF COST


Sr. No	Item of Work	Schedule B Amount	Contractor Rate	Amount
1	Civil Schedule Items	25676497	i) 10.25% Above	25225960
3	Non Schedule Items	7212884	ii) 7212884/-	7212884
3	W/S & S/F	137542	iii) 0.15% Below	137336


Total Amount of Bid

A + B + C =

32576179


ASSISTANT ENGINEER
PUBLIC HEALTH ENGINEERING
SUB-DIVISION JACOBABAD


(ABDUL REHMAN MANGI)
ASSISTANT ENGINEER
EDUCATION WORKS SUB-DIVISION
JACOBABAD



(ALTAF HUSSAIN BHURGRI)
EXECUTIVE ENGINEER
EDUCATION WORKS DIVISION
JACOBABAD


BIDDER QUALIFICATION REPORT


NIT NO. EE/EWD/TC/ 1925 DATED: 21.02.2018

EDUCATION WORKS DIVISION JACOBABAD

1	Name of Procuring Agency	<u>Executive Engineer Education Works Division JACOBABAD</u>
2	Tender Reference No.	<u>NIT No. 1925, dated: 21.02.2018</u>
3	Tender Description / Name of Work / Item	<u>Rehabilitaion / Expansion of High Priority 4560-Schools @ District Jacobabad. (Primary & Elemt: Schools) at GBPS - JACOBABAD (MAIN) GBPS - HAMIDIA TALUKA Jacobabad (Package No. 2)</u>
4	Method of Procurement	<u>Single Stage - One envelope procedure</u>
5	Tender Published	<u>News Papers & on SPPRA Website</u>
6	N.T.N	<u>Available</u>
7	Registration with P.E.C	<u>Registered</u>
8	Sindh Board of Revenue	<u>Registered</u>
9	Relevant Experience	<u>Available</u>
10	Turnover of at least last three years	<u>Available</u>
11	Funds / Budget	<u>Available</u>
12	05% Earnest Money	<u>Available</u>
13	Tender Fee / Cost Bidding Document	<u>Deposited</u>


ASSISTANT ENGINEER
PUBLIC HEALTH ENGINEERING
SUB-DIVISION JACOBABAD


(ABDUL REHMAN MANGI)
ASSISTANT ENGINEER
EDUCATION WORKS SUB-DIVISION
JACOBABAD


(ALTAF HUSSAIN BHURGRI)
EXECUTIVE ENGINEER
EDUCATION WORKS DIVISION
JACOBABAD

Method and procedure of procurement: NATIONAL COMPETITIVE BIDDING (SINGLE STAGE-ONE ENVELOPE).

MINUTES OF BID OPENING MEETING

A meeting of the procurement committee of this department was held on dated: 13.03.2018. for opening the bids received in respect of subject NIT till the deadlines of submission. The meeting was attended by all following members of the procurement committee and the representative of bidders. (Attendance sheet is enclosed).

The bids were opened at **2:00 PM** in the presence of the above mentioned participants and the rates quoted by bidders were read aloud and encircled by Chairman of the Procurement Committee. All the members of the procurement committee signed each and every page of financial proposal/bids. The bids do not contain any over-writing or cutting. (*Also mention cutting or over writing if any*). Following is the details of bids announced.


The committee shall examine all the bids as per the Qualification/ eligibility criteria provided in the bidding documents, arithmetical checks and verify the documents and bid security submitted by the bidders.


The meeting ended with the note of thanks to and from the chair.


(MEMBER)

(MEMBER)

(CHAIRMAN)


ASSISTANT ENGINEER
PUBLIC HEALTH ENGINEERING
SUB-DIVISION JACOBABAD


(ABDUL REHMAN MANGI)
ASSISTANT ENGINEER
EDUCATION WORKS SUB-DIVISION
JACOBABAD


(ALTAH HUSSAIN BHURGRI)
EXECUTIVE ENGINEER
EDUCATION WORKS DIVISION
JACOBABAD

FINANCIAL REVIEW

NAME OF WORK:-

Rehabilitaion / Expansion of High Priority 4560-Schools @ District Jacobabad. (Primary & Elemt: Schools) at GBPS - JACOBABAD (MAIN)
GBPS - HAMIDIA TALUKA Jacobabad (Package No. 2)

S #	Discription	Estimated Cost	M/s. Abdul Khalique Dayo		M/s. Muhammad Anwar Brohi		M/s. Zulfiqar Ali Buriro	
			Rate	Amount	Rate	Amount	Rate	Amount
1	2	3	4	5	6	7	8	9
PART-A CIVIL SCHEDULE ITEMS								
1	Schedule Items	22,880,689		22,880,689		22,880,689		22,880,689
2	Carriage of Material	2,377,408	i) 10.25% Above	2,345,271	i) 10.85% Above	2,482,555	i) 11.25% Above	2,574,078
3	Contingency	418,400						
4	Total Part-A	25,676,497		25,225,960		25,363,244		25,454,767

PART-A NON SCHEDULE

1	Non Schedule Items	7,212,884		7,212,884		7,222,884		7,224,884
2	Total Part-C	7,212,884		7,212,884		7,222,884		7,224,884

PART-B W/S & S/F

1	Schedule Items	137,542		137,542		137,542		137,542
2			iii) 0.15% Below	206	iii) At Par		iii) 1.20% Above	1,651
3	Total Part-B	137,542		137,336		137,542		139,193
4	Total Part-A+B+C	33,026,923		32,576,179		32,723,670		32,818,843
	A) Total Cost as per Estimate	33,026,923						
	B) Total Cost as per Tender	32,576,179						
	Saving A-B	450,744						
	Percentage Saving	1.36%						
	A.A Amount	-						
	Lowest Tender Amount	32,576,179						
	Saving Over A.A	-						

The Lowest rate quoted by M/s. Abdul Khalique Dayo Government Contractor are :

Part-A @ Rs. 25225960/- 10.25% Above on Estimate (Rupees Two Crore, Fifty Two Lacs,

Twenty Five Thousand, Nine Hundred, Sixty) Only

Part-A @ Rs. 7212884/- Lowest Quoted Rates, on Estimate (Rupees Seventy Two Lacs, Twelve Thousand,

Eight Hundred, Eighty Four) Only

Part-B @ Rs. 137336/- 0.15% Below, on Estimate (Rupees One Lac, Thirty Seven Thousand, Three Hundred,

Thirty Six) Only

(Signature)
ASSISTANT ENGINEER
PUBLIC HEALTH ENGINEERING
SUB-DIVISION JACOBABAD

(Signature)
(ABDUL REHMAN MANGI)
ASSISTANT ENGINEER
EDUCATION WORKS SUB-DIVISION
JACOBABAD

(Signature)
(ALTAH HUSSAIN BHURGI)
EXECUTIVE ENGINEER
EDUCATION WORKS DIVISION
JACOBABAD

BID EVALUATION REPORT

1 Name of Procuring Agency	Executive Engineer Education Works Division Jacobabad
2 Tender Reference No.	NIT No. 1925 dated: 21.02.2018
3 Tender Description / Name of Work / Item	Rehabilitaion / Expansion of High Priority 4560-Schools @ District Jacobabad. (Primary & Elemt: Schools) at GBPS - RAILWAY COLONY, GBPS - SOOMRA MUHALLA, GBPS - BUGHIA, GBPS - HAWALDAR BROHI, GBPS - SPECIAL FORCE TALUKA Jacobabad (Package No. 3)
4 Method of Procurement	Single Stage - One envelope procedure
5 Tender Published	News Papers & on SPPRA Website
6 Total bid documents Sold:	03 Nos
7 Total Bids Received	03 Nos
8 Technical Bid Opening Date (if applicable)	Not Applicables
9 No. of bid technically qualified (if applicable)	Not Applicable
10 Bids(s) Rejected	-
11 Financial Bid Opening Date	13.03.2018
13 Bid Evaluation Report	

S.No.	Name of Firm or Bidder	Name of Work	Ranking in Terms of cost	Ranking in Terms of cost	Comparison with Estimated Cost (if any)	Reasons for acceptance / Rejection	Remarks
1	M/s. Imtiaz Ali	GBPS - RAILWAY COLONY	6306634	1st	0.17% Below	Lowest	Recommended for award of work
		GBPS - SOOMRA MUHALLA	5746038				
		GBPS - BUGHIA	7366218				
		GBPS - HAWALDAR BROHI	5922167				
		GBPS - SPECIAL FORCE	13563826				
			38904883				
2	M/s. Abdul Khaliq Dayo	GBPS - RAILWAY COLONY	6320532	2nd	0.05% Above	Higher	Responsive
		GBPS - SOOMRA MUHALLA	5758700				
		GBPS - BUGHIA	7379513				
		GBPS - HAWALDAR BROHI	5931280				
		GBPS - SPECIAL FORCE	13587218				
			38977243				
3	M/s. Raja Panhyar	GBPS - RAILWAY COLONY	6369808	3rd	0.83% Above	Highest	Responsive
		GBPS - SOOMRA MUHALLA	5803596				
		GBPS - BUGHIA	7440005				
		GBPS - HAWALDAR BROHI	5981489				
		GBPS - SPECIAL FORCE	13609165				
			39204063				

(Signature)
 ASSISTANT ENGINEER
 PUBLIC HEALTH ENGINEERING
 SUB-DIVISION JACOBABAD



(Signature)
 (ABDUL REHMAN MANGI)
 ASSISTANT ENGINEER
 EDUCATION WORKS SUB-DIVISION
 JACOBABAD


(Signature)
 (ALTAF HUSSAIN BHURGRI)
 EXECUTIVE ENGINEER
 EDUCATION WORKS DIVISION
 JACOBABAD


**ATTENDENCE SHEET OF PARTICIPATION IN
TENDER PROCESS IN EDUCATION WORKS DIVISION JACOBABAD**


Name of Work :- **Rehabilitaion / Expansion of High Priority 4560-Schools @ District Jacobabad. (Primary & Elemt: Schools) at GBPS - RAILWAY COLONY, GBPS - SOOMRA MUHALLA, GBPS - BUGHIA, GBPS - HAWALDAR BROHI, GBPS - SPECIAL FORCE TALUKA Jacobabad (Package No. 3)**

Executive Engineer Education Works Division JACOBABAD held on 13.03.2018

Sr. No	Name of Contractor / Firm	Signature
1	M/s. Imtiaz Ahmed	
2	M/s. Abdul Khaliq Dayo	
3	M/s. Raja Panhyar	


ASSISTANT ENGINEER
PUBLIC HEALTH ENGINEERING
SUB-DIVISION JACOBABAD


(ABDUL REHMAN MANGI)
ASSISTANT ENGINEER
EDUCATION WORKS SUB-DIVISION
JACOBABAD


(ALTAF HUSSAIN BHURGRI)
EXECUTIVE ENGINEER
EDUCATION WORKS DIVISION
JACOBABAD


**OFFICE OF THE
EXECUTIVE ENGINEER EDUCATION WORKS DIVISION JACOBABAD
COMPRATIVE STATEMENT**


NIT NO. EE/EWD/TC/ 1925 DATED: 21.02.2018


Name of Work :-

**Rehabilitaion / Expansion of High Priority 4560-Schools @
District Jacobabad. (Primary & Elemt: Schools) at GBPS -
RAILWAY COLONY, GBPS - SOOMRA MUHALLA, GBPS -
BUGHIA, GBPS - HAWALDAR BROHI, GBPS - SPECIAL
FORCE TALUKA Jacobabad (Package No. 3)**

Sr. No	Name of Contractor	Rate Quoted	
1	M/s. Imtiaz Ahmed	i) 10.0% Above ii) 7758170/- iii) 0.22% Below	(Part-A Schedule) (Part-A Non Schedule) (Part-B Schedule)
2	M/s. Abdul Khaliq Dayo	i) 10.22% Above ii) 7768170/- iii) At Par	(Part-A Schedule) (Part-A Non Schedule) (Part-B Schedule)
3	M/s. Raja Panhyar	i) 11.0% Above ii) 7773170/- iii) 1.0% Above	(Part-A Schedule) (Part-A Non Schedule) (Part-B Schedule)


ASSISTANT ENGINEER
PUBLIC HEALTH ENGINEERING
SUB-DIVISION JACOBABAD


(ABDUL REHMAN MANGI)
ASSISTANT ENGINEER
EDUCATION WORKS SUB-DIVISION
JACOBABAD



(ALTAF HUSSAIN BHURGRI)
EXECUTIVE ENGINEER
EDUCATION WORKS DIVISION
JACOBABAD


GENERAL ABSTRACT


Name of Work :-

Rehabilitaion / Expansion of High Priority 4560-Schools @ District Jacobabad. (Primary & Elemt: Schools) at GBPS - RAILWAY COLONY, GBPS - SOOMRA MUHALLA, GBPS - BUGHIA, GBPS - HAWALDAR BROHI, GBPS - SPECIAL FORCE TALUKA Jacobabad (Package No. 3)

Sr. No	Name of Contractor / Firm	Tender Amount
1	M/s. Imtiaz Ahmed	38904883
2	M/s. Abdul Khaliq Dayo	38977243
3	M/s. Raja Panhyar	39204063


ASSISTANT ENGINEER
PUBLIC HEALTH ENGINEERING
SUB-DIVISION JACOBABAD


(ABDUL REHMAN MANGI)
ASSISTANT ENGINEER
EDUCATION WORKS SUB-DIVISION
JACOBABAD


(ALTAF HUSSAIN BHURGRI)
EXECUTIVE ENGINEER
EDUCATION WORKS DIVISION
JACOBABAD

Name of Work :-


Rehabilitaion / Expansion of High Priority 4560-Schools @ District Jacobabad. (Primary & Elemt: Schools) at GBPS - RAILWAY COLONY, GBPS - SOOMRA MUHALLA, GBPS - BUGHIA, GBPS - HAWALDAR BROHI, GBPS - SPECIAL FORCE TALUKA Jacobabad (Package No. 3)


SUMMARY OF COST

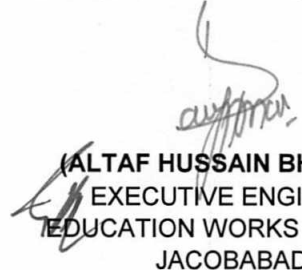
Sr. No	Item of Work	Schedule B Amount	Contractor Rate	Amount
1	Civil Schedule Items	30965968	i) 10.0% Above	30818871
3	Non Schedule Items	7758170	ii) 7758170/-	7758170
3	W/S & S/F	328565	iii) 0.22% Below	327842

Total Amount of Bid

A + B + C = 38904883


ASSISTANT ENGINEER
PUBLIC HEALTH ENGINEERING
SUB-DIVISION JACOBABAD


(ABDUL REHMAN MANGI)
ASSISTANT ENGINEER
EDUCATION WORKS SUB-DIVISION
JACOBABAD



(ALTAF HUSSAIN BHURGRI)
EXECUTIVE ENGINEER
EDUCATION WORKS DIVISION
JACOBABAD


BIDDER QUALIFICATION REPORT


NIT NO. EE/EWD/TC/ 1925 DATED: 21.02.2018

EDUCATION WORKS DIVISION JACOBABAD

1 Name of Procuring Agency	<u>Executive Engineer Education Works Division JACOBABAD</u>
2 Tender Reference No.	<u>NIT No. 1925, dated: 21.02.2018</u>
3 Tender Description / Name of Work / Item	<u>Rehabilitaion / Expansion of High Priority 4560-Schools @ District Jacobabad. (Primary & Elemt: Schools) at GBPS - RAILWAY COLONY, GBPS - SOOMRA MUHALLA, GBPS - BUGHIA, GBPS - HAWALDAR BROHI, GBPS - SPECIAL FORCE TALUKA Jacobabad (Package No. 3)</u>
4 Method of Procurement	<u>Single Stage - One envelope procedure</u>
5 Tender Published	<u>News Papers & on SPPRA Website</u>
6 N.T.N	<u>Available</u>
7 Registration with P.E.C	<u>Registered</u>
8 Sindh Board of Revenue	<u>Registered</u>
9 Relevant Experience	<u>Available</u>
10 Turnover of at least last three years	<u>Available</u>
11 Funds / Budget	<u>Available</u>
12 05% Earnest Money	<u>Available</u>
13 Tender Fee / Cost Bidding Document	<u>Deposited</u>


ASSISTANT ENGINEER
PUBLIC HEALTH ENGINEERING
SUB-DIVISION JACOBABAD


(ABDUL REHMAN MANGI)
ASSISTANT ENGINEER
EDUCATION WORKS SUB-DIVISION
JACOBABAD


(ALTAF HUSSAIN BHURGRI)
EXECUTIVE ENGINEER
EDUCATION WORKS DIVISION
JACOBABAD

NIT NO. EE/EWD/TC/ 1925 DATED: 21.02.2018

Method and procedure of procurement: NATIONAL COMPETITIVE BIDDING (SINGLE STAGE-ONE ENVELOPE).

MINUTES OF BID OPENING MEETING


A meeting of the procurement committee of this department was held on dated: 13.03.2018. for opening the bids received in respect of subject NIT till the deadlines of submission. The meeting was attended by all following members of the procurement committee and the representative of bidders. (Attendance sheet is enclosed).

The bids were opened at **2:00 PM** in the presence of the above mentioned participants and the rates quoted by bidders were read aloud and encircled by Chairman of the Procurement Committee. All the members of the procurement committee signed each and every page of financial proposal/bids. The bids do not contain any over-writing or cutting. (Also mention cutting or over writing if any). Following is the details of bids announced.


The committee shall examine all the bids as per the Qualification/ eligibility criteria provided in the bidding documents, arithmetical checks and verify the documents and bid security submitted by the bidders.

The meeting ended with the note of thanks to and from the chair.


(MEMBER)


ASSISTANT ENGINEER
PUBLIC HEALTH ENGINEERING
SUB-DIVISION JACOBABAD

(MEMBER)


(ABDUL REHMAN MANGI)
ASSISTANT ENGINEER
EDUCATION WORKS SUB-DIVISION
JACOBABAD

(CHAIRMAN)


(ALTAF HUSSAIN BHURGRI)
EXECUTIVE ENGINEER
EDUCATION WORKS DIVISION
JACOBABAD

FINANCIAL REVIEW

NAME OF WORK:-

Rehabilitation / Expansion of High Priority 4560-Schools @ District Jacobabad. (Primary & Elment: Schools) at GBPS - RAILWAY COLONY,
GBPS - SOOMRA MUHALLA, GBPS - BUGHIA, GBPS - HAWALDAR BROHI, GBPS - SPECIAL FORCE TALUKA Jacobabad (Package No. 3)

S#	Description	Estimated Cost	M/s. Imtiaz Ahmed		M/s. Abdul Khaliq Dayo		M/s. Raja Panhyar	
			Rate	Amount	Rate	Amount	Rate	Amount
1	2	3	4	5	6	7	8	9

PART-A CIVIL SCHEDULE ITEMS

1	Schedule Items	28,017,155		28,017,155		28,017,155		28,017,155
2	Carriage of Material	2,848,813	i) 10.0% Above	2,801,716	i) 10.22% Above	2,863,353	i) 11.0% Above	3,081,887
3	Contingency	100,000						
4	Total Part-A	30,965,968		30,818,871		30,880,508		31,099,042

PART-A NON SCHEDULE

1	Non Schedule Items	7,758,170		7,758,170		7,768,170		7,773,170
2	Total Part-C	7,758,170		7,758,170		7,768,170		7,773,170

PART-B W/S & S/F

1	Schedule Items	328,565		328,565		328,565		328,565
2			iii) 0.22% Below	723	iii) At Par		iii) 1.0% Above	3,286
3	Total Part-B	328,565		327,842		328,565		331,851
4	Total Part-A+B+C	39,052,703		38,904,883		38,977,243		39,204,063

The Lowest rate quoted by M/s. Imtiaz Ahmed Government Contractor are :

Part-A @ Rs. 30818871/- **10.0% Above** on Estimate (Rupees Three Crore, Eight Lacs, Eighteen Thousand Eight Hundred, Seventy One) Only

Part-A @ Rs. 7758170/- **Lowest Quoted Rates**, on Estimate (Rupees Seventy Seven Lacs, Fifty Eight Thousand One Hundred, Seventy) Only

Part-B @ Rs. 327842/- **0.22% Below**, on Estimate (Rupees Three Lac, Twenty Seven Thousand, Eight Hundred Forty Two) Only

Imtiaz Ahmed
ASSISTANT ENGINEER
PUBLIC HEALTH ENGINEERING
SUB-DIVISION JACOBABAD

Abdul Rehman Mangi
(ABDUL REHMAN MANGI)
ASSISTANT ENGINEER
EDUCATION WORKS SUB-DIVISION
JACOBABAD

Altaf Hussain Bhurgri
(ALTAF HUSSAIN BHURGRI)
EXECUTIVE ENGINEER
EDUCATION WORKS DIVISION
JACOBABAD

BID EVALUATION REPORT

1	Name of Procuring Agency	Executive Engineer Education Works Division Jacobabad
2	Tender Reference No.	NIT No. 1925 dated: 21.02.2018
3	Tender Description / Name of Work / Item	Rehabilitaion / Expansion of High Priority 4560-Schools @ District Jacobabad. (Primary & Elemt: Schools) at GBPS- Mengal Brohi, GBPS-Sabzal khoso, GGLSS - FAIMLY LINE, GBPS-Hamid Khan Lashari, GBPS-Haji Akhtar Hussain Khoso, GBPS Muhammad Umar Soomro, GGPS-Gulab Machhi TALUKA Jacobabad (Package No. 6)
4	Method of Procurement	Single Stage - One envelope procedure
5	Tender Published	News Papers & on SPPRA Website
6	Total bid documents Sold:	03 Nos
7	Total Bids Received	03 Nos
8	Technical Bid Opening Date (if applicable)	Not Applicables
9	No. of bid technically qualified (if applicable)	Not Applicable
10	Bids(s) Rejected	-
11	Financial Bid Opening Date	13.03.2018
13	Bid Evaluation Report	

S.No.	Name of Firm or Bidder	Name of Work	Ranking in Terms of cost	Ranking in Terms of cost	Comparison with Estimated Cost (if any)	Reasons for acceptance / Rejection	Remarks
1	M/s. Zulfiqar Ali Buriro	GGLSS - RAILWAY COLONY	3775823	1st	0.10% Below	Lowest	Recommended for award of work
		GGPS - HAJI LAKHMIR	7220729				
		GGPS - QADIR PUR - II (CMS)	5122065				
		GBPS - SHAIKH ABDUL HAKIM	9242813				
		GBPS - SOOFI PAHALWAN FAQIR	6162642				
		GBPS-Altat Pechuho	2968158				
		GBPS Akil Pur	4503742				
		38995972					
2	M/s. Abdul Khalique Dayo	GGLSS - RAILWAY COLONY	3798514	2nd	0.20% Above	Higher	Responsive
		GGPS - HAJI LAKHMIR	7264123				
		GGPS - QADIR PUR - II (CMS)	5152847				
		GBPS - SHAIKH ABDUL HAKIM	9263536				
		GBPS - SOOFI PAHALWAN FAQIR	6175630				
		GBPS-Altat Pechuho	2985995				
		GBPS Akil Pur	4548718				
		39189363					
3	M/s. Muhammad Anwar Brohi	GGLSS - RAILWAY COLONY	3817423	3rd	0.50% Above	Highest	Responsive
		GGPS - HAJI LAKHMIR	7268680				
		GGPS - QADIR PUR - II (CMS)	5163878				
		GBPS - SHAIKH ABDUL HAKIM	9344644				
		GBPS - SOOFI PAHALWAN FAQIR	6191407				
		GBPS-Altat Pechuho	2995502				
		GBPS Akil Pur	4573424				
		39354958					

(Signature)
 ASSISTANT ENGINEER
 PUBLIC HEALTH ENGINEERING
 SUB-DIVISION JACOBABAD

(Signature)
 (ABDUL REHMAN MANGI)
 ASSISTANT ENGINEER
 EDUCATION WORKS SUB-DIVISION
 JACOBABAD




(Signature)
 (ALTAF HUSSAIN BHURGRI)
 EXECUTIVE ENGINEER
 EDUCATION WORKS DIVISION
 JACOBABAD


**ATTENDANCE SHEET OF PARTICIPATION IN
TENDER PROCESS IN EDUCATION WORKS DIVISION JACOBABAD**


Name of Work :-


Rehabilitaion / Expansion of High Priority 4560-Schools @ District Jacobabad. (Primary & Elemt: Schools) at GBPS-Mengal Brohi, GBPS-Sabzal khoso, GGLSS - FAIMLY LINE, GBPS-Hamid Khan Lashari, GBPS- Haji Akhtar Hussain Khoso, GBPS Muhammad Umar Soomro, GGPS-Gulab Machhi TALUKA Jacobabad (Package No. 6)

Executive Engineer Education Works Division JACOBABAD held on 13.03.2018

Sr. No	Name of Contractor / Firm	Signature
1	M/s. Zulfiqar Ali Buriro	
2	M/s. Abdul Khalique Dayo	
3	M/s. Asif Ali Mugheri	


ASSISTANT ENGINEER
PUBLIC HEALTH ENGINEERING
SUB-DIVISION JACOBABAD


(ABDUL REHMAN MANGI)
ASSISTANT ENGINEER
EDUCATION WORKS SUB-DIVISION
JACOBABAD


(ALTAF HUSSAIN BHURGRI)
EXECUTIVE ENGINEER
EDUCATION WORKS DIVISION
JACOBABAD

**OFFICE OF THE
EXECUTIVE ENGINEER EDUCATION WORKS DIVISION JACOBABAD**


COMPRATIVE STATEMENT


NIT NO. EE/EWD/TC/ 1925 DATED: 21.02.2018


Name of Work :-

Rehabilitaion / Expansion of High Priority 4560-Schools @ District Jacobabad. (Primary & Elemt: Schools) at GBPS-Mengal Brohi, GBPS-Sabzal khoso, GGLSS - FAIMLY LINE, GBPS-Hamid Khan Lashari, GBPS- Haji Akhtar Hussain Khoso, GBPS Muhammad Umar Soomro, GGPS-Gulab Machhi TALUKA Jacobabad (Package No. 6)

Sr. No	Name of Contractor	Rate Quoted	
1	M/s. Zulfiqar Ali Buriro	i) 10.20% Above ii) 5065879/- iii) 0.25% Below	(Part-A Schedule) (Part-A Non Schedule) (Part-B Schedule)
2	M/s. Abdul Khaliq Dayo	i) 10.80% Above ii) 5075879/- iii) At Par	(Part-A Schedule) (Part-A Non Schedule) (Part-B Schedule)
3	M/s. Asif Ali Mugheri	i) 11.30% Above ii) 5080879/- iii) 1.90% Above	(Part-A Schedule) (Part-A Non Schedule) (Part-B Schedule)


ASSISTANT ENGINEER
PUBLIC HEALTH ENGINEERING
SUB-DIVISION JACOBABAD


(ABDUL REHMAN MANGI)
ASSISTANT ENGINEER
EDUCATION WORKS SUB-DIVISION
JACOBABAD



(ALTAF HUSSAIN BHURGRI)
EXECUTIVE ENGINEER
EDUCATION WORKS DIVISION
JACOBABAD


GENERAL ABSTRACT


Name of Work :-

Rehabilitaion / Expansion of High Priority 4560-Schools @ District Jacobabad. (Primary & Elemt: Schools) at GBPS-Mengal Brohi, GBPS-Sabzal khoso, GGLSS - FAIMLY LINE, GBPS-Hamid Khan Lashari, GBPS- Haji Akhtar Hussain Khoso, GBPS Muhammad Umar Soomro, GGPS-Gulab Machhi TALUKA Jacobabad (Package No. 6)

Sr. No	Name of Contractor / Firm	Tender Amount
1	M/s. Zulfiqar Ali Buriro	38995972
2	M/s. Abdul Khaliq Dayo	39189363
3	M/s. Asif Ali Mugheri	39354958


ASSISTANT ENGINEER
PUBLIC HEALTH ENGINEERING
SUB-DIVISION JACOBABAD


(ABDUL REHMAN MANGI)
ASSISTANT ENGINEER
EDUCATION WORKS SUB-DIVISION
JACOBABAD


(ALTAF HUSSAIN BHURGRI)
EXECUTIVE ENGINEER
EDUCATION WORKS DIVISION
JACOBABAD


Name of Work :-


Rehabilitaion / Expansion of High Priority 4560-Schools @ District Jacobabad. (Primary & Elemt: Schools) at GBPS-Mengal Brohi, GBPS-Sabzal khoso, GGLSS - FAIMLY LINE, GBPS-Hamid Khan Lashari, GBPS- Haji Akhtar Hussain Khoso, GBPS Muhammad Umar Soomro, GGPS-Gulab Machhi TALUKA Jacobabad (Package No. 6)

SUMMARY OF COST

Sr. No	Item of Work	Schedule B Amount	Contractor Rate	Amount
1	Civil Schedule Items	34128870	i) 10.20% Above	33472020
3	Non Schedule Items	5065879	ii) 5065879/-	5065879
3	W/S & S/F	459221	iii) 0.25% Below	458073

Total Amount of Bid
A + B + C = 38995972


4.5.24/2024
ASSISTANT ENGINEER
PUBLIC HEALTH ENGINEERING
SUB-DIVISION JACOBABAD


(ABDUL REHMAN MANGI)
ASSISTANT ENGINEER
EDUCATION WORKS SUB-DIVISION
JACOBABAD



(ALTAF HUSSAIN BHURGRI)
EXECUTIVE ENGINEER
EDUCATION WORKS DIVISION
JACOBABAD


BIDDER QUALIFICATION REPORT


NIT NO. EE/EWD/TC/ 1925 DATED: 21.02.2018

EDUCATION WORKS DIVISION JACOBABAD

1	Name of Procuring Agency	<u>Executive Engineer Education Works Division JACOBABAD</u>
2	Tender Reference No.	<u>NIT No. 1925, dated: 21.02.2018</u>
3	Tender Description / Name of Work / Item	<u>Rehabilitaion / Expansion of High Priority 4560-Schools @ District Jacobabad. (Primary & Elemt: Schools) at GBPS- Mengal Brohi, GBPS-Sabzal khoso, GGLSS - FAIMLY LINE, GBPS-Hamid Khan Lashari, GBPS-Haji Akhtar Hussain Khoso, GBPS Muhammad Umar Soomro, GGPS-Gulab Machhi TALUKA Jacobabad (Package No. 6)</u>
4	Method of Procurement	<u>Single Stage - One envelope procedure</u>
5	Tender Published	<u>News Papers & on SPPRA Website</u>
6	N.T.N	<u>Available</u>
7	Registration with P.E.C	<u>Registered</u>
8	Sindh Board of Revenue	<u>Registered</u>
9	Relevant Experience	<u>Available</u>
10	Turnover of at least last three years	<u>Available</u>
11	Funds / Budget	<u>Available</u>
12	05% Earnest Money	<u>Available</u>
13	Tender Fee / Cost Bidding Document	<u>Deposited</u>


ASSISTANT ENGINEER
PUBLIC HEALTH ENGINEERING
SUB-DIVISION JACOBABAD


(ABDUL REHMAN MANGI)
ASSISTANT ENGINEER
EDUCATION WORKS SUB-DIVISION
JACOBABAD


(ALTAF HUSSAIN BHURGRI)
EXECUTIVE ENGINEER
EDUCATION WORKS DIVISION
JACOBABAD

Method and procedure of procurement: NATIONAL COMPETITIVE BIDDING (SINGLE STAGE-ONE ENVELOPE).

MINUTES OF BID OPENING MEETING


A meeting of the procurement committee of this department was held on dated: 13.03.2018. for opening the bids received in respect of subject NIT till the deadlines of submission. The meeting was attended by all following members of the procurement committee and the representative of bidders. (Attendance sheet is enclosed).

The bids were opened at **2:00 PM** in the presence of the above mentioned participants and the rates quoted by bidders were read aloud and encircled by Chairman of the Procurement Committee. All the members of the procurement committee signed each and every page of financial proposal/bids. The bids do not contain any over-writing or cutting. (Also mention cutting or over writing if any). Following is the details of bids announced.


The committee shall examine all the bids as per the Qualification/ eligibility criteria provided in the bidding documents, arithmetical checks and verify the documents and bid security submitted by the bidders.

The meeting ended with the note of thanks to and from the chair.


(MEMBER)


ASSISTANT ENGINEER
PUBLIC HEALTH ENGINEERING
SUB-DIVISION JACOBABAD

(MEMBER)


(ABDUL REHMAN MANGI)
ASSISTANT ENGINEER
EDUCATION WORKS SUB-DIVISION
JACOBABAD

(CHAIRMAN)


(ALTAF HUSSAIN BHURGRI)
EXECUTIVE ENGINEER
EDUCATION WORKS DIVISION
JACOBABAD

FINANCIAL REVIEW

NAME OF WORK:-

Rehabilitation / Expansion of High Priority 4560-Schools @ District Jacobabad. (Primary & Element: Schools) at GBPS- Mengal Brohi, GBPS- Sabzal Khoso, GGLSS - FAIMLY LINE, GBPS-Hamid Khan Lashari, GBPS- Haji Akhtar Hussain Khoso, GBPS Muhammad Umar Soomro, GGPS-Gulab Machhi TALUKA Jacobabad (Package No. 6)

S #	Description	Estimated Cost	M/s. Zulfiqar Ali Buriro		M/s. Abdul Khaliq Dayo		M/s. Asif Ali Mugheri	
			Rate	Amount	Rate	Amount	Rate	Amount
1	2	3	4	5	6	7	8	9

PART-A CIVIL SCHEDULE ITEMS

1	Schedule Items	30,373,884		30,373,884		30,373,884		30,373,884
2	Carriage of Material	3,147,508	i) 10.20% Above	3,098,136	i) 10.80% Above	3,280,379	i) 11.30% Above	3,432,249
3	Contingency	607,478						
4	Total Part-A	34,128,870		33,472,020		33,654,263		33,806,133

PART-A NON SCHEDULE

1	Non Schedule Items	5,065,879		5,065,879		5,075,879		5,080,879
2	Total Part-C	5,065,879		5,065,879		5,075,879		5,080,879

PART-B W/S & S/F

1	Schedule Items	459,221		459,221		459,221		459,221
2			iii) 0.25% Below	1,148	iii) At Par		iii) 1.90% Above	8,725
3	Total Part-B	459,221		458,073		459,221		467,946
4	Total Part-A+B+C	39,653,970		38,995,972		39,189,363		39,354,958

The Lowest rate quoted by M/s. Zulfiqar Ali Buriro Government Contractor are :

Part-A @ Rs. 33472020/- **10.20% Above** on Estimate (Rupees Three Crore, Thirty Four Lacs,
Seventy Two Thousand, Twenty) Only

Part-A @ Rs. 5065879/- **Lowest Quoted Rates**, on Estimate (Rupees Fifty Lacs, Sixty Five Thousand,
Eight Hundred, Seventy Nine) Only

Part-B @ Rs. 458073/- **0.25% Below**, on Estimate (Rupees Four Lac, Fifty Eight Thousand,
Seventy Three) Only

ASSISTANT ENGINEER
PUBLIC HEALTH ENGINEERING
SUB-DIVISION JACOBABAD


ASSISTANT ENGINEER
EDUCATION WORKS SUB-DIVISION
JACOBABAD


EXECUTIVE ENGINEER
EDUCATION WORKS DIVISION
JACOBABAD


BID EVALUATION REPORT

1	Name of Procuring Agency	Executive Engineer Education Works Division Jacobabad
2	Tender Reference No.	NIT No. 1925 dated: 21.02.2018
3	Tender Description / Name of Work / Item	Rehabilitaion / Expansion of High Priority 4560-Schools @ District Jacobabad. (Primary & Elemt: Schools) at GBPS - QAZI SARWER BUX DAYO, GBPS - RAIS MUHAMMAD ANWER DAYO, GBPS - LAL BHATTI, GBPS - ABDUL QADIR SHAH, GBPS - BAHADUR PUR TALUKA Thul (Package No. 15)
4	Method of Procurement	Single Stage - One envelope procedure
5	Tender Published	News Papers & on SPPRA Website
6	Total bid documents Sold:	03 Nos
7	Total Bids Received	03 Nos
8	Technical Bid Opening Date (if applicable)	Not Applicables
9	No. of bid technically qualified (if applicable)	Not Applicable
10	Bids(s) Rejected	-
11	Financial Bid Opening Date	13.03.2018
13	Bid Evaluation Report	

S.No.	Name of Firm or Bidder	Name of Work	Ranking in Terms of cost	Ranking in Terms of cost	Comparison with Estimated Cost (if any)	Reasons for acceptance / Rejection	Remarks
1	M/s. Zulfiqar Ali Buriro	GBPS - QAZI SARWER BUX DAYO	7632098	1st	0.10% Below	Lowest	Recommended for award of work
		GBPS - RAIS MUHAMMAD ANWER	6680638				
		GBPS - LAL BHATTI	5511948				
		GBPS - ABDUL QADIR SHAH	5115845				
		GBPS - BAHADUR PUR	14704780				
		39645309					
2	M/s. Abdul Khaliq Dayo	GBPS - QAZI SARWER BUX DAYO	7655017	2nd	0.20% Above	Higher	Responsive
		GBPS - RAIS MUHAMMAD ANWER	6747303				
		GBPS - LAL BHATTI	5364955				
		GBPS - ABDUL QADIR SHAH	5166896				
		GBPS - BAHADUR PUR	14810108				
		39744279					
3	M/s. Muhammad Anwar Brohi	GBPS - QAZI SARWER BUX DAYO	7677937	3rd	0.50% Above	Highest	Responsive
		GBPS - RAIS MUHAMMAD ANWER	6767505				
		GBPS - LAL BHATTI	5381018				
		GBPS - ABDUL QADIR SHAH	5182365				
		GBPS - BAHADUR PUR	14834649				
		39843474					


 ASSISTANT ENGINEER
 PUBLIC HEALTH ENGINEERING
 SUB-DIVISION JACOBABAD





 (ABDUL REHMAN MANGI)
 ASSISTANT ENGINEER
 EDUCATION WORKS SUB-DIVISION
 JACOBABAD



 (ALTAH HUSSAIN BHURGRI)
 EXECUTIVE ENGINEER
 EDUCATION WORKS DIVISION
 JACOBABAD


**ATTENDANCE SHEET OF PARTICIPATION IN
TENDER PROCESS IN EDUCATION WORKS DIVISION JACOBABAD**

Name of Work :- **Rehabilitaion / Expansion of High Priority 4560-Schools @ District Jacobabad. (Primary & Elemt: Schools) at GBPS - QAZI SARWER BUX DAYO, GBPS - RAIS MUHAMMAD ANWER DAYO, GBPS - LAL BHATTI, GBPS - ABDUL QADIR SHAH, GBPS - BAHADUR PUR TALUKA Thul (Package No. 15)**

Executive Engineer Education Works Division JACOBABAD held on 13.03.2018

Sr. No	Name of Contractor / Firm	Signature
1	M/s. Zulfiqar Ali Buriro	
2	M/s. Abdul Khalique Dayo	
3	M/s. Muhammad Anwar Brohi	


ASSISTANT ENGINEER
PUBLIC HEALTH ENGINEERING
SUB-DIVISION JACOBABAD


(ABDUL REHMAN MANGI)
ASSISTANT ENGINEER
EDUCATION WORKS SUB-DIVISION
JACOBABAD


(ALTAF HUSSAIN BHURGRI)
EXECUTIVE ENGINEER
EDUCATION WORKS DIVISION
JACOBABAD

**OFFICE OF THE
EXECUTIVE ENGINEER EDUCATION WORKS DIVISION JACOBABAD**


COMPRATIVE STATEMENT


NIT NO. EE/EWD/TC/ 1925 DATED: 21.02.2018


Name of Work :-

**Rehabilitaion / Expansion of High Priority 4560-Schools @
District Jacobabad. (Primary & Elemt: Schools) at GBPS -
QAZI SARWER BUX DAYO, GBPS - RAIS MUHAMMAD
ANWER DAYO, GBPS - LAL BHATTI, GBPS - ABDUL QADIR
SHAH, GBPS - BAHADUR PUR TALUKA Thul (Package No.
15)**

Sr. No	Name of Contractor	Rate Quoted	
1	M/s. Zulfiqar Ali Buriro	i) 10.65% Above ii) 6753947/- iii) 0.22% Below	(Part-A Schedule) (Part-A Non Schedule) (Part-B Schedule)
2	M/s. Abdul Khaliq Dayo	i) 10.95% Above ii) 6763947/- iii) At Par	(Part-A Schedule) (Part-A Non Schedule) (Part-B Schedule)
3	M/s. Muhammad Anwar Brohi	i) 11.25% Above ii) 6768947/- iii) 1.50% Above	(Part-A Schedule) (Part-A Non Schedule) (Part-B Schedule)


**ASSISTANT ENGINEER
PUBLIC HEALTH ENGINEERING
SUB-DIVISION JACOBABAD**


**(ABDUL REHMAN MANGI)
ASSISTANT ENGINEER
EDUCATION WORKS SUB-DIVISION
JACOBABAD**



**(ALTAF HUSSAIN BHURGRI)
EXECUTIVE ENGINEER
EDUCATION WORKS DIVISION
JACOBABAD**


GENERAL ABSTRACT


Name of Work :-

Rehabilitaion / Expansion of High Priority 4560-Schools @ District Jacobabad. (Primary & Elemt: Schools) at GBPS - QAZI SARWER BUX DAYO, GBPS - RAIS MUHAMMAD ANWER DAYO, GBPS - LAL BHATTI, GBPS - ABDUL QADIR SHAH, GBPS - BAHADUR PUR TALUKA Thul (Package No. 15)

Sr. No	Name of Contractor / Firm	Tender Amount
1	M/s. Zulfiqar Ali Buriro	39645309
2	M/s. Abdul Khaliq Dayo	39344279
3	M/s. Muhammad Anwar Brohi	39443474


ASSISTANT ENGINEER
PUBLIC HEALTH ENGINEERING
SUB-DIVISION JACOBABAD


(ABDUL REHMAN MANGI)
ASSISTANT ENGINEER
EDUCATION WORKS SUB-DIVISION
JACOBABAD


(ALTAF HUSSAIN BHURGRI)
EXECUTIVE ENGINEER
EDUCATION WORKS DIVISION
JACOBABAD

Name of Work :-


Rehabilitaion / Expansion of High Priority 4560-Schools @ District Jacobabad. (Primary & Elemt: Schools) at GBPS - QAZI SARWER BUX DAYO, GBPS - RAIS MUHAMMAD ANWER DAYO, GBPS - LAL BHATTI, GBPS - ABDUL QADIR SHAH, GBPS - BAHADUR PUR TALUKA Thul (Package No. 15)

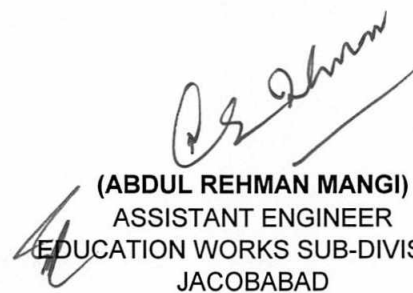
SUMMARY OF COST


Sr. No	Item of Work	Schedule B Amount	Contractor Rate	Amount
1	Civil Schedule Items	32514130	i) 10.65% Above	32484095
3	Non Schedule Items	6753947	ii) 6753947/-	6753947
3	W/S & S/F	408165	iii) 0.22% Below	407267

Total Amount of Bid

A + B + C = 39645309


ASSISTANT ENGINEER
PUBLIC HEALTH ENGINEERING
SUB-DIVISION JACOBABAD


(ABDUL REHMAN MANGI)
ASSISTANT ENGINEER
EDUCATION WORKS SUB-DIVISION
JACOBABAD



(ALTAF HUSSAIN BHURGRI)
EXECUTIVE ENGINEER
EDUCATION WORKS DIVISION
JACOBABAD


BIDDER QUALIFICATION REPORT


NIT NO. EE/EWD/TC/ 1925 DATED: 21.02.2018

EDUCATION WORKS DIVISION JACOBABAD

1 Name of Procuring Agency	<u>Executive Engineer Education Works Division JACOBABAD</u>
2 Tender Reference No.	<u>NIT No. 1925, dated: 21.02.2018</u>
3 Tender Description / Name of Work / Item	<u>Rehabilitaion / Expansion of High Priority 4560-Schools @ District Jacobabad. (Primary & Elemt: Schools) at GBPS - QAZI SARWER BUX DAYO, GBPS - RAIS MUHAMMAD ANWER DAYO, GBPS - LAL BHATTI, GBPS - ABDUL QADIR SHAH, GBPS - BAHADUR PUR TALUKA Thui (Package No. 15)</u>
4 Method of Procurement	<u>Single Stage - One envelope procedure</u>
5 Tender Published	<u>News Papers & on SPPRA Website</u>
6 N.T.N	<u>Available</u>
7 Registration with P.E.C	<u>Registered</u>
8 Sindh Board of Revenue	<u>Registered</u>
9 Relevant Experience	<u>Available</u>
10 Turnover of at least last three years	<u>Available</u>
11 Funds / Budget	<u>Available</u>
12 05% Earnest Money	<u>Available</u>
13 Tender Fee / Cost Bidding Document	<u>Deposited</u>


ASSISTANT ENGINEER
PUBLIC HEALTH ENGINEERING
SUB-DIVISION JACOBABAD


(ABDUL REHMAN MANGI)
ASSISTANT ENGINEER
EDUCATION WORKS SUB-DIVISION
JACOBABAD


(ALTAF HUSSAIN BHURGRI)
EXECUTIVE ENGINEER
EDUCATION WORKS DIVISION
JACOBABAD

Method and procedure of procurement: NATIONAL COMPETITIVE BIDDING (SINGLE STAGE-ONE ENVELOPE).

MINUTES OF BID OPENING MEETING


A meeting of the procurement committee of this department was held on dated: 13.03.2018. for opening the bids received in respect of subject NIT till the deadlines of submission. The meeting was attended by all following members of the procurement committee and the representative of bidders. (Attendance sheet is enclosed).

The bids were opened at **2:00 PM** in the presence of the above mentioned participants and the rates quoted by bidders were read aloud and encircled by Chairman of the Procurement Committee. All the members of the procurement committee signed each and every page of financial proposal/bids. The bids do not contain any over-writing or cutting. (Also mention cutting or over writing if any). Following is the details of bids announced.


The committee shall examine all the bids as per the Qualification/ eligibility criteria provided in the bidding documents, arithmetical checks and verify the documents and bid security submitted by the bidders.

The meeting ended with the note of thanks to and from the chair.


(MEMBER)


ASSISTANT ENGINEER
PUBLIC HEALTH ENGINEERING
SUB-DIVISION JACOBABAD

(MEMBER)


(ABDUL REHMAN MANGI)
ASSISTANT ENGINEER
EDUCATION WORKS SUB-DIVISION
JACOBABAD

(CHAIRMAN)


(ALTAF HUSSAIN BHURGRI)
EXECUTIVE ENGINEER
EDUCATION WORKS DIVISION
JACOBABAD

FINANCIAL REVIEW

NAME OF WORK:-

Rehabilitation / Expansion of High Priority 4560-Schools @ District Jacobabad. (Primary & Element: Schools) at GBPS - QAZI SARWER BUX DAYO, GBPS - RAIS MUHAMMAD ANWER DAYO, GBPS - LAL BHATTI, GBPS - ABDUL QADIR SHAH, GBPS - BAHADUR PUR TALUKA Thul (Package No. 15)

S #	Description	Estimated Cost	M/s. Zulfiqar Ali Buriro		M/s. Abdul Khaliq Dayo		M/s. Muhammad Anwar Brohi	
			Rate	Amount	Rate	Amount	Rate	Amount
1	2	3	4	5	6	7	8	9

PART-A CIVIL SCHEDULE ITEMS

1	Schedule Items	29,357,519		29,357,519		29,357,519		29,357,519
2	Carriage of Material	3,156,611	i) 10.65% Above	3,126,576	j) 10.95% Above	3,214,648	i) 11.25% Above	3,302,721
3	Contingency							
4	Total Part-A	32,514,130		32,484,095		32,572,167		32,660,240

PART-A NON SCHEDULE

1	Non Schedule Items	6,753,947		6,753,947		6,363,947		6,368,947
2	Total Part-C	6,753,947		6,753,947		6,363,947		6,368,947

PART-B W/S & S/F

1	Schedule Items	408,165		408,165		408,165		408,165
2			iii) 0.22% Below	898	iii) At Par		iii) 1.50% Above	6,122
3	Total Part-B	408,165		407,267		408,165		414,287
4	Total Part-A+B+C	39,676,242		39,645,309		39,344,279		39,443,474
	A) Total Cost as per Estimate	39,676,242	The Lowest rate quoted by M/s. Zulfiqar Ali Buriro Government Contractor are :					
	B) Total Cost as per Tender	39,645,309	Part-A @ Rs. 32484095/- 10.65% Above on Estimate (Rupees Three Crore, Twenty Four Lacs, Eighty Four Thousand, Ninety Five) Only					
	Saving A-B	30,933	Part-A @ Rs. 6753947/- Lowest Quoted Rates, on Estimate (Rupees Sixty Seven Lacs, Fifty Three Thousand, Nine Hundred, Forty Seven) Only					
	Percentage Saving	0.08%	Part-B @ Rs. 407267/- 0.22% Below, on Estimate (Rupees Four Lac, Seven Thousand, Two Hundred, Sixty Seven) Only					
	A.A Amount	-						
	Lowest Tender Amount	39,645,309						
	Saving Over A.A	-						

Signature
 ASSISTANT ENGINEER
 PUBLIC HEALTH ENGINEERING
 SUB-DIVISION JACOBABAD

Signature
 (ABDUL REHMAN MANGI)
 ASSISTANT ENGINEER
 EDUCATION WORKS SUB-DIVISION
 JACOBABAD

Signature
 (AL TAF HUSSAIN BHURGRI)
 EXECUTIVE ENGINEER
 EDUCATION WORKS DIVISION
 JACOBABAD

BID EVALUATION REPORT

1 Name of Procuring Agency	Executive Engineer Education Works Division Jacobabad
2 Tender Reference No.	NIT No. 1925 dated: 21.02.2018
3 Tender Description / Name of Work / Item	Rehabilitaion / Expansion of High Priority 4560-Schools @ District Jacobabad. (Primary & Elemt: Schools) at GBPS - MIRPUR BURIRO (SINDHI), GGPS - THULL - II, GBPS - BAHOO KHOSO, GBPS - MUHAMMAD SIDDIQUE, GGPS - QADIR DAD NOONARI TALUKA Thul (Package No. 16)
4 Method of Procurement	Single Stage - One envelope procedure
5 Tender Published	News Papers & on SPPRA Website
6 Total bid documents Sold:	03 Nos
7 Total Bids Received	03 Nos
8 Technical Bid Opening Date (if applicable)	Not Applicables
9 No. of bid technically qualified (if applicable)	Not Applicable
10 Bids(s) Rejected	-
11 Financial Bid Opening Date	13.03.2018
13 Bid Evaluation Report	

S.No.	Name of Firm or Bidder	Name of Work	Ranking in Terms of cost	Ranking in Terms of cost	Comparison with Estimated Cost (if any)	Reasons for acceptance / Rejection	Remarks	
1	M/s. Zulfiqar Ali Buriro	GBPS - MIRPUR BURIRO (SINDHI)	11329916	1st	0.16% Below	Lowest	Recommended for award of work	
		GGPS - THULL - II	7856115					
		GBPS - BAHOO KHOSO	6739735					
		GBPS - MUHAMMAD SIDDIQUE	8979028					
		GGPS - QADIR DAD NOONARI	5327151					
			40231945					
2	M/s. Abdul Khaliq Dayo	GBPS - MIRPUR BURIRO (SINDHI)	11384386	2nd	0.32% Above	Higher	Responsive	
		GGPS - THULL - II	7893864					
		GBPS - BAHOO KHOSO	6772137					
		GBPS - MUHAMMAD SIDDIQUE	9022196					
		GGPS - QADIR DAD NOONARI	5310815					
			40383398					
3	M/s. Din Muhammad Enterprises	GBPS - MIRPUR BURIRO (SINDHI)	11475171	3rd	1.12% Above	Highest	Responsive	
		GGPS - THULL - II	7956834					
		GBPS - BAHOO KHOSO	6826142					
		GBPS - MUHAMMAD SIDDIQUE	8999795					
		GGPS - QADIR DAD NOONARI	5380706					
			40638648					

(Signature)
 ASSISTANT ENGINEER
 PUBLIC HEALTH ENGINEERING
 SUB-DIVISION JACOBABAD

(Signature)
 (ABDUL REHMAN MANGI)
 ASSISTANT ENGINEER
 EDUCATION WORKS SUB-DIVISION
 JACOBABAD




(Signature)
 (ALTAF HUSSAIN BHURGRI)
 EXECUTIVE ENGINEER
 EDUCATION WORKS DIVISION
 JACOBABAD


**ATTENDANCE SHEET OF PARTICIPATION IN
TENDER PROCESS IN EDUCATION WORKS DIVISION JACOBABAD**


Name of Work :-


Rehabilitaion / Expansion of High Priority 4560-Schools @
District Jacobabad. (Primary & Elemt: Schools) at GBPS -
MIRPUR BURIRO (SINDHI), GGPS - THULL - II, GBPS -
BAHOO KHOSO, GBPS - MUHAMMAD SIDDIQUE, GGPS -
QADIR DAD NOONARI TALUKA Thul (Package No. 16)

Executive Engineer Education Works Division JACOBABAD held on 13.03.2018

Sr. No	Name of Contractor / Firm	Signature
1	M/s. Zulfiqar Ali Buriro	
2	M/s. Abdul Khaliq Dayo	
3	M/s. Din Muhammadf Enterprises	


ASSISTANT ENGINEER
PUBLIC HEALTH ENGINEERING
SUB-DIVISION JACOBABAD


(ABDUL REHMAN MANGI)
ASSISTANT ENGINEER
EDUCATION WORKS SUB-DIVISION
JACOBABAD


(ALTAF HUSSAIN BHURGRI)
EXECUTIVE ENGINEER
EDUCATION WORKS DIVISION
JACOBABAD

**OFFICE OF THE
EXECUTIVE ENGINEER EDUCATION WORKS DIVISION JACOBABAD**


COMPRATIVE STATEMENT


NIT NO. EE/EWD/TC/ 1925 DATED: 21.02.2018


Name of Work :-

**Rehabilitaion / Expansion of High Priority 4560-Schools @
District Jacobabad. (Primary & Elemt: Schools) at GBPS -
MIRPUR BURIRO (SINDHI), GGPS - THULL - II, GBPS -
BAHOO KHOSO, GBPS - MUHAMMAD SIDDIQUE, GGPS -
QADIR DAD NOONARI TALUKA Thul (Package No. 16)**

Sr. No	Name of Contractor	Rate Quoted	
1	M/s. Zulfiqar Ali Buriro	i) 10.72% Above ii) 6199691/- iii) 0.10% Below	(Part-A Schedule) (Part-A Non Schedule) (Part-B Schedule)
2	M/s. Abdul Khaliq Dayo	i) 11.20% Above ii) 6204691/- iii) At Par	(Part-A Schedule) (Part-A Non Schedule) (Part-B Schedule)
3	M/s. Din Muhammadf Enterprises	i) 12.0% Above ii) 6210691/- iii) 1.75% Above	(Part-A Schedule) (Part-A Non Schedule) (Part-B Schedule)


**ASSISTANT ENGINEER
PUBLIC HEALTH ENGINEERING
SUB-DIVISION JACOBABAD**


**(ABDUL REHMAN MANGI)
ASSISTANT ENGINEER
EDUCATION WORKS SUB-DIVISION
JACOBABAD**



**(ALTAH HUSSAIN BHURGRI)
EXECUTIVE ENGINEER
EDUCATION WORKS DIVISION
JACOBABAD**


GENERAL ABSTRACT


Name of Work :-

Rehabilitaion / Expansion of High Priority 4560-Schools @ District Jacobabad. (Primary & Elemt: Schools) at GBPS - MIRPUR BURIRO (SINDHI), GGPS - THULL - II, GBPS - BAHOO KHOSO, GBPS - MUHAMMAD SIDDIQUE, GGPS - QADIR DAD NOONARI TALUKA Thul (Package No. 16)

Sr. No	Name of Contractor / Firm	Tender Amount
1	M/s. Zulfiqar Ali Buriro	40231945
2	M/s. Abdul Khaliq Dayo	40383398
3	M/s. Din Muhammadf Enterprises	40638648


ASSISTANT ENGINEER
PUBLIC HEALTH ENGINEERING
SUB-DIVISION JACOBABAD


(ABDUL REHMAN MANGI)
ASSISTANT ENGINEER
EDUCATION WORKS SUB-DIVISION
JACOBABAD


(ALTAF HUSSAIN BHURGRI)
EXECUTIVE ENGINEER
EDUCATION WORKS DIVISION
JACOBABAD


Name of Work :-


Rehabilitaion / Expansion of High Priority 4560-Schools @ District Jacobabad. (Primary & Elemt: Schools) at GBPS - MIRPUR BURIRO (SINDHI), GGPS - THULL - II, GBPS - BAHOO KHOSO, GBPS - MUHAMMAD SIDDIQUE, GGPS - QADIR DAD NOONARI TALUKA Thul (Package No. 16)


SUMMARY OF COST

Sr. No	Item of Work	Schedule B Amount	Contractor Rate	Amount
1	Civil Schedule Items	33754568	i) 10.72% Above	33706560
3	Non Schedule Items	6199691	ii) 6199691/-	6199691
3	W/S & S/F	326020	iii) 0.10% Below	325694

Total Amount of Bid
A + B + C = 40231945


ASSISTANT ENGINEER
PUBLIC HEALTH ENGINEERING
SUB-DIVISION JACOBABAD


(ABDUL REHMAN MANGI)
ASSISTANT ENGINEER
EDUCATION WORKS SUB-DIVISION
JACOBABAD



(ALTAF HUSSAIN BHURGRI)
EXECUTIVE ENGINEER
EDUCATION WORKS DIVISION
JACOBABAD


BIDDER QUALIFICATION REPORT


NIT NO. EE/EWD/TC/ 1925 DATED: 21.02.2018

EDUCATION WORKS DIVISION JACOBABAD

1 Name of Procuring Agency	<u>Executive Engineer Education Works Division JACOBABAD</u>
2 Tender Reference No.	<u>NIT No. 1925, dated: 21.02.2018</u>
3 Tender Description / Name of Work / Item	<u>Rehabilitaion / Expansion of High Priority 4560-Schools @ District Jacobabad. (Primary & Elemt: Schools) at GBPS - MIRPUR BURIRO (SINDHI), GGPS - THULL - II, GBPS - BAHOO KHOSO, GBPS - MUHAMMAD SIDDIQUE, GGPS - QADIR DAD NOONARI TALUKA Thul (Package No. 16)</u>
4 Method of Procurement	<u>Single Stage - One envelope procedure</u>
5 Tender Published	<u>News Papers & on SPPRA Website</u>
6 N.T.N	<u>Available</u>
7 Registration with P.E.C	<u>Registered</u>
8 Sindh Board of Revenue	<u>Registered</u>
9 Relevant Experience	<u>Available</u>
10 Turnover of at least last three years	<u>Available</u>
11 Funds / Budget	<u>Available</u>
12 05% Earnest Money	<u>Available</u>
13 Tender Fee / Cost Bidding Document	<u>Deposited</u>


ASSISTANT ENGINEER
PUBLIC HEALTH ENGINEERING
SUB-DIVISION JACOBABAD


(ABDUL REHMAN MANGI)
ASSISTANT ENGINEER
EDUCATION WORKS SUB-DIVISION
JACOBABAD


(ALTAF HUSSAIN BHURGRI)
EXECUTIVE ENGINEER
EDUCATION WORKS DIVISION
JACOBABAD

Method and procedure of procurement: NATIONAL COMPETITIVE BIDDING (SINGLE STAGE-ONE ENVELOPE).

MINUTES OF BID OPENING MEETING


A meeting of the procurement committee of this department was held on dated: 13.03.2018. for opening the bids received in respect of subject NIT till the deadlines of submission. The meeting was attended by all following members of the procurement committee and the representative of bidders. (Attendance sheet is enclosed).

The bids were opened at **2:00 PM** in the presence of the above mentioned participants and the rates quoted by bidders were read aloud and encircled by Chairman of the Procurement Committee. All the members of the procurement committee signed each and every page of financial proposal/bids. The bids do not contain any overwriting or cutting. (Also mention cutting or over writing if any). Following is the details of bids announced.


The committee shall examine all the bids as per the Qualification/ eligibility criteria provided in the bidding documents, arithmetical checks and verify the documents and bid security submitted by the bidders.

The meeting ended with the note of thanks to and from the chair.


(MEMBER)


ASSISTANT ENGINEER
PUBLIC HEALTH ENGINEERING
SUB-DIVISION JACOBABAD

(MEMBER)


(ABDUL REHMAN MANGI)
ASSISTANT ENGINEER
EDUCATION WORKS SUB-DIVISION
JACOBABAD

(CHAIRMAN)


(ALTAF HUSSAIN BHURGRI)
EXECUTIVE ENGINEER
EDUCATION WORKS DIVISION
JACOBABAD

FINANCIAL REVIEW

NAME OF WORK:-

Rehabilitaion / Expansion of High Priority 4560-Schools @ District Jacobabad. (Primary & Elemt: Schools) at GBPS - MIRPUR BURIRO (SINDHI), GGPS - THULL - II, GBPS - BAHOO KHOSO, GBPS - MUHAMMAD SIDDIQUE, GGPS - QADIR DAD NOONARI TALUKA Thul (Package No. 16)

S #	Discription	Estimated Cost	M/s. Zulfiqar Ali Buriro		M/s. Abdul Khaliq Dayo		M/s. Din Muhammad Enterprises	
			Rate	Amount	Rate	Amount	Rate	Amount
1	2	3	4	5	6	7	8	9
PART-A CIVIL SCHEDULE ITEMS								
1	Schedule Items	30,443,064		30,443,064		30,443,064		30,443,064
2	Carriage of Material	3,311,504	i) 10.72% Above	3,263,496	i) 11.20% Above	3,409,623	i) 12.0% Above	3,653,168
3	Contingency							
4	Total Part-A	33,754,568		33,706,560		33,852,687		34,096,232
PART-A NON SCHEDULE								
1	Non Schedule Items	6,199,691		6,199,691		6,204,691		6,210,691
2	Total Part-C	6,199,691		6,199,691		6,204,691		6,210,691
PART-B W/S & S/F								
1	Schedule Items	326,020	iii) 0.10% Below	326,020	iii) At Par	326,020	iii) 1.75% Above	326,020
2				326				5,705
3	Total Part-B	326,020		325,694		326,020		331,725
4	Total Part-A+B+C	40,280,279		40,231,945		40,383,398		40,638,648
	A) Total Cost as per Estimate	40,280,279						
	B) Total Cost as per Tender	40,231,945						
	Saving A-B	48,334						
	Percentage Saving	0.12%						
	A.A Amount	-						
	Lowest Tender Amount	40,231,945						
	Saving Over A.A	-						

The Lowest rate quoted by M/s. Zulfiqar Ali Buriro Government Contractor are :
 Part-A @ Rs. 33706560/- 10.72% Above on Estimate (Rupees Three Crore, Thirty Seven Lacs, Six Thousand, Five Hundred, Sixty) Only
 Part-A @ Rs. 6199691/- Lowest Quoted Rates, on Estimate (Rupees Sixty One Lacs, Ninety Nine Thousand, Six Hundred, Ninety One) Only
 Part-B @ Rs. 325694/- 0.10% Below, on Estimate (Rupees Three Lac, Twenty Five Thousand, Six Hundred, Ninety Four) Only

Asst. Eng. Health
 ASSISTANT ENGINEER
 PUBLIC/HEALTH ENGINEERING
 SUB-DIVISION JACOBABAD


Abdul Rehman Mangi
 (ABDUL REHMAN MANGI)
 ASSISTANT ENGINEER
 EDUCATION WORKS SUB-DIVISION
 JACOBABAD


Altaf Hussain Bhurgri
 (ALTAF HUSSAIN BHURGRI)
 EXECUTIVE ENGINEER
 EDUCATION WORKS DIVISION
 JACOBABAD


BID EVALUATION REPORT

1	Name of Procuring Agency	Executive Engineer Education Works Division Jacobabad
2	Tender Reference No.	NIT No. 1925 dated: 21.02.2018
3	Tender Description / Name of Work / Item	Rehabilitaion / Expansion of High Priority 4560-Schools @ District Jacobabad. (Primary & Elemt: Schools) at GBPS - ABDUL QADIR KHOSO, GBPS - SACHAL KATTO, GBPS - GULSHER KHAN KANRANI, GBPS - UMED ALI BROHI, GBPS -Abdul Ghani Shah, GGPS -Madad pur TALUKA Thul (Package No. 19)
4	Method of Procurement	Single Stage - One envelope procedure
5	Tender Published	News Papers & on SPPRA Website
6	Total bid documents Sold:	03 Nos
7	Total Bids Received	03 Nos
8	Technical Bid Opening Date (if applicable)	Not Applicables
9	No. of bid technically qualified (if applicable)	Not Applicable
10	Bids(s) Rejected	-
11	Financial Bid Opening Date	13.03.2018
13	Bid Evaluation Report	

S.No.	Name of Firm or Bidder	Name of Work	Ranking in Terms of cost	Ranking in Terms of cost	Comparison with Estimated Cost (if any)	Reasons for acceptance / Rejection	Remarks
1	M/s. Bashir Ahmed Khoso	GBPS - ABDUL QADIR KHOSO	6202812	1st	0.15% Below	Lowest	Recomanded for award of work
		GBPS - SACHAL KATTO	5836836				
		GBPS - GULSHER KHAN KANRANI	5554696				
		GBPS - UMED ALI BROHI	6763242				
		GBPS -Abdul Ghani Shah	6344459				
		GGPS -Madad pur	6217027				
			36919072				
2	M/s. Gul Hassan Soomro	GBPS - ABDUL QADIR KHOSO	6224555	2nd	0.20% Above	Higher	Responsive
		GBPS - SACHAL KATTO	5857296				
		GBPS - GULSHER KHAN KANRANI	5574167				
		GBPS - UMED ALI BROHI	6786949				
		GBPS -Abdul Ghani Shah	6366697				
		GGPS -Madad pur	6167816				
			36977480				
3	M/s. Abdul Haque	GBPS - ABDUL QADIR KHOSO	6249403	3rd	0.60% Above	Highest	Responsive
		GBPS - SACHAL KATTO	5806281				
		GBPS - GULSHER KHAN KANRANI	5596419				
		GBPS - UMED ALI BROHI	6814043				
		GBPS -Abdul Ghani Shah	6392113				
		GGPS -Madad pur	6209620				
			37067879				


ASSISTANT ENGINEER
PUBLIC HEALTH ENGINEERING
SUB-DIVISION JACOBABAD





(ABDUL REHMAN MANGI)
ASSISTANT ENGINEER
EDUCATION WORKS SUB-DIVISION
JACOBABAD



(ALTAH HUSSAIN BHURGRI)
EXECUTIVE ENGINEER
EDUCATION WORKS DIVISION
JACOBABAD


**ATTENDANCE SHEET OF PARTICIPATION IN
TENDER PROCESS IN EDUCATION WORKS DIVISION JACOBABAD**

Name of Work :- **Rehabilitaion / Expansion of High Priority 4560-Schools @ District Jacobabad. (Primary & Elemt: Schools) at GBPS - ABDUL QADIR KHOSO, GBPS - SACHAL KATTO, GBPS - GULSHER KHAN KANRANI, GBPS - UMED ALI BROHI, GBPS -Abdul Ghani Shah, GGPS -Madad pur TALUKA Thul (Package No. 19)**

Executive Engineer Education Works Division JACOBABAD held on 13.03.2018

Sr. No	Name of Contractor / Firm	Signature
1	M/s. Bashir Ahmed Khoso	
2	M/s. Gul Hassan Soomro	
3	M/s. Abdul Haq	


ASSISTANT ENGINEER
PUBLIC HEALTH ENGINEERING
SUB-DIVISION JACOBABAD


(ABDUL REHMAN MANGI)
ASSISTANT ENGINEER
EDUCATION WORKS SUB-DIVISION
JACOBABAD


(ALTAF HUSSAIN BHURGRI)
EXECUTIVE ENGINEER
EDUCATION WORKS DIVISION
JACOBABAD

**OFFICE OF THE
EXECUTIVE ENGINEER EDUCATION WORKS DIVISION JACOBABAD**


COMPRATIVE STATEMENT


NIT NO. EE/EWD/TC/ 1925 DATED: 21.02.2018

Name of Work :-


**Rehabilitaion / Expansion of High Priority 4560-Schools @
District Jacobabad. (Primary & Elemt: Schools) at GBPS -
ABDUL QADIR KHOSO, GBPS - SACHAL KATTO, GBPS -
GULSHER KHAN KANRANI, GBPS - UMED ALI BROHI, GBPS
-Abdul Ghani Shah, GGPS -Madad pur TALUKA Thul
(Package No. 19)**

Sr. No	Name of Contractor	Rate Quoted	
1	M/s. Bashir Ahmed Khoso	i) 13.75% Above ii) 5590914/- iii) 0.12% Below	(Part-A Schedule) (Part-A Non Schedule) (Part-B Schedule)
2	M/s. Gul Hassan Soomro	i) 14.10% Above ii) 5593914/- iii) At Par	(Part-A Schedule) (Part-A Non Schedule) (Part-B Schedule)
3	M/s. Abdul Haq	i) 14.40% Above ii) 5598914/- iii) 1.0% Above	(Part-A Schedule) (Part-A Non Schedule) (Part-B Schedule)


ASSISTANT ENGINEER
PUBLIC HEALTH ENGINEERING
SUB-DIVISION JACOBABAD


(ABDUL REHMAN MANGI)
ASSISTANT ENGINEER
EDUCATION WORKS SUB-DIVISION
JACOBABAD

0.138979756
5590914



(ALTAF HUSSAIN BHURGRI)
EXECUTIVE ENGINEER
EDUCATION WORKS DIVISION
JACOBABAD


GENERAL ABSTRACT


Name of Work :-

Rehabilitaion / Expansion of High Priority 4560-Schools @ District Jacobabad. (Primary & Elemt: Schools) at GBPS - ABDUL QADIR KHOSO, GBPS - SACHAL KATTO, GBPS - GULSHER KHAN KANRANI, GBPS - UMED ALI BROHI, GBPS -Abdul Ghani Shah, GGPS -Madad pur TALUKA Thul (Package No. 19)

Sr. No	Name of Contractor / Firm	Tender Amount
1	M/s. Bashir Ahmed Khoso	36878942
2	M/s. Gul Hassan Soomro	36977480
3	M/s. Abdul Haq	37067879


ASSISTANT ENGINEER
PUBLIC HEALTH ENGINEERING
SUB-DIVISION JACOBABAD


(ABDUL REHMAN MANGI)
ASSISTANT ENGINEER
EDUCATION WORKS SUB-DIVISION
JACOBABAD


(ALTAF HUSSAIN BHURGRI)
EXECUTIVE ENGINEER
EDUCATION WORKS DIVISION
JACOBABAD

Name of Work :-


Rehabilitaion / Expansion of High Priority 4560-Schools @ District Jacobabad. (Primary & Elemt: Schools) at GBPS - ABDUL QADIR KHOSO, GBPS - SACHAL KATTO, GBPS - GULSHER KHAN KANRANI, GBPS - UMED ALI BROHI, GBPS - Abdul Ghani Shah, GGPS -Madad pur TALUKA Thul (Package No. 19)


SUMMARY OF COST

Sr. No	Item of Work	Schedule B Amount	Contractor Rate	Amount
1	Civil Schedule Items	30937467	i) 13.75% Above	30897273
3	Non Schedule Items	5590914	ii) 5590914/-	5590914
3	W/S & S/F	391224	iii) 0.12% Below	390755

Total Amount of Bid

A + B + C = 36878942


ASSISTANT ENGINEER
PUBLIC HEALTH ENGINEERING
SUB-DIVISION JACOBABAD


(ABDUL REHMAN MANGI)
ASSISTANT ENGINEER
EDUCATION WORKS SUB-DIVISION
JACOBABAD



(ALTAF HUSSAIN BHURGRI)
EXECUTIVE ENGINEER
EDUCATION WORKS DIVISION
JACOBABAD


BIDDER QUALIFICATION REPORT


NIT NO. EE/EWD/TC/ 1925 DATED: 21.02.2018

EDUCATION WORKS DIVISION JACOBABAD

1	Name of Procuring Agency	Executive Engineer Education Works Division JACOBABAD
2	Tender Reference No.	NIT No. 1925, dated: 21.02.2018
3	Tender Description / Name of Work / Item	Rehabilitaion / Expansion of High Priority 4560-Schools @ District Jacobabad. (Primary & Elemt: Schools) at GBPS - ABDUL QADIR KHOSO, GBPS - SACHAL KATTO, GBPS - GULSHER KHAN KANRANI, GBPS - UMED ALI BROHI, GBPS -Abdul Ghani Shah, GGPS -Madad pur TALUKA Thul (Package No. 19)
4	Method of Procurement	Single Stage - One envelope procedure
5	Tender Published	News Papers & on SPPRA Website
6	N.T.N	Available
7	Registration with P.E.C	Registered
8	Sindh Board of Revenue	Registered
9	Relevant Experience	Available
10	Turnover of at least last three years	Available
11	Funds / Budget	Available
12	05% Earnest Money	Available
13	Tender Fee / Cost Bidding Document	Deposited


ASSISTANT ENGINEER
PUBLIC HEALTH ENGINEERING
SUB-DIVISION JACOBABAD


(ABDUL REHMAN MANGI)
ASSISTANT ENGINEER
EDUCATION WORKS SUB-DIVISION
JACOBABAD


(ALTAF HUSSAIN BHURGRI)
EXECUTIVE ENGINEER
EDUCATION WORKS DIVISION
JACOBABAD

Method and procedure of procurement: NATIONAL COMPETITIVE BIDDING (SINGLE STAGE-ONE ENVELOPE).

MINUTES OF BID OPENING MEETING


A meeting of the procurement committee of this department was held on dated: 13.03.2018. for opening the bids received in respect of subject NIT till the deadlines of submission. The meeting was attended by all following members of the procurement committee and the representative of bidders. (Attendance sheet is enclosed).

The bids were opened at **2:00 PM** in the presence of the above mentioned participants and the rates quoted by bidders were read aloud and encircled by Chairman of the Procurement Committee. All the members of the procurement committee signed each and every page of financial proposal/bids. The bids do not contain any over-writing or cutting. (Also mention cutting or over writing if any). Following is the details of bids announced.


The committee shall examine all the bids as per the Qualification/ eligibility criteria provided in the bidding documents, arithmetical checks and verify the documents and bid security submitted by the bidders.

The meeting ended with the note of thanks to and from the chair.


(MEMBER)


ASSISTANT ENGINEER
PUBLIC HEALTH ENGINEERING
SUB-DIVISION JACOBABAD

(MEMBER)


(ABDUL REHMAN MANGI)
ASSISTANT ENGINEER
EDUCATION WORKS SUB-DIVISION
JACOBABAD

(CHAIRMAN)


(ALTAF HUSSAIN BHURGRI)
EXECUTIVE ENGINEER
EDUCATION WORKS DIVISION
JACOBABAD

FINANCIAL REVIEW

NAME OF WORK:-

Rehabilitation / Expansion of High Priority 4560-Schools @ District Jacobabad. (Primary & Elemt: Schools) at GBPS - ABDUL QADIR KHOSO, GBPS - SACHAL KATTO, GBPS - GULSHER KHAN KANRANI, GBPS - UMED ALI BROHI, GBPS - Abdul Ghani Shah, GGPS -Madad pur TALUKA Thul (Package No. 19)

S#	Discription	Estimated Cost	M/s. Bashir Ahmed Khoso		M/s. Gul Hassan Soomro		M/s. Abdul Haq	
			Rate	Amount	Rate	Amount	Rate	Amount
1	2	3	4	5	6	7	8	9
PART-A CIVIL SCHEDULE ITEMS								
1	Schedule Items	27,162,438		27,162,438		27,162,438		27,162,438
2	Carriage of Material	3,775,029	i) 13.75% Above	3,734,835	i) 14.10% Above	3,829,904	i) 14.40% Above	3,911,391
3	Contingency							
4	Total Part-A	30,937,467		30,897,273		30,992,342		31,073,829
PART-A NON SCHEDULE								
1	Non Schedule Items	5,590,914		5,590,914		5,593,914		5,598,914
2	Total Part-C	5,590,914		5,590,914		5,593,914		5,598,914
PART-B W/S & S/F								
1	Schedule Items	391,224	iii) 0.12% Below	391,224	iii) At Par	391,224	iii) 1.0% Above	391,224
2				469				3,912
3	Total Part-B	391,224		390,755		391,224		395,136
4	Total Part-A+B+C	36,919,605		36,878,942		36,977,480		37,067,879
	A) Total Cost as per Estimate	36,919,605						
	B) Total Cost as per Tender	36,878,942						
	Saving A-B	40,663						
	Percentage Saving	0.11%						
	A.A Amount	-						
	Lowest Tender Amount	36,878,942						
	Saving Over A.A	-						

The Lowest rate quoted by M/s. Bashir Ahmed Khoso Government Contractor are :

Part-A @ Rs. 30897273/- 13.75% Above on Estimate (Rupees Three Crore, Eight Lacs,

Ninety Seven Thousand, Two Hundred, Seventy Three) Only

Part-A @ Rs. 5590914/- Lowest Quoted Rates, on Estimate (Rupees Fifty Five Lacs, Ninety Thousand,

Nine Hundred, Fourteen) Only

Part-B @ Rs. 390755/- 0.12% Below, on Estimate (Rupees Three Lac, Ninety Thousand, Seven Hundred,

Fifty Five) Only


ASSISTANT ENGINEER
PUBLIC HEALTH ENGINEERING
SUB-DIVISION JACOBABAD


(ABDUL REHMAN MANGI)
ASSISTANT ENGINEER
EDUCATION WORKS SUB-DIVISION
JACOBABAD


(ALTAF HUSSAIN BHURGRI)
EXECUTIVE ENGINEER
EDUCATION WORKS DIVISION
JACOBABAD

BID EVALUATION REPORT

1 Name of Procuring Agency	Executive Engineer Education Works Division Jacobabad
2 Tender Reference No.	NIT No. 1925 dated: 21.02.2018
3 Tender Description / Name of Work / Item	Rehabilitaion / Expansion of High Priority 4560-Schools @ District Jacobabad. (Primary & Elemt: Schools) at GBPS - HABIB ULLAH NOONARI, GBPS - ZANGI PUR (OLD), GGPS - WARIS DINO NOONARI, GBPS - RAJO KHAN BANGLANI, GBPS - RAJAB ALI PAHORE, GBPS - LAL BUX BURIRO TALUKA Thul (Package No. 21)
4 Method of Procurement	Single Stage - One envelope procedure
5 Tender Published	News Papers & on SPPRA Website
6 Total bid documents Sold:	03 Nos
7 Total Bids Received	03 Nos
8 Technical Bid Opening Date (if applicable)	Not Applicables
9 No. of bid technically qualified (if applicable)	Not Applicable
10 Bids(s) Rejected	-
11 Financial Bid Opening Date	13.03.2018
13 Bid Evaluation Report	

S.No.	Name of Firm or Bidder	Name of Work	Ranking in Terms of cost	Ranking in Terms of cost	Comparison with Estimated Cost (if any)	Reasons for acceptance / Rejection	Remarks
1	M/s. Agha Arif Khan Durrani & Sons	GBPS - MAHBOOB-JI-WANDH	6082252	1st	0.19% Below	Lowest	Recommended for award of work
		GBPS - ABDUL KHALIQUE NOONARI	6841316				
		GBPS-Anees u Rahman	5113330				
		GBPS - CHANDAN	6371902				
		GBPS -Channa	6365524				
		GBPS -Sikandar abad	7078020				
			37852344				
2	M/s. Abdul Khaliq Dayo	GBPS - MAHBOOB-JI-WANDH	6189961	2nd	0.21% Above	Higher	Responsive
		GBPS - ABDUL KHALIQUE NOONARI	6952067				
		GBPS-Anees u Rahman	5217155				
		GBPS - CHANDAN	6480771				
		GBPS -Channa	6474368				
		GBPS -Sikandar abad	7153994				
			38468316				
3	M/s. Din Muhammad Enterprises	GBPS - MAHBOOB-JI-WANDH	6239961	3rd	0.79% Above	Highest	Responsive
		GBPS - ABDUL KHALIQUE NOONARI	7002067				
		GBPS-Anees u Rahman	5267155				
		GBPS - CHANDAN	6530771				
		GBPS -Channa	6524368				
		GBPS -Sikandar abad	7381860				
			38946182				

(Signature)
 ASSISTANT ENGINEER
 PUBLIC HEALTH ENGINEERING
 SUB-DIVISION JACOBABAD




(Signature)
 (ABDUL REHMAN MANGI)
 ASSISTANT ENGINEER
 EDUCATION WORKS SUB-DIVISION
 JACOBABAD


(Signature)
 (ALTAF HUSSAIN BHURGRI)
 EXECUTIVE ENGINEER
 EDUCATION WORKS DIVISION
 JACOBABAD


**ATTENDANCE SHEET OF PARTICIPATION IN
TENDER PROCESS IN EDUCATION WORKS DIVISION JACOBABAD**


Name of Work :- **Rehabilitaion / Expansion of High Priority 4560-Schools @ District Jacobabad. (Primary & Elemt: Schools) at GBPS - HABIB ULLAH NOONARI, GBPS - ZANGI PUR (OLD), GGPS - WARIS DINO NOONARI, GBPS - RAJO KHAN BANGLANI, GBPS - RAJAB ALI PAHORE, GBPS - LAL BUX BURIRO TALUKA Thul (Package No. 21)**

Executive Engineer Education Works Division JACOBABAD held on 13.03.2018

Sr. No	Name of Contractor / Firm	Signature
1	M/s. Agha Muhammad Arif Khan Durani & Sons.	
2	M/s. Abdul Khaliq Dayo	
3	M/s. Din Muhammad Enterprises	


ASSISTANT ENGINEER
PUBLIC HEALTH ENGINEERING
SUB-DIVISION JACOBABAD


(ABDUL REHMAN MANGI)
ASSISTANT ENGINEER
EDUCATION WORKS SUB-DIVISION
JACOBABAD


(ALTAF HUSSAIN BHURGRI)
EXECUTIVE ENGINEER
EDUCATION WORKS DIVISION
JACOBABAD

**OFFICE OF THE
EXECUTIVE ENGINEER EDUCATION WORKS DIVISION JACOBABAD**


COMPRATIVE STATEMENT


NIT NO. EE/EWD/TC/ 1925 DATED: 21.02.2018

Name of Work :-

**Rehabilitaion / Expansion of High Priority 4560-Schools @
District Jacobabad. (Primary & Elemt: Schools) at GBPS -
HABIB ULLAH NOONARI, GBPS - ZANGI PUR (OLD), GGPS -
WARIS DINO NOONARI, GBPS - RAJO KHAN BANGLANI,
GBPS - RAJAB ALI PAHORE, GBPS - LAL BUX BURIRO
TALUKA Thul (Package No. 21)**

Sr. No	Name of Contractor	Rate Quoted	
1	M/s. Agha Muhammad Arif Khan Durrani & Sons.	i) 12.40% Above ii) 5137592/- iii) 0.22% Below	(Part-A Schedule) (Part-A Non Schedule) (Part-B Schedule)
2	M/s. Abdul Khaliq Dayo	i) 12.80% Above ii) 5637592/- iii) At Par	(Part-A Schedule) (Part-A Non Schedule) (Part-B Schedule)
3	M/s. Din Muhammad Enterprises	i) 13.40% Above ii) 5937592/- iii) 1.50% Above	(Part-A Schedule) (Part-A Non Schedule) (Part-B Schedule)


ASSISTANT ENGINEER
PUBLIC HEALTH ENGINEERING
SUB-DIVISION JACOBABAD


(ABDUL REHMAN MANGI)
ASSISTANT ENGINEER
EDUCATION WORKS SUB-DIVISION
JACOBABAD



(ALTAF HUSSAIN BHURGRI)
EXECUTIVE ENGINEER
EDUCATION WORKS DIVISION
JACOBABAD


GENERAL ABSTRACT


Name of Work :-

Rehabilitaion / Expansion of High Priority 4560-Schools @ District Jacobabad. (Primary & Elemt: Schools) at GBPS - HABIB ULLAH NOONARI, GBPS - ZANGI PUR (OLD), GGPS - WARIS DINO NOONARI, GBPS - RAJO KHAN BANGLANI, GBPS - RAJAB ALI PAHORE, GBPS - LAL BUX BURIRO TALUKA Thul (Package No. 21)

Sr. No	Name of Contractor / Firm	Tender Amount
1	M/s. Agha Muhammad Arif Khan Durrani & Sons	37852344
2	M/s. Abdul Khaliq Dayo	38468315
3	M/s. Din Muhammad Enterprises	38946182


ASSISTANT ENGINEER
PUBLIC HEALTH ENGINEERING
SUB-DIVISION JACOBABAD


(ABDUL REHMAN MANGI)
ASSISTANT ENGINEER
EDUCATION WORKS SUB-DIVISION
JACOBABAD


(ALTAF HUSSAIN BHURGRI)
EXECUTIVE ENGINEER
EDUCATION WORKS DIVISION
JACOBABAD

Name of Work :-


Rehabilitaion / Expansion of High Priority 4560-Schools @ District Jacobabad. (Primary & Elemt: Schools) at GBPS - HABIB ULLAH NOONARI, GBPS - ZANGI PUR (OLD), GGPS - WARIS DINO NOONARI, GBPS - RAJO KHAN BANGLANI, GBPS - RAJAB ALI PAHORE, GBPS - LAL BUX BURIRO TALUKA Thul (Package No. 21)


SUMMARY OF COST


Sr. No	Item of Work	Schedule B Amount	Contractor Rate	Amount
1	Civil Schedule Items	32436277	i) 12.40% Above	32381209
3	Non Schedule Items	5137592	ii) 5137592/-	5137592
3	W/S & S/F	334278	iii) 0.22% Below	333543

Total Amount of Bid

A + B + C = 37852344


ASSISTANT ENGINEER
PUBLIC HEALTH ENGINEERING
SUB-DIVISION JACOBABAD


(ABDUL REHMAN-MANGI)
ASSISTANT ENGINEER
EDUCATION WORKS SUB-DIVISION
JACOBABAD



(ALTAF HUSSAIN BHURGRI)
EXECUTIVE ENGINEER
EDUCATION WORKS DIVISION
JACOBABAD


BIDDER QUALIFICATION REPORT


NIT NO. EE/EWD/TC/ 1925 DATED: 21.02.2018

EDUCATION WORKS DIVISION JACOBABAD

1	Name of Procuring Agency	Executive Engineer Education Works Division JACOBABAD
2	Tender Reference No.	NIT No. 1925, dated: 21.02.2018
3	Tender Description / Name of Work / Item	Rehabilitaion / Expansion of High Priority 4560-Schools @ District Jacobabad. (Primary & Elemt: Schools) at GBPS - HABIB ULLAH NOONARI, GBPS - ZANGI PUR (OLD), GGPS - WARIS DINO NOONARI, GBPS - RAJO KHAN BANGLANI, GBPS - RAJAB ALI PAHORE, GBPS - LAL BUX BURIRO TALUKA Thul (Package No. 21)
4	Method of Procurement	Single Stage - One envelope procedure
5	Tender Published	News Papers & on SPPRA Website
6	N.T.N	Available
7	Registration with P.E.C	Registered
8	Sindh Board of Revenue	Registered
9	Relevant Experience	Available
10	Turnover of at least last three years	Available
11	Funds / Budget	Available
12	05% Earnest Money	Available
13	Tender Fee / Cost Bidding Document	Deposited


ASSISTANT ENGINEER
PUBLIC HEALTH ENGINEERING
SUB-DIVISION JACOBABAD


(ABDUL REHMAN MANGI)
ASSISTANT ENGINEER
EDUCATION WORKS SUB-DIVISION
JACOBABAD


(ALTAF HUSSAIN BHURGRI)
EXECUTIVE ENGINEER
EDUCATION WORKS DIVISION
JACOBABAD

FINANCIAL REVIEW

NAME OF WORK:-

Rehabilitation / Expansion of High Priority 4560-Schools @ District Jacobabad. (Primary & Elemt: Schools) at GBPS - HABIB ULLAH NOONARI, GBPS - ZANGI PUR (OLD), GGPS - WARIS DINO NOONARI, GBPS - RAJO KHAN BANGLANI, GBPS - RAJAB ALI PAHORE, GBPS - LAL BUX BURIRO TALUKA Thul (Package No. 21)

S#	Description	Estimated Cost	M/s. Agha Muhammad Arif		M/s. Abdul Khaliq Dayo		M/s. Din Muhammad Enterprises	
			Rate	Amount	Rate	Amount	Rate	Amount
1	2	3	4	5	6	7	8	9

PART-A CIVIL SCHEDULE ITEMS

1	Schedule Items	28,808,905		28,808,905		28,808,905		28,808,905
2	Carriage of Material	3,627,372	i) 12.40% Above	3,572,304	j) 12.80% Above	3,687,540	i) 13.40% Above	3,860,393
3	Contingency							
4	Total Part-A	32,436,277		32,381,209		32,496,445		32,669,298

PART-A NON SCHEDULE

1	Non Schedule Items	5,137,592		5,137,592		5,637,592		5,937,592
2	Total Part-C	5,137,592		5,137,592		5,637,592		5,937,592

PART-B W/S & S/F

1	Schedule Items	334,278		334,278		334,278		334,278
2			iii) 0.22% Below	735	iii) At Par		iii) 1.50% Above	5,014
3	Total Part-B	334,278		333,543		334,278		339,292
4	Total Part-A+B+C	37,908,147		37,852,344		38,468,315		38,946,182

The Lowest rate quoted by M/s. Agha Muhammad Arif Government Contractor are :

Part-A @ Rs. 32381209/- **12.40% Above** on Estimate (Rupees Three Crore, Twenty Three Lacs, Eighty One Thousand, Two Hundred, Nine) Only

Part-A @ Rs. 5137592/- **Lowest Quoted Rates**, on Estimate (Rupees Fifty One Lacs, Thirty Seven Thousand, Five Hundred, Ninety Two) Only

Part-B @ Rs. 333543/- **0.22% Below**, on Estimate (Rupees Three Lac, Thirty Three Thousand, Five Hundred, Forty Three) Only

Abdul Rehman Mangi
 ASSISTANT ENGINEER
 PUBLIC HEALTH ENGINEERING
 SUB-DIVISION JACOBABAD

Abdul Rehman Mangi
 (ABDUL-REHMAN MANGI)
 ASSISTANT ENGINEER
 EDUCATION WORKS SUB-DIVISION
 JACOBABAD

Altaf Hussain Bhurgri
 (ALTAF HUSSAIN BHURGRI)
 EXECUTIVE ENGINEER
 EDUCATION WORKS DIVISION
 JACOBABAD

Method and procedure of procurement: NATIONAL COMPETITIVE BIDDING (SINGLE STAGE-ONE ENVELOPE).

MINUTES OF BID OPENING MEETING

A meeting of the procurement committee of this department was held on dated: 13.03.2018. for opening the bids received in respect of subject NIT till the deadlines of submission. The meeting was attended by all following members of the procurement committee and the representative of bidders. (Attendance sheet is enclosed).

The bids were opened at **2:00 PM** in the presence of the above mentioned participants and the rates quoted by bidders were read aloud and encircled by Chairman of the Procurement Committee. All the members of the procurement committee signed each and every page of financial proposal/bids. The bids do not contain any over-writing or cutting. (*Also mention cutting or over writing if any*). Following is the details of bids announced.


The committee shall examine all the bids as per the Qualification/ eligibility criteria provided in the bidding documents, arithmetical checks and verify the documents and bid security submitted by the bidders.


The meeting ended with the note of thanks to and from the chair.


(MEMBER)

(MEMBER)

(CHAIRMAN)


ASSISTANT ENGINEER
PUBLIC HEALTH ENGINEERING
SUB-DIVISION JACOBABAD


(ABDUL REHMAN MANGI)
ASSISTANT ENGINEER
EDUCATION WORKS SUB-DIVISION
JACOBABAD


(ALTAF HUSSAIN BHURGRI)
EXECUTIVE ENGINEER
EDUCATION WORKS DIVISION
JACOBABAD
