


# Bid Evaluation Report

Sl. No. 11406

1. Name of Procuring Agency: **Project Management Unit (PMU)**  
**Flood Emergency Reconstruction Project (FERP)**  
**Sindh Irrigation Department (SID)**
2. Tender Reference No: **INF/KRY.No.919/2012** 3/3/12
3. Tender Description/Name of work/item: **Package No. 22: Raising & Strengthening of R.N Mangli Bund mile from 0/0 to 1/3, Front Bund from mile 0/0 to 0/7 and R.N Bund from 0/2 to 1/1 (Ali Wahan Complex), 26/4 & Gemro Bund from mile 11/4 to 13/4, Construction Bund Landhi along R.N Mangli Bund at mile 0/2 and Gauge Pillars, mile/ furlong stones.**
4. Method of Procurement: **Single Stage: Two Envelope Bidding Procedure**  
**National Competitive Bidding (NCB)**
5. Tender Published: **Daily "Kawish" Hyderabad on 4<sup>th</sup> March 2012**  
*Print & Electronic Media (SPPRA ID No. & News papers names with dates)*
6. Total Bid documents Sold: **03 Number bid document sold**
7. Total Bids Received: **02 Bids received**
8. Technical Bid Opening date:(if applicable) **21<sup>st</sup> March 2012***(Provide details in separate form) (copies attached)*
9. No. of Bid technically qualified (if applicable): **01 Bid Technically Qualified**
10. Bid(s) Rejected: **01 (Bid Rejected)**
11. Financial Bid Opening date: **24<sup>th</sup> March 2012 at 15:00 hours**
12. Bid Evaluation Report:

S No	Name of Firm or Bidder	Cost offered by the Bidder	Ranking in terms of cost	Comparison with Estimated cost	Reasons for acceptance/rejection	Remarks
0	1	2	3	4	5	6
1.	M/S Jan Muhammad & Brothers	226,873,883	1 <sup>st</sup> Lowest	23.31 % above	1 <sup>st</sup> Lowest Evaluated Responsive Bidder	Pass (ADB approval attached)

  
Deputy Director (Procurement)  
Flood Emergency Reconstruction Project,  
Hyderabad

**DEPUTY DIRECTOR**

Flood Emergency Reconstruction Project



Serial No 213883  
PEC-5A

...in Pakistan  
...with  
...of the  
...Order  
...PEC


...

### PAKISTAN ENGINEERING COUNCIL

Licence No 3761 Category C-3 Validity 31st December, 2012

#### LICENCE OF PAKISTANI CONSTRUCTOR/OPERATOR ( Under the bye-laws of Pakistan Engineering Council 1987 )

This is to certify that M/s JAN MUHAMMAD & BROTHERS (Licensee)  
with its registered office at Shafiqabad, Bijli Chowk, Pano Akil, Distt Sukkur  
has have been licenced under Construction and Operation of Engineering Works Bye-Laws  
1987, until the validity date to construct ~~XXXX~~ engineering works, the construction/capital cost  
of which does not exceed Rs 250 (TWO HUNDRED FIFTY) million; provided the licensee fulfils all  
the qualification requirements prescribed by Client or Employer for a particular engineering  
work; and subject to the licensee continuing to fulfil all the requirements of the bye-laws.  
Field of Specialization: CE 01, 04, 10 (THREE ONLY) XXXXXXXXXXXXXXXXXXXXXXXXXXXXX  
(Specialization Code Nos. for detail see overleaf)



Registrar

Pakistan Engineering Council,  
Islamabad.

Date of Issue 10/05/2012

- Note:
- 1. This Certificate of Registration is valid until 31st December 2012. It should be renewed on payment of the required fee for the next year. Application of renewal for the next year should be submitted by 05 November 2012.
  - 2. Names of Professional Engineers working with the firm are shown on the reverse. The Consulting Engineer (the Engineer Incharge in case the consultant is not appointed) shall monitor the number of engineers employed by the Constructor and inform the Council accordingly.
  - 3. This Licence shall be renewed before 31st March, 2013 without late payment surcharge

# SINDH PUBLIC PROCUREMENT REGULATORY AUTHORITY

## CONTRACT EVALUATION FORM

### TO BE FILLED IN BY ALL PROCURING AGENCIES FOR PUBLIC CONTRACTS OF WORKS, SERVICES & GOODS

- 1) NAME OF THE ORGANIZATION / DEPTT. Sindh Irrigation Department
- 2) PROVINCIAL / LOCAL GOVT / OTHER Provincial Government
- 3) TITLE OF CONTRACT Flood Emergency Reconstruction Project
- 4) TENDER NUMBER Package No. 22-ADB/IRR/SINDH/FERP
- 5) BRIEF DESCRIPTION OF Raising & Strengthening of R.N Mangli Bund from mile 0/0 to 1/3, Front Bund from mile 0/0 to 0/7 and R.N Bund from mile 0/2 to 1/1 (Ali Wahan Complex), 26/4 & Gemro Bund from mile 11/4 to 13/4, Construction Bund Landhi along R.N Mangli Bund at mile 0/2 & Gauge Pillars, mile/ furlong stones.
- 6) FORUM THAT APPROVED THE SCHEME Asian Development Bank
- 7) TENDER ESTIMATED VALUE Rs. 185,000,000/-
- 8) ENGINEER'S ESTIMATE Rs. 185,491,404 /-  
(For civil works only)
- 9) ESTIMATED COMPLETION PERIOD (AS PER CONTRACT) 180 days
- 10) TENDER OPENED ON (DATE & TIME) 21<sup>st</sup> March 2012
- 11) NUMBER OF TENDER DOCUMENTS SOLD 03 Nos. (In BER Reports attached)  
(Attach list of buyers)
- 12) NUMBER OF BIDS RECEIVED 02 Nos.
- 13) NUMBER OF BIDDERS PRESENT AT THE TIME OF OPENING OF BIDS 01 No.
- 14) BID EVALUATION REPORT Enclosed  
(Enclose a copy)
- 15) NAME AND ADDRESS OF THE SUCCESSFUL BIDDER 01No. (In BER Reports attached)
- 16) CONTRACT AWARD PRICE 226,873,883/-
- 17) RANKING OF SUCCESSFUL BIDDER IN EVALUATION REPORT (i.e. 1<sup>st</sup>, 2<sup>nd</sup>, 3<sup>rd</sup> EVALUATION BID). 1<sup>st</sup> : 226,873,883/-
- 18) METHOD OF PROCUREMENT USED : - (Tick one)
- a) SINGLE STAGE – ONE ENVELOPE PROCEDURE \_\_\_\_\_  Domestic/Local
- b) SINGLE STAGE – TWO ENVELOPE PROCEDURE \_\_\_\_\_
- c) TWO STAGE BIDDING PROCEDURE \_\_\_\_\_
- d) TWO STAGE – TWO ENVELOPE BIDDING PROCEDURE \_\_\_\_\_

PLEASE SPECIFY IF ANY OTHER METHOD OF PROCUREMENT WAS ADOPTED i.e. EMERGENCY, DIRECT CONTRACTING / NEGOTIATION ETC. WITH BRIEF REASONS: No

19) APPROVING AUTHORITY FOR AWARD OF CONTRACT: Procurement Committee

20) WHETHER THE PROCUREMENT WAS INCLUDED IN ANNUAL PROCUREMENT PLAN?

Yes	<input checked="" type="checkbox"/>	No	<input type="checkbox"/>
-----	-------------------------------------	----	--------------------------

21) ADVERTISEMENT :

i) SPPRA Website  
(If yes, give date and SPPRA Identification No.)

Yes	<input checked="" type="checkbox"/>	INF/KRY-No. 919/2012	<input type="checkbox"/>
No	<input type="checkbox"/>		<input type="checkbox"/>

ii) News Papers  
(If yes, give names of newspapers and dates)

Yes	<input checked="" type="checkbox"/>	Daily "Kawish" Hyd Dated 04-03-2012	<input type="checkbox"/>
No	<input type="checkbox"/>		<input type="checkbox"/>

22) NATURE OF CONTRACT

Domestic/Local	<input checked="" type="checkbox"/>	No	<input type="checkbox"/>
----------------	-------------------------------------	----	--------------------------

23) WHETHER QUALIFICATION CRITERIA WAS INCLUDED IN BIDDING / TENDER DOCUMENTS?  
(If yes, enclose a copy)

Yes	<input checked="" type="checkbox"/>	No	<input type="checkbox"/>
-----	-------------------------------------	----	--------------------------

24) WHETHER BID EVALUATION CRITERIA WAS INCLUDED IN BIDDING / TENDER DOCUMENTS?  
(If yes, enclose a copy)

Yes	<input checked="" type="checkbox"/>	No	<input type="checkbox"/>
-----	-------------------------------------	----	--------------------------

25) WHETHER APPROVAL OF COMPETENT AUTHORITY WAS OBTAINED FOR USING A METHOD OTHER THAN OPEN COMPETITIVE BIDDING? Yes

Yes	<input checked="" type="checkbox"/>	No	<input type="checkbox"/>
-----	-------------------------------------	----	--------------------------

26) WAS BID SECURITY OBTAINED FROM ALL THE BIDDERS?

Yes	<input checked="" type="checkbox"/>	No	<input type="checkbox"/>
-----	-------------------------------------	----	--------------------------

27) WHETHER THE SUCCESSFUL BID WAS LOWEST EVALUATED BID / BEST EVALUATED BID (in case of Consultancies)

Yes	<input checked="" type="checkbox"/>	No	<input type="checkbox"/>
-----	-------------------------------------	----	--------------------------

28) WHETHER THE SUCCESSFUL BIDDER WAS TECHNICALLY COMPLIANT?

Yes	<input checked="" type="checkbox"/>	No	<input type="checkbox"/>
-----	-------------------------------------	----	--------------------------

29) WHETHER NAMES OF THE BIDDERS AND THEIR QUOTED PRICES WERE READ OUT AT THE TIME OF OPENING OF BIDS?

Yes	<input checked="" type="checkbox"/>	No	<input type="checkbox"/>
-----	-------------------------------------	----	--------------------------

30) WHETHER EVALUATION REPORT GIVEN TO BIDDERS BEFORE THE AWARD OF CONTRACT?  
(Attach copy of the bid evaluation report)

Yes	<input type="checkbox"/>	No	<input checked="" type="checkbox"/>
-----	--------------------------	----	-------------------------------------

31) ANY COMPLAINTS RECEIVED  
(If yes, result thereof)

Yes	
No	√

32) ANY DEVIATION FROM SPECIFICATIONS GIVEN IN THE TENDER NOTICE / DOCUMENTS  
(If yes, give details)

Yes	
No	√

33) WAS THE EXTENSION MADE IN RESPONSE TIME?  
(If yes, give reasons)

Yes	√ Due to Variation in contract
No	

34) DEVIATION FROM QUALIFICATION CRITERIA  
(If yes, give detailed reasons.)

Yes	
No	√

35) WAS IT ASSURED BY THE PROCURING AGENCY THAT THE SELECTED FIRM IS NOT BLACK LISTED?

Yes	√	No	
-----	---	----	--

36) WAS A VISIT MADE BY ANY OFFICER/OFFICIAL OF THE PROCURING AGENCY TO THE SUPPLIER'S PREMISES IN CONNECTION WITH THE PROCUREMENT? IF SO, DETAILS TO BE ASCERTAINED REGARDING FINANCING OF VISIT, IF ABROAD:  
(If yes, enclose a copy)

Yes	√	No	
-----	---	----	--

37) WERE PROPER SAFEGUARDS PROVIDED ON MOBILIZATION ADVANCE PAYMENT IN THE CONTRACT (BANK GUARANTEE ETC.)?

Yes	√	No	
-----	---	----	--

38) SPECIAL CONDITIONS, IF ANY  
(If yes, give Brief Description)

Yes	
No	√

39) Date of Award of Contract: 29<sup>th</sup> March 2012

Signature & Official Stamp of  
Authorized Officer


*[Signature]*  
DEPUTY DIRECTOR

Project Management Unit (PMU)  
Emergency Reconstruction Project

**FOR OFFICE USE ONLY**

**SPPRA, Block. No.8, Sindh Secretariat No.4-A, Court Road, Karachi**

**Tele: 021-9205356; 021-9205369 & Fax: 021-9206291**



MAINTENANCE WORK MEMO  
Govt. Billing Vendor Session  
Near Treasury office, Hyd

Jan Muhammad and Brothers / 3963  
29 MAR 2012 / 29-03-2012

Executive Engineer  
Ghotki Division Irrigation  
GHOTKI

M/S Jan Muhammad & Brothers  
Balji Chowk Fano Akil

"CONTRACT AGREEMENT"


THIS AGREEMENT made the Monday 26<sup>th</sup> March 2012, between Sindh Irrigation Department (SID) through the Executive Engineer Ghotki Division Sindh of the one part and M/s, Jan Muhammad & Brothers of the other part. WHEREAS the Employer desired that the works known as Package No: 22 Raising & Strengthening of R.N Mangli Bund from Mile 0/0 to 1/3, Front Band from Mile 0/0 to 0/7 & R.N Band from Mile 0/2 to 1/1 (At Wahar Complex), Providing Stone Pitching along R.N Band from Mile 22/4 to 26/4 and Genra Bund from Mile 11/4 to 13/4, Construction of Bund Landhi along R.N Mangli Bund at Mile 0/2 and Gauge Pillars, Mile/Furlong

28  
28




General Conditions of Sale

General Conditions of Sale



23



*M/S Jan Mohammad and Brothers*  
*23 Nov 2012*

*3963*  
*29-03-2012*

*Jan Mohammad*

*Jan Mohammad & Brothers*  
*Bali Chowk Pano Ak*

Should be executed by the Contractor, and has accepted a Bid by the Contractor for the execution and completion of these Works and the remedying of any defects therein.

The Employer and the Contractor agree as follows.


1. In this Agreement words and expressions shall have the same meanings as are respectively assigned to them in the Contract documents referred.
2. The following documents shall be deemed to form and be read and construed as part of this Agreement. This Agreement shall prevail over all other Contract documents.
  - the Letter of Acceptance.
  - the Letters of Technical Bid and Price Bid.
  - the Addenda Nos.
  - the particular Conditions
  - the General Conditions
  - the Specification
  - the Drawings;
  - the completed Schedules,
  - the cash flow projection.





General Conditions of Sale

General Conditions of Sale




28

22

28

2



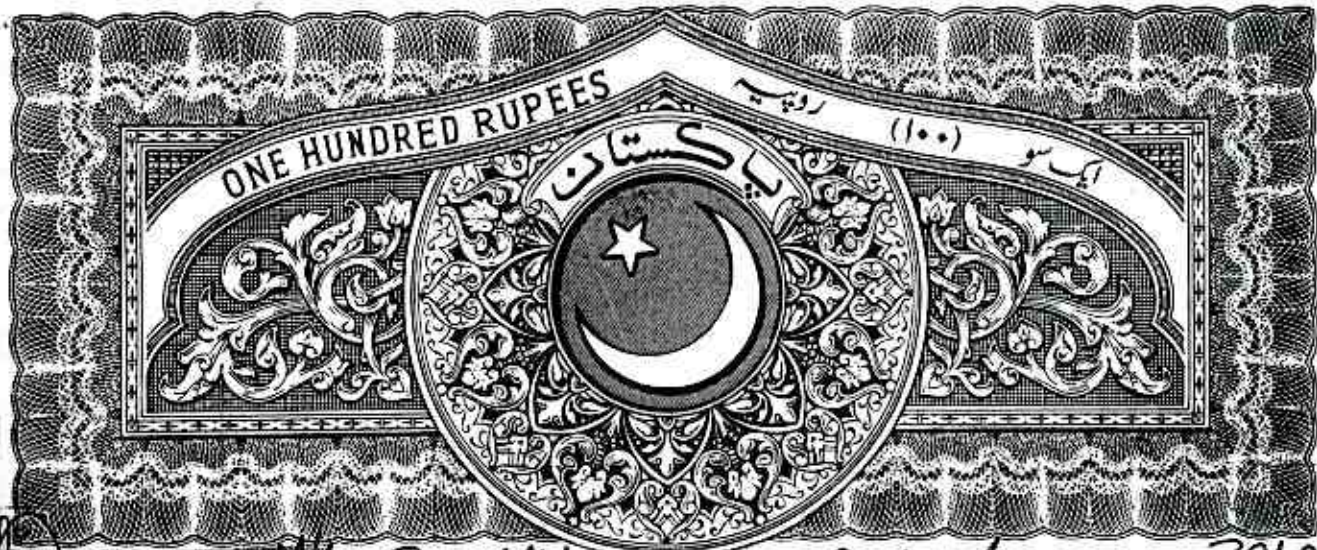

PAKISTAN  
Near Treasury office, H...

Jan Muhammad and Brothers

3963

29 MAR 2012

29-03-2012


In consideration of the payments to be made by the Employer to the Contractor as indicated in this Agreement, the Contractor hereby covenants with the Employer to execute the Work and to remedy defects therein in conformity in all respects with the provisions of the Contract.

The Employer hereby covenants to pay the Contractor in consideration of the execution and completion of the Works and the remedying of defects therein, the Contract Price or such other sum as may become payable under the provisions of the Contract at the times and in the manner prescribed by the Contract.

IN WITNESS whereof the parties hereto have caused this Agreement to be executed in accordance with the laws of Islamic Republic of Pakistan on the day, month and year indicated above.

*[Signature]*  
M/S, JAN MUHAMMAD & BROTHERS  
CONTRACTOR

*[Signature]*  
EXECUTIVE ENGINEER  
GHOTKI DIVISION (IRRIGATION)  
@GHOTKI





**OFFICE OF THE EXECUTIVE ENGINEER  
Ghotki Division**

Reference No: TC 567  
Date: 26-03-2012

To :

**M/S Jan Mohammad & Brothers**

**Package No.22 : Raising and Strengthening of R.N Mangli Bund from mile from 0/0 to 1/3, Front Bund from mile 0/0 to 0/7 & R.N Bund from mile 0/2 to 1/1 (Ali Wahan Complex), Providing Stone Pitching along R.N Bund from mile from 22/4 to 26/4 and Gemro Bund from mile from 11/4 to 13/4, Construction Bund Landhi along R.N Mangli Bund at mile 0/2 and Gauge Pillars, mile /furlong Stones.**

**Subject: Notification of Award**

**(Bid Number: NCB-22-FERP/Irrigation-Sindh)**

This is to notify you that your Bid dated 21<sup>st</sup> March 2012 consisting of the Technical and Price Bids for execution of the **Package No: 22. Raising and Strengthening of R.N Mangli Bund from mile from 0/0 to 1/3, Front Bund from mile 0/0 to 0/7 & R.N Bund from mile 0/2 to 1/1 (Ali Wahan Complex), Providing Stone Pitching along R.N Bund from mile from 22/4 to 26/4 and Gemro Bund from mile from 11/4 to 13/4, Construction Bund Landhi along R.N Mangli Bund at mile 0/2 and Gauge Pillars, mile /furlong Stones. NCB-22-ADB/IRR/Sindh/FERP**, for the Accepted Contract Amount of the equivalent of PRs 226,873,883.(Two Hundred & Twenty Six Million, Eight Hundred Seventy Three Thousand, Eight Hundred & Eighty Three Pak Rupees Only.) as corrected and modified in accordance with the Instructions to Bidders is hereby accepted by the Procurement Committee.

You are requested to furnish the Performance Security in accordance with the Conditions of Contract, using for that purpose the Performance Security Form included in Section 9 (Contract Forms) of the Bidding Document. Please find attached Appendix 1. We would appreciate if your authorized Representative could meet the undersigned before 29-03-2012 for agreeing certain time lines stipulated therein. (Appendix 1).









Assad Ullah  
Executive Engineer  
Ghotki Division  
Executive Engineer  
Ghotki Division Irrigation  
GHOTKI

**4. CONCLUSIONS AND RECOM MENDATIONS**

On the basis of the systematic evaluation of bids as presented in this report, it was concluded that only one (01) out of the two (02) submitted bids were considered as Substantially Responsive (**Appendix 9**).


Of the two (02) bids received, one (01) bid was considered Substantially Non-Responsive. One (01) bidder at serial number 2 is considered as Substantially Responsive and is proposed for opening his Price Proposal by the Procurement Committee. Price Proposal of Bidder No. 2 may be returned unopened.

 Signed Mohammad Ehsan Leghari M.D S.I.D.A Chairman	 Signed Anwar Ali Siyal Director Ghotki FCAWB Member	 Signed Assad Ullah Executive Engineer Ghotki Division Member/Secretary	 Signed Habib Ullah Divisional Account Officer Member
 Signed Jamal-u-Din Mangan DD-PMU-FERP Member	 Signed Ahmed Junaid Memon PD-PMU-FERP Member		

Executive Engineer  
Ghotki Division Irrigation  
GHOTKI


Appendix 2

6) The Record of Bid Opening (Price Proposals) was prepared soon after the bids were announced. The details are as follows:

Name of the Bidder	Bid Price as Opened in words	Discount Offered	Final Bid Price (after discount if any)	Signature
M/S Jan Mohammad & Brothers	Two Hundred & Sixty Six Million, Three Hundred & Forty Thousand Four Hundred & Fifty Pak Rupees & Sixty Seven Paisas	15.1-	PKs 226873883	



Signed  
Muhammad Ehsan Leghari  
M.D S.I.D.A  
Chairman



Signed  
Anwar Ali Siyal  
Director Ghotki FCAWB  
Member




Signed  
Assad Ullah  
Executive Engineer  
Ghotki Division  
Member/Secretary



Signed  
Habib Ullah  
Divisional Account Officer  
Member



Signed  
Jamal-u-Din Mangan  
DD-PMU-FERP  
Member



Signed  
Ahmed Junaid Memon  
PD-PMU-FERP  
Member

Executive Engineer  
Ghotki Division Irrigation  
GHOTKI



Contract Title: Package No. 22: Raising & Strengthening of R.N Mangli Bund from Mile 0/0 to 1/3, Front Bund from mile 0/0 to 0/7 & R.N Bund from Mile 0/2 to 1/1 (All Wahan Complex). Providing Stone Pitching along R.N Bund from Mile 22/4 to 26/4 and Gemro Bund from Mile 11/4 to 13/4. Construction of Bund Landhi along R.N Mangli Bund at Mile 0/2 and Gauge Pillars.mile/furlong Stones.

### COMPARATIVE STATEMENT- BID PRICE

S.No	Items	Engineer Estimate	Bidder Name	
			M/S Jan Mohammad & Brothers	% Difference
		Final Amount		
<b>A</b>	<b>Civil Works</b>			
<b>Earth Work</b>				
1	Jungle Clearance and removing within 100ft (a) light	25,790.59		155586.11%
2	Ploughing 3 times	31,251.34		59.17%
3	Borrow Pit Excavation undressed lead up to 100ft in ordinary soil.	4,748,382.79		54.55%
4	Carriage of 100 CIV 5ton of all material like stone aggregate, spawl, coal, lime, surkhi etc B G Rail fastening points and crossing bridge girders pipes sheet, Rails M S bars etc or 1000 Nos. Bricks 10"x5"x3" or 1000 Nos tiles 12"x6"x2" or 150 Cft of timber or 100 maunds of fuel wood by truck or any other means owned by the contractor including supply of earth from source to site of work.	32,482,414.10		0.05%
5	Earth work compaction (Soft, ordinary and Hard soil) (b) Laying Earth in 6" layers leveling, dressing and watering for compaction etc complete.	936,221.87		52.69%
6	Earth work compaction by sheep foot roller and power Roller with Optimum moisture content for 90% modified AASHO density.	5,691,163.83		-17.94%
<b>Stone Pitching</b>				
1	Earth work excavation in Irrigation Channels drains etc dressed to designed section grades and profile excavated materials disposed off and dressed with 50 ft lead (a) ordinary soil.	1,836,860.85		67.91%
2	Stone filling dry hand packed as filling behind the retaining walls or in pitching and aprons including supply of stone from source to site of work.	7,992,336.87		10.13%
3	Formation, dressing and preparing sub-grade on slope.	3,080,117.92		-1.65%
4	Stone pitching i/c sub-base with hammer dressed stone on surface laid in courses i/c supply of materials from source to site of work.	124,607,789.89		-2.00%
<b>Bund Landhi - Errecting Gauge Pillars, M/S &amp; Supply of Stones</b>				
1	Excavation in foundation of buildings, bridges and other structure i/c dag, belling, dressing refilling around structures with excavated Earth watering and ramming lead up-to 5ft (b) ordinary soil.	3,904.90		-24.79%
2	Cement Concrete brick/stone ballast 1- 1/2" to 2" gauge (ratio 1:4:8) including supply of material from source to site of work.	19,552.53		-35.04%
3	Damp proof course with cement sand and shingle concrete (ratio 1:2:4) i/c two coats of asphaltic mixture 3" thick i/c supply of materials from source to site of work.	10,763.69		-48.31%
4	Pacca brick work in foundation and plinth in cement sand mortar ratio (1:4) including supply of material from source to site of work.	82,451.91		-42.02%
5	Pacca brick work other than building including striking of joint upto 20 feet height i/c supply of material from source to site of work (Ratio 1:5)	231,620.13		-42.93%

Executive Engineer  
Ghotki Division Irrigation  
GHOTKI  
*Amjad*

S.No	Items	Engineer Estimate	Bidder Name	
			M/S Jan Mohammad & Brothers	% Difference
		Final Amount		
6	RCC work in Ratio 1:2:4 roof slabs, beams, columns, raftis, lintels & other structural members laid in situ or pre cast laid in position complete in all respect ratio (1:2:4) 90 lbs cement 2cft, sand 4 cft, shingle 1/8" to 1/4" gauge i/c supply of materials from source to site of work.	8,346.51		-65.00%
7	Fabrication of mild steel reinforcement of cement concrete including cutting, bending, leveling in position, making joints and fastening including cost of blinding wire & removal of rust from bars (using tor bars) including supply of material from source to site of work i/c supply of steel from source to site of work.	35,008.26		-32.43%
9	Preparing surface and painting doors and windows any type i/c edges 3 coats.	1,311.79		31.89%
10	Filling watering and ramming earth under floor with new earth excavated from outside lead upto one chain and lift upto 5 ft i/c supply of materials from source to site of work.	10,937.52		19.94%
11	Supplying R.S Griders (8" x 4")	10,815.00		70.00%
12	Supplying T- Iron (2"/2x2"/2x1/4")	13,192.50		61.95%
13	1st class tiles roofing consisting of 4" earth 1" mud plaster with gobi lying over 1/2" thick cement plaster ratio 1:6 with 34 lbs. of hot bitumen coating sand blinded provided over 2 layers of tiles 12"x6" x 1 1/4" laid in 1:4 cement mortar with 1/2" thick sand wicheed layer of 1:6 cement pointing under side of tiles complete and i/c curing and supply of Material from source to site of work.	20,480.35		10.55%
14	Cement concrete plain i/c placing, compacting, finishing and curing complete i/c screening and washing of stone aggregate w/o shuttering ratio 1:3:6 i/c supply of material from source to site of work.	21,096.29		-46.80%
15	Providing & laying 1" thick topping cement concrete (ratio 1:2:4) i/c surface finishing and dividing into panels 2" thick i/c supply of material from source to site of work.	9,688.15		-36.95%
16	Cement Plaster (1:2 upto 20' height 1/2" thick) including supply of material from source to site of work.	17,562.87		13.75%
17	White washing three coats.	1,938.48		32.10%
18	Cement pointing struck joints on walls ratio 1:2 i/c supply of material from source to site of work.	13,154.78		-22.15%
19	Supply and fixing cement concrete spots i/c fixing in position with top and bottom kharas.	147,750.00		-98.38%
20	Extra for wet earth work.	2,015.86		-37.78%
21	Cement concrete brick or stone ballast 1/1-2" to 2" gauge 1:3:6 i/c supply of materials from source to site of work.	30,569.91		16.75%
22	Cement pointing flush upto 20 feet height, (ratio 1:2) including supply of material from source to site of work.	13,021.47		44.76%
23	Cement Plaster (1:4 upto 20' height 1/2" thick) including supply of material from source to site of work.	200.47		29.41%
24	Preparing surface and painting corrugated surface patent roofing etc (two coats).	1,553.89		12.73%
25	Writing letters or figures per letters per inch height.	8,152.32		33.94%
26	Providing for wide gauge reading to 10 of a foot	23,284.80		101.80%
	Preparing surface and painting small detached articles exceeding one sft and not exceeding 3 sft of painted surface 3 coats.	88,419.75		-99.80%
C	Contingencies	500,000.00		0.00%
D	Environment Management Plan	2,730,000.00		0.00%
		185,931.00		22.31%

**Conclusion:** M/S Jan Mohammad & Brothers has offered evaluated rate i.e. 22.31% above the estimate and is proposed as Lowest Evaluated Responsive Bidder.

Executive Engineer  
Ghotki Division Irrigation  
GHCTKI

*Quaid*



**INTEGRITY PACT**  
**DECLARATION OF FEES, COMMISSION AND BROKERAGE ETC.**  
**PAYABLE BY THE SUPPLIERS/CONTRACTORS/CONSULTANTS.**

Contract Number: IFB No: 22-ADB/IRR/Sindh/FERP(NCB) Dated: 26-03-2012

Contract Value: PRs. 226,873,883/-

Contract Title: Package No. 22: Raising & Strengthening of R.N Mangli Bund Mile from 0/0 to 1/3, Front Bund from Mile 0/0 to 0/7 & R.N Bund from 0/2 to 1/1 (Ali Wahan Complex), 26/4 and Gemro Bund from mile 11/4 to 13/4, Construction Bund Landhi along R.N Mangli Bund at mile 0/2 and Gauge Pillars, mile/ furlong stones.


M/S Jan Muhammad & Brothers Government Contractor hereby declares that it has not obtained or induced the procurement of any contract, right, interest, privilege or other obligation or benefit from Government of Sindh (GoS) or any administrative subdivision or agency thereof or any other entity owned or controlled by it (GoS) through any corrupt business practice.

Without limiting the generality of the foregoing, M/S Jan Muhammad & Brothers Government Contractor represents and warrants that it has fully declared the brokerage, commission, fees etc. paid or payable to anyone and not given or agreed to give and shall not give or agree to give to anyone within or outside Pakistan either directly or indirectly through any natural or juridical person, including its affiliate, agent, associate, broker, consultant, director, promoter, shareholder, sponsor or subsidiary, any commission, gratification, bribe, finder's fee or kickback, whether described as consultation fee or otherwise, with the object of obtaining or inducing the procurement of a contract, right, interest, privilege or other obligation or benefit, in whatsoever form, from Procuring Agency (PA), except that which has been expressly declared pursuant hereto.


M/S Jan Muhammad & Brothers Government Contractor certifies that it has made and will make full disclosure of all agreements and arrangements with all persons in respect of or related to the transaction with PA and has not taken any action or will not take any action to circumvent the above declaration, representation or warranty.

M/S Jan Muhammad & Brothers Government Contractor accepts full responsibility and strict liability for making any false declaration, not making full disclosure, misrepresenting facts or taking any action likely to defeat the purpose of this declaration, representation and warranty. It agrees that any contract, right, interest, privilege or other obligation or benefit obtained or procured as aforesaid shall, without prejudice to any other right and remedies available to PA under any law, contract or other instrument, be voidable at the option of PA.

Notwithstanding any rights and remedies exercised by PA in this regard, M/S Jan Muhammad & Brothers Government Contractor agrees to indemnify PA for any loss or damage incurred by it on account of its corrupt business practices and further pay compensation to PA in an amount equivalent to ten times the sum of any commission, gratification, bribe, finder's fee or kickback given M/S Jan Muhammad & Brothers Government Contractor as aforesaid for the purpose of obtaining or inducing the procurement of any contract, right, interest, privilege or other obligation or benefit, in whatsoever form, from PA.

  
Deputy Director (Procurement)  
Flood Emergency Reconstruction Project,  
Hyderabad

Government Project Management Unit (GPMU)  
Flood Emergency Reconstruction Project

  
M/S Jan Muhammad & Brothers  
Government Contractor





Asian Development Bank

TRANSMITTED

*Ahmed*  
27-3-12

Pakistan Resident Mission

26 March 2012

Mr. Ahmed Junaid Memon  
Project Director  
Flood Emergency Reconstruction Project  
Hyderabad

Subject: Loan No 2742/2743-PAK (SF): Flood Emergency Reconstruction Project (FERP)  
- Contract Award for Civil Works Packages 21, 22, 23, 24, 25 & 26

Dear Mr. Memon,

1. ADB approves EA's recommendation to award the contracts to the following lowest evaluated responsive bidders as recommended in the Bid Evaluation Reports (BERs) submitted through your letter dated 24 March 2012.


S.No	Package No	Bidder Name	Contract Price
1	Package No. 21: Raising and Strengthening of Paliya Loop Bund from Mile 0/0 To 3/3, Abad Ring Bund from Mile 0/6 To 2/6, L.S Bund from Mile 9/4 To 17/2, Mile 20/0 To 23/2, Mile 26/2 To 27/4, Mile 28/0 to 32/3 and Providing Stone Pitching along L.S Bund from Mile 10/0 to 11/1	M/S KMK-SE (J.V)	PRs. 328,889,591
2	Package No 22: Raising and Strengthening of R.N Mangli Bund from mile from 0/0 to 1/3, Front Bund from mile 0/0 to 0/7 & R.N Bund from mile 0/2 to 1/1 (Ali Wahan Complex). Providing Stone Pitching along R.N Bund from mile 22/4 to 26/4 and Gemro Bund from mile 11/4 to 13/4, Construction Bund Landhi along R.N Mangli Bund at mile 0/2 and Gauge Pillars, mile /furlong Stones.	M/S Jan Mohammad & Brothers	PRs. 226,873,883
3	Package No 23: Raising and Strengthening of Dilwaro Bund from mile 0/0 to 7/0 & Raising of Stone Pitching from mile 0/0 to 1/0 & Providing Stone Pitching from mile 1/0 to 3/0, Construction of Bund Landi, Gauge Pillars & Mile/Furlong Stones and Providing Stone Pitching along Ranwali Bund from Mile 9/0 to 11/0	M/S Sher Mohammad Mugheri	PRs. 154,163,620
4	Package No 24: Raising & Strengthening of Ghotki Feeder Bund from Mile 3/0 to 8/0 and Raising of Stone Pitching along Machka Bund from Mile 0/0 to 2/4+230	M/S Abdul Hakeem Chachar & Sons	PRs. 46,189,856.


**ADB**
**Asian Development Bank**
**Pakistan Resident Mission**

	<b>Package No. 25: Raising &amp; Strengthening and stone pitching along L.M bund Mile 0/0 to 7/2 &amp; left spur mile 0/0 to 2/3</b>	<b>M/S I.O.M (J.V)</b>	<b>PRs. 331,411,389</b>
	<b>Package No. 26: Constructing stone pitching along K.K. Bund from Mile 3/0 to 6/0 and Mile 24/0 to 25/6</b>	<b>M/S Abdul Qayoom Mazari</b>	<b>PRs.105,524,611</b>

2. Please send us copies of the signed contracts at the earliest possible.

Yours sincerely,



Werner E. Liepach  
Country Director

CC Mr. Babar Effandi, Secretary Irrigation Department, Government of Sindh

RMF/im

Level 8, North Wing, Serena Office Complex  
Khayaban-e-Suhrawardy G-5, Islamabad  
GPO Box 1863, Islamabad, Pakistan

Tel +(92-51) 260.0351 - 69 / 208.7300  
Fax+(92-51) 260.0366

adbprn@adb.org  
www.adb.org
