

SINDH PUBLIC PROCUREMENT REGULATORY AUTHORITY

CONTRACT EVALUATION FORM

1	NAME OF THE ORGANIZATION	LYARI DEVELOPMENT AUTHORITY
2	PROVINCIAL / LOCAL GOVERNMENT / OTHER	LOCAL GOVERNMENT
3	TITLE OF CONTRACT	Construction of 60' wide roads in sector 12 in Hawksbay INFRA-001
4	TENDER NO	
5	BRIEF DESCRIPTION OF CONTRACT	Construction of 60' wide Road in Sector 12 in Hawksbay, Scheme 42
6	FORUM THAT APPROVED THE SCHEME	DDWP
7	TENDER ESTIMATED VALUE	Rs. 8,17,38,091/-
8	ENGINEERING ESTIMATE (FOR CIVIL WORKS ONLY)	Rs. 8,17,38,091/-
9	ESTIMATED COMPLETION PERIOD	Twelve (12) Months
10	TENDER OPENED ON (DATE & TIME)	04-06-2012
11	NUMBER OF TENDER DOCUMENTS SOLD (ATTACH LIST)	04 Nos
12	NUMBER OF BIDS RECEIVED	04 Nos
13	NUMBER OF BIDDERS PRESENT AT THE TIME OF OPENING	List enclosed
14	BID EVALUATION REPORT (ATTACH A COPY)	Enclosed
15	NAME & ADDRESS OF THE SUCCESSFUL BIDDER	M/s. Riasat Brothers, F-102, Block F, North Nazimabad, Karachi
16	CONTRACT AWARD PRICE	Rs. 7,96,04,975/-
17	RANKING OF SUCCESSFUL BIDDER IN EVALUATION REPORT (i.e. 1 st , 2 nd , 3 rd EVALUATED BID)	1 st Lowest
18	METHOD OF PROCUREMENT a) SINGLE STAGE ONE ENVELOPE PROCEDURE b) SINGLE STAGE TWO ENVELOPE PROCEDURE c) TWO STAGE BIDDING PROCEDURE d) TWO STAGE TWO ENVELOPE PROCEDURE	Single envelope procedure
19	APPROVING AUTHORITY FOR AWARD OF CONTRACT	Director General, LDA
20	WHETHER PROCUREMENT WAS INCLUDED IN ANNUAL PROCUREMENT PLAN	Yes

21	ADVERTISEMENT	The News, daily Jang, Kawish dated 11 th May 2012. 6260/2012
22	SPPRA WEBSITE NEWSPAPERS NATURE OF CONTRACT	Domestic/Local
23	WHETHER QUALIFICATION CRITERIA WAS INCLUDED IN BIDDING DOCUMENTS?	Open competition bidding method was used.
24	WHETHER EVALUATION CRITERIA BID WAS INCLUDED IN BIDDING DOCUMENTS?	Yes
25	WHETHER APPROVAL OF COMPETENT AUTHORITY WAS OBTAINED FOR USING A METHOD OTHER THAN COMPETITIVE BIDDING?	Yes
26	WAS BID SECURITY OBTAINED FROM ALL THE BIDDERS?	Yes
27	WHETHER THE SUCCESSFUL BID WAS LOWEST EVALUATED BID/BEST EVALUATED BID?	Yes
28	WHETHER THE SUCCESSFUL BIDDER WAS TECHNICALLY COMPLAINT?	Yes
29	WHETHER THE NAMES OF THE BIDDERS AND THEIR QUOTED PRICES WERE READ OUT AT THE TIME OF OPENING OF BIDS?	Yes
30	WHETHER EVALUATION REPORT WAS GIVEN TO BIDDERS BEFORE THE AWARD OF CONTRACT?	Yes
31	ANY COMPLAINT RECEIVED	No
32	ANY DEVIATION FROM SPECIFICATIONS GIVEN IN THE TENDER NOTICE/DOCUMENTS	No
33	WAS THE EXTENSION MADE IN RESPONSE TIME?	No
34	ANY DEVIATION FROM QUALIFICATION CRITERIA	No
35	WAS IT ASSURED BY THE PROCURING AGENCY THAT THE SELECTED FIRM IS NOT BLACK LISTED?	Yes

36 WAS A VISIT MADE BY ANY OFFICER/OFFICIAL OF THE PROCURRING AGENCY TO THE SUPPLIERS PREMISES IN CONNECTION WITH THE PROCUREMENT? DETAILS TO BE ASCERTAINED REGARDING FINANCES OF VISIT IF ABROAD

No

37 WERE PROPER SAFEGUARD PROVIDED ON MOBILIZATION ADVANCE PAYMENT IN THE CONTRACT (BANK GUARANTEE ETC)

Yes

38 SPECIAL CONDITIONS IF ANY

No

39 DATE OF AWARD OF CONTRACT

28th June 2012

40 SIGNATURE & OFFICIAL STAMP OF AUTHORIZED OFFICER



EXECUTIVE ENGINEER
Halkway Division
Lyari Development Authority

FOR OFFICE USE ONLY


BID EVALUATION REPORT


1. Name of Agency : Lyari Development Authority
2. Tender Reference No : Infra-001
3. Tender description/Name of work : Construction of 60' wide Road in Sector 12 in Hawksbay, Scheme 42
4. Method of Procurement : Single Envelop procedure
5. Tender published : The News, Daily Jang, Kawish dated 11th May 2012.
6. Total Bid sold : 04 Nos
7. Total bid received : 04 Nos
8. Technical Bid Opening date : 04th June 2012.
9. No of Bid technically qualified : 04 Nos
10. Bid(s) Rejected : NA
11. Financial bid opening date : 04th June 2012.
12. Bid Evaluation Report :

S.#	Name of Firm/Bidder	Cost offered by Bidder	Ranking in term of cost	Comparasion of Estimated Cost	Reasons for acceptance /rejection	Remarks
1	2	3	4	5	6	7
01	M/s. Riasat Brothers	Rs. 7,96,04,975/-	1 st Lowest	2.26%	Accepted being 1 st lowest	
02	M/s. Samad Khan Baber & Company	Rs. 8,46,86,506/-	2 nd Lowest	6.55%	-	
03	M/s. Abdul sattar & Sons	Rs. 8,16,26,378/-			-	
04	M/s. Kamran & Kampany	Not quoted				


Deputy Director (F&A)
Member

Deputy Director (F&A)
Lyari Development Authority


Consultant
Member


Executive Engineer
Member
EXECUTIVE ENGINEER
KARACHI HAZIMABAD ZONE
DPC (CENTRAL)


Executive Engineer
Chairman
EXECUTIVE ENGINEER
Hawksbay Division
Lyari Development Authority



LYARI DEVELOPMENT AUTHORITY
OFFICE OF THE EXECUTIVE ENGINEER, HAWKS BAY-III

No. EE/HBD-III/LDA/Infra-001/2012/ 22.6

Dated 28th June, 2012.

M/s. Riayat Brothers,
Flat No. 204-206,
Shahida Mension Commercial Area,
Block 2, P.E.C.H.S.
Karachi.

WORK ORDER

Sub: **CONSTRUCTION OF 60' WIDE ROADS IN BLOCK 12 IN HAWKS BAY, SCHEME 42**
(CONTRACT NO: INFRA-001)

With reference to letter of acceptance for the subject work amounting to Rs. 7,96,04,975/- (Rupees Seven Crore Ninety Six Lacs Fifty Four thousand Nine hundred Seventy Five only) issued vide this office letter No. EE/HBD-III/Infra-001/ dated 26th June, 2012, you are requested to make immediate arrangements to start the work within (14) Fourteen days from the date of issue of this letter and complete the same within the period stipulated for completion of work in the tender documents i.e (12) Twelve months. The time allowed for completion of work shall be considered as the essence of contract.

Please note that the work should be carried out strictly in accordance with the drawing, design, specification, terms & conditions agreed to as per contract agreement of above mentioned work. In this connection please get in touch with the Resident Engineer of the consultant M/s. Osmani & Company (Pvt) Ltd and Assistant Executive Engineer of this division.

The execution of work and quality control shall be supervised by the consultant M/s. Osmani & Co (Pvt) Ltd and payment towards work done shall be released after verification of bills by the consultant.

In case you failed, to commence the work within 14 (fourteen) days from the date of issue of this letter, action under the relevant clauses of the contract agreement shall be initiated against you.


Executive Engineer
Hawks Bay Division-III
28/6

Copy for information to:

1. The Director (F&A), LDA
2. The Chief Engineer, LDA
3. The Superintending Engineer, LDA
4. M/s. Osmani & company (Pvt) Ltd.
5. The Resident Engineer, M/s. OCL
6. The PS to Director General, LDA.

1

SUMMARY BILL OF QUANTITIES

Owner : Lyari Development Authority
 Project : Infrastructure Development Works at Hawksbay Scheme -42
 Work : Construction of 60ft. Wide Road in Sector 12. (Hawksbay Scheme -42)
 Head : Road Work
 Location : Hawksbay
 Bill No. : INFRA - 01

Description	Amount
Roads Work	37324947/-
Construction of RCC Drain	42280028/-
Total (Rs.)	79604975/-

Seven Crore Ninety Six Lac Four Thousand

In Words

Nine Hundred Seventy Five Only

[Signature]

RACTOR

[Signature]
04/6/12

[Signature]
4/6/2012

[Signature]
4/6

BILL OF QUANTITIES

Client : Lyari Development Authority
 Project : Infrastructure Development Works at Hawksbay Scheme - 42
 Work : Construction of 60ft. Wide Road in Sector 12. (Hawksbay Scheme - 42)
 : Road Work
 : Hawksbay
 : INFRA - 01

Particulars	Qty.	Unit	Rate		Amount (Rs.)
			In Figure	In Words	
<p>Concrete in contact with earth to be carried out with S.R.</p> <p>Steel formwork is to be used in all the items of R.C.C.</p>					
V GARRIAGE WAY					
Leveling the existing road surface.	204,031	Sft	2/-	Two Rupees only	408062/-
Subgrade Compaction upto an average depth of 6" by sheep foot roller and power roller with optimum moisture content to achieve minimum 90% modified S.H.T.O. density.	138,604	Sft	2/-	Two Rupees only	277208/-
Subgrade work for embankment from borrow pits including spreading in 6 inch layers, clod breaking, ramming, rolling & compaction by sheep foot / power roller to optimum moisture content 95-100% of modified S.H.T.O dry density complete, upto an average depth of 5 miles and lift upto 5 ft (in ordinary soil). Compacted depth will be considered for payment)	203,863	CR	15/-	Fifteen Rupees only	3057945/-
Applying priming coat or tack coat with approved binder at the required rate including cleaning the road surface thoroughly, heating to the required temperature and spraying the binder with pressure as specified etc. complete. (Prime Coat)	204,031	Sft	7/-	Seven Rupees only	1428217/-
Spreading to proper line and grade plant mixed Asphalt concrete paver finished (Hydraulic/ Electronic-control) according to specified job mix formula approved by the Engineer including rolling, finishing to proper line, setting, level and camber etc. complete. Rate includes applying tack coat with bitumen 80/100 penetration grade, all cost of materials, roller, T&P and carriage of materials from source of supply to plant and plant to site of work.	204,031	Sft	73/-	Seventy Three Rupees only	14894263/-
Subgrade Concrete plain including placing, compacting, curing and curing complete including screening and spreading of stone aggregate without shuttering. Ratio 1:3:6. (Under kerb blocks)	1,417	CR	87/-	Eighty Seven Rupees only	123279/-
Subgrade concrete plain including placing, compacting, curing and curing complete including screening and spreading of stone aggregate using partial wood shuttering. Ratio 1:3:6.	1,417	CR	100/-	One Hundred Rupees only	141700/-
Supplying Bitumen for Prime Coat i/c cartage upto site of work.	20	Ton	5000/-	Five Thousand Rupees only	100000/-

Particulars	Qty.	Unit	Rate		Amount (Rs.)
			In Figure	In Words	
<p>Providing, laying and spreading graded granular sub-base material upto any thickness in sub-base course in required grade and camber and compacted to minimum 98% modified AASHTO dry density by approved mechanical means (vibratory roller, road roller and smooth wheel rollers, etc) as per design specifications including watering, cartage of materials to site with all lead and lift, etc complete (actual compacted depth shall be considered for payment).</p>	25,504	Cft.	36/2	Thirty Six Rupees only	918144/-
<p>Providing, laying and spreading graded aggregate base course material upto any thickness in base course in required grade and camber and compacted to minimum 100% modified AASHTO dry density by approved mechanical means (vibratory roller, road roller and smooth wheel rollers, etc) as per design specifications including watering, cartage of materials to site with all lead and lift, etc complete (actual compacted depth shall be considered for payment).</p>	118,338	CR.	45/50	Forty Five Rupees Fifty Paise	5384379/-
<p>Providing & fixing in proper position pre-cast cement concrete road kerb block industrial make Envirocrete or any other of approved equivalent quality having minimum cylindrical strength of 3000 psi with a mix ratio leaner than 1:1-1/2:3 (1 cement : 1-1/2 sand : 3 fine crushed), using SR cement, size 12" (300mm) deep 12" (300mm) long 4" (100mm) thick on top and 1" (150mm) thick at bottom of approved shape & section, dry mix, hydraulically compressed, steam cured. Laying & jointing with 3/4" (20mm) thick cement sand mortar (1:3), deep ruled pointing on front and top and flush on back side i/c. curing etc. complete as per the directions of Engineer.</p>	5,668	Rft.	300/-	Three Hundred Rupees only.	1700400/-
<p>Removing of Edge Stone including cost of excavation, backfilling of excavated stuff and stacking salvaged material (serviceable) and disposing surplus material as directed by the Engineer.</p>	11,335	Rft.	10/-	Ten Rupees only.	113350/-
<p>Supplying, installation at any height, testing and commissioning of the following items of work (unless specifically stated otherwise) including all materials, labor, tools, plants, accessories, etc required for proper completion of each item in all respect including all lead and lift as per drawings, approved shop drawings, specification, miscellaneous details and instructions of Engineer.</p>					

10/1

Particulars	Qty.	Unit	Rate		Amount (Rs.)
			In Figure	In Words	
erecting and erecting as approved steel tubular pole 10 Meter long hot dip galvanized, street pole complete base plate, anchor L-bolt, nut washer, accessories as shown in the drawing with all installation accessories cover base plate and as per following specification or as approved. Wall thickness 4.0mm thick Pole bottom 150mm, Top 50mm Total 10Meter High. Rafter-1.0" x 0.7" 20mm thick -4 nos. Base plate 2'.0" x 2'.0" x 20mm thick -2 no's Inspection window with cover plate. Nos of holes in base plate- 4 nos. Length of MS hot dip galvanized bolt 3' ft x 3/4" dia and bar with nuts and washers-4 nos.	114	Nos.	65000/-	Only from thousand rupees only	7410000/-
Construction of RCC foundation for road lights pole as per following specification with 2" dia u-pvc pipe for cable entry complete with all installation accessories as approved. Excavation of soft/hard soil size 3'ft x 3'ft x 5'ft Rein Concrete (Ratio 1:4:8) size: 3' x 3' x 6" RCC foundation (Ratio 1:2:4) size 2'.6" x 2'.6" x 5.6" Steel bar 6'ft x 6'ft x 1/2" dia-4nos Rings 1/4" dia-5 Nos.	114	Nos.	12000/-	From thousand rupees only	1368000/-
Total Rs.					37324947/-

Three crore seventy three lac Twenty four thousand
 In Words
 Nine Hundred & forty seven only

K. Jayaram

CONTRACTOR

BILL OF QUANTITIES

Owner : Lyari Development Authority
 Project : Infrastructure Development Works at Hawksbay Scheme -42
 Work : Construction of 60ft. Wide Road in Sector 12. (Hawksbay Scheme - 42)
 Item : Construction of RCC Drain
 Location : Hawksbay
 No. : INFRA - 01


Particulars	Qty.	Unit	Rate		Amount (Rs.)
			In Figure	In Words	
<p>1. Cement Concrete in contact with earth to be carried out with S.R. Cement Rebar steel formwork is to be used in all the items of R.C.C. All concrete for R.C.C work shall be produced from approved batching plants only in the quantity required for immediate use.</p>					
RAIN					
Earth work excavation in irrigation channels, drains etc., dressed to designed section grades and profiles excavated material disposed off and finished including all lead & lift. (Ordinary Soil)	110,932	CR	10/-	Ten Only	11,09,320/-
Cement concrete plain including placing, compacting, finishing and curing, complete including screening and washing of stone aggregate without shuttering. (Using S.R.Cement) Ratio 1:4:8	8,666	CR	120/-	One Hundred Twenty Only	10,39,920/-
Providing Construction joints in concrete work of 9" wide corrugated PVC waterstop (with bulb) i.e. soldering, cost of material and labour etc. complete.	11,315	Rft.	140/-	One Hundred Forty Only	1,584,100/-
Providing Expansion joints in concrete work of 9" wide corrugated PVC waterstop (with bulb) i.e. soldering and providing wooden key of partial wood by cutting of planks to the exact shapes of structure and cost of material and labour etc. complete.	600	Rft.	150/-	One Hundred Fifty Only	90,000/-
Bitumen coating (two coat) to plastered or cement concrete surface.	49,607	SH	30/-	Thirty Only	14,882,100/-
Cement concrete mixed in batching plant having cylindrical crushing strength of 4000 psi using S.R. Cement, crushed aggregate 1" & down gauge & approved admixture (as per specifications of manufacturer), carriage from batching plant to site & work through approved transit mixers, pouring of concrete in formwork at site, as per directions of the Engineer, providing & removing of steel formwork, fair faced surface, curing, testing etc., complete)	40,117	Cft.	435/-	Four Hundred Thirty Five	17,450,895/-

Particulars	Qty.	Unit	Rate		Amount (Rs.)
			In Figure	In Words	
Cement concrete mixed in batching plant having cylindrical crushing strength of 4000 psi using 1:1:4 Cement, crushed aggregate 1" & down gauge & approved admixture (as per specifications of manufacturer), carriage from batching plant to site of work through approved transit mixers; pouring of concrete in formwork at site, as per directions of the Engineer, providing & removing of steel formwork, (on fair faced surface), curing, testing etc., (complete) (for Precast Slabs)	6,108	Cft.	430/-	Four Hundred Thirty only.	2626440/-
Providing & laying Deformed steel reinforcement bars having minimum yield stress of 60,000 psi with bent including the cost of straightening, cutting, bending, binding, wastage, and such overlaps as are not shown over the drawings, placing in position in cement concrete 1:2:4 precast or m.s.chairs, tying with binding wire, cost of chair and wires etc. in all kinds of RCC work in foundation, basement, plinth and ground floor of building including septic tank and under ground tank and in projections for future extension.	2,773	Cwt.	6045/-	Must Sixtyfour Twentyfive only.	16762785/-
Supplying, stacking & back filling in layers around structure approved granular materials, with all lead, watering & compacting as per the direction of the Engineer etc., complete. Compacted thickness will be considered for payment.	15,101	Cft.	8/50	Eight Paise Fifty Paise	128358/-
Total Rs.					42280028/-

Four Lac Twenty Two Lac Eighty Thousand
 In Words
 Twenty Eight Only

[Signature]
 CONTRACTOR

[Signature]




M. Pongad Chohan Adho
 5079
 5 21-6-12
 5 21-6-12
 5 21-6-12

ASSISTANT SUPERINTENDENT OF STAMP
 STAMP OFFICE CITY COURTS
 KARACHI
 21 JUN 2012

CONTRACT AGREEMENT

THIS CONTRACT AGREEMENT (Hereinafter called the "Agreement") made on the 28th day of the June, 2012 between LYARI DEVELOPMENT AUTHORITY (LDA), 4th Floor, Civic Center, Sir Shah Suleman Road, Gulshan-e-Iqbal, Karachi, (hereafter called the "Employer") of the one Part and M/s. Riasat Brothers, Flat No: 204-206, Shahida Mension Commercial Area, Block 2, P.E.C.H.S Karachi. (Hereafter called the Contractor) of the other part.

WHERE AS The employer is desirous that certain works, viz CONSTRUCTION OF 60' WIDE ROAD IN BLOCK 12 HAWKS BAY ROAD IN HAWKS BAY, SCHEME 42 (CONTRACT NO INFRA-001) should be executed by the Contractor and has accepted a Bid by the Contractor for the execution and completion of such works and remedying of any



ASSISTANT SUPERINTENDENT OF STAMPS
 STAMP OFFICE, CITY COURTS,
 KARACHI
 28 JUN 2012


M. Anjum Q. Khan
 28/6/12
 22:6:12
 22:6:12
 22:6:12

NOW this agreement witnessed as follows:

1. In this agreement, words and expressions shall have the same meanings as are respectively assigned to them in the Conditions of Contract hereinafter referred to.
2. The following documents after incorporating addenda, if any, except those parts relating to instructions to Bidders shall be deemed to form and be read and construed as part of this agreement, viz:
 - a) The Contract Agreement (if completed);
 - b) The Letter of Acceptance;
 - c) The Completed Form of Bid;
 - d) Special Stipulations (Appendix-A to Bid);
 - e) The Particular Conditions of Contract, Part-II;
 - f) Specifications-Special Provisions;
 - g) Specifications-Technical Provisions;
 - h) The General Conditions-Part-I;
 - i) The Priced Bill of Quantities;

378067

378067




TAMP OFFICE
 KARACHI
 Zafar Ahmed
 Advocate
 15 Dated 28/6/12
 15 225 Dated 28/6/12
 15 Dated 28/6/12

ASSISTANT SUPERINTENDENT OF STAMPS
 STAMP OFFICE CITY COURTS,
 KARACHI
 28 JUN 2012

3. In consideration of the payments to be made by the Employer to the Contractor as hereinafter mentioned, the Contractor hereby covenants with the Employer to execute and complete the Works and remedy defects therein in conformity and in all respects with the provisions of the Contract.

4. The Employer hereby covenants to pay the Contractor, in consideration of the execution and completion of the works as per provisions of the Contract, the Contract price or such other sum as may become payable under the provisions of the Contract at the times and in the manner prescribed by the Contract.



FORM NO. 1
15
205

Riyaz Ahmad
Lahore
Dated 28/6/12
Dated 28/6/12

ASSISTANT SUPERINTENDENT OF STAMPS
STAMP OFFICE, DISTRICT COURTS
KARACHI

28 JUN 2012

IN WITNESS WHEREOF, the parties hereto have caused this agreement to be executed on the day, month and year first before written in accordance with their respective laws.

Signature of the Contractor

RIASAT BROTHERS

(Seal) Proprietor

Signature of the Employer

EXECUTIVE ENGINEER
Division
Lyari Development Authority

Signed, Sealed and Delivered in the presence of:

Witness:

Haji Sirajuddin & Brothers


(Name, Title and Address)

Witness:

(Name, Title and Address)

378062

Sajid / Utulani No. 314 Dated 28/6/12



Tajam Ahmad
 Advocate
 15 24/6/12
 15 23/6/12
 15 24/6/12

ASSISTANT SUPERINTENDENT OF STAMPS
 STAMP OFFICE CITY COURTS,
 KARACHI


28 JUN 2012

CONTRACT AGREEMENT

"CONSTRUCTION OF 60' WIDE ROAD IN BLOCK 12 IN HAWKS BAY (INFRA - 001) BY
M/S. RIASAT BROTHERS

378055

2,000/- ... 28/6/12



Rupees **50**

2012

ASSISTANT SUPERINTENDENT OF STAMPS
STAMP OFFICE CITY COURTS,
LAHORE

28 JUN 2012

Rafiq Ahmad
Advocate
15
225
15
28/6/12
28/6/12
28/6/12


CONTRACT AGREEMENT

**"CONSTRUCTION OF 60' WIDE ROAD IN BLOCK 12 IN HAWKS BAY (INFRA - 001) BY
M/S. RIASAT BROTHERS**

2
or
y-III

378065

307/00/1-31/17-2002-25/17

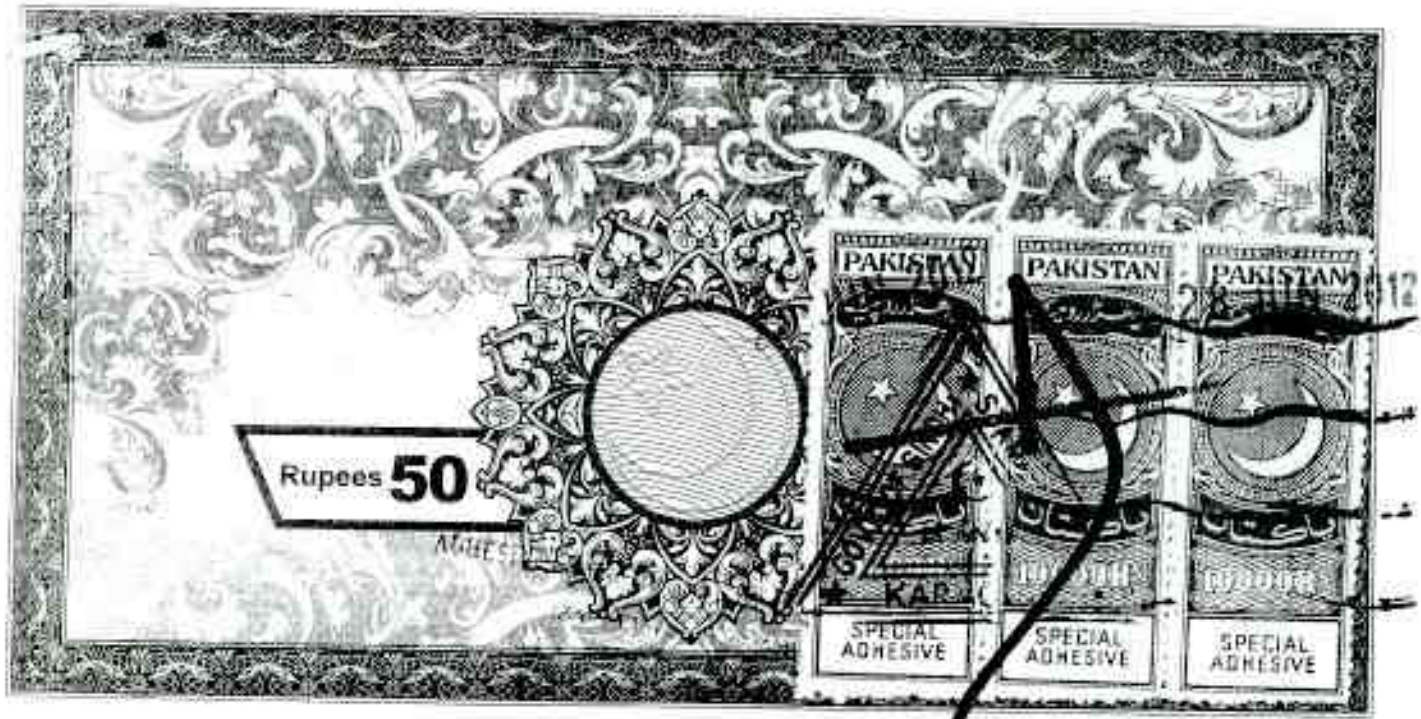

KARACHI
 Tufan Ahmed
 Advocate
 15 23/6/12
 225 20/6/11
 15 28/6/11

ASSISTANT SUPERINTENDENT OF STAMPS
 STAMP OFFICE, CITY COURTS,
 KARACHI
 28 JUN 2012


CONTRACT AGREEMENT

"CONSTRUCTION OF 60' WIDE ROAD IN BLOCK 12 IN HAWKS BAY (INFRA - 001) BY

M/S. RIASAT BROTHERS

378065

378065 / 317 25/97



STAMP OFFICE KARACHI
 15
 225
 15
 28/6/12
 28/6/12
 28/6/12
 28/6/12

ASSISTANT SUPERINTENDENT OF STAMPS
 STAMP OFFICE CITY COURTS,
 KARACHI

28 JUN 2012

CONTRACT AGREEMENT


"CONSTRUCTION OF 60' WIDE ROAD IN BLOCK 12 IN HAWKS BAY (INFRA - 001) BY

M/S. RIASAT BROTHERS

2

215201

2520/1/2012 No. 317 Dated 28/4/12



2012

ASSISTANT SUPERINTENDENT OF STAMPS
STAMP OFFICE, CITY COURTS,
KARACHI
28 JUN 2012

KARACHI
Rafiq Ahmad
Shahid
15 Dated 28/6/12
225 Dated 28/4/12
15 28/4/12

28/6/12 **CONTRACT AGREEMENT**

**"CONSTRUCTION OF 60' WIDE ROAD IN BLOCK 12 IN HAWKS BAY (INFRA - 001) BY
M/S. RIASAT BROTHERS**

2
1



LYARI DEVELOPMENT AUTHORITY
OFFICE OF THE EXECUTIVE ENGINEER HAWKS BAY DIVISION-III,
1ST FLOOR, APOLO CENTRE, ADJECENT TO BEHERIA GRAYVEYARD
MAIN DALMIA ROAD, Karachi. Phone:021-9230985

No. EE/HBD-III/INFRA-006/LDA/2012/33

Dated: 2012

The Director (CB), SPPRA,
Block No. 08, Sindh Secretariat No. 4-A,
Court Road Karachi

Subject: CONTRACT EVALUATION FORM FOR THE WORK OF
"REHABILITATION OF INFRASTRUCTURE WORKS IN SECTOR 3 &
3-A IN HAWKS BAY SCHEME- 42, LDA CONTRACT NO: INFRA-006.

I am directed to enclose herewith Contract Evaluation Form for the subject work. The supporting documents of contract agreement are also attached as desired in prescribed Performa, wherein Letter of award, Form of Contract and bill of quantity are available for your ready reference & record.


Executive Engineer
Hawksbay Division-III
Lyari Development Authority

Copy to the:

1. The Chief Engineer, LDA.
2. The Superintending Engineer, LDA.
3. The Director (F&A), LDA.
4. The PSO to Director General, LDA.
5. M/s. Osmani & company (Pvt) Ltd.

SPPK

No. _____

Dated _____

Sindh Public Engg. Reg. Comm.

Regulatory Authority Govt. of Sindh

16.7
Civ
Mun

SINDH PUBLIC PROCUREMENT REGULATORY AUTHORITY

CONTRACT EVALUATION FORM

1	NAME OF THE ORGANIZATION	LYARI DEVELOPMENT AUTHORITY LOCAL GOVERNMENT
2	PROVINCIAL / LOCAL GOVERNMENT / OTHER	
3	TITLE OF CONTRACT	Rehabilitation of infrastructure works in Sector 3 & 3-A in Hawksbay INFRA-006
4	TENDER NO	
5	BRIEF DESCRIPTION OF CONTRACT	As Above
6	FORUM THAT APPROVED THE SCHEME	DDWP
7	TENDER ESTIMATED VALUE	Rs. 7,58,25,862/-
8	ENGINEERING ESTIMATE (FOR CIVIL WORKS ONLY)	Rs. 7,56,25,862/-
9	ESTIMATED COMPLETION PERIOD	Four (04) Months
10	TENDER OPENED ON (DATE & TIME)	04-06-2012
11	NUMBER OF TENDER DOCUMENTS SOLD (ATTACH LIST)	04 Nos
12	NUMBER OF BIDS RECEIVED	04 Nos
13	NUMBER OF BIDDERS PRESENT AT THE TIME OF OPENING	List enclosed
14	BID EVALUATION REPORT (ATTACH A COPY)	Enclosed
15	NAME & ADDRESS OF THE SUCCESSFUL BIDDER	M/s. Ziaul Haq & Sons, A-103, Block "N" North Nazimabad, Karachi.
16	CONTRACT AWARD PRICE	Rs. 7,32,69,458/-
17	RANKING OF SUCCESSFUL BIDDER IN EVALUATION REPORT (i.e 1 st , 2 nd , 3 rd EVALUATED BID)	1 st Lowest
18	METHOD OF PROCUREMENT a) SINGLE STAGE ONE ENVELOPE PROCEDURE b) SINGLE STAGE TWO ENVELOPE PROCEDURE c) TWO STAGE BIDDING PROCEDURE d) TWO STAGE TWO ENVELOPE PROCEDURE	Single envelope procedure

19	APPROVING AUTHORITY FOR AWARD OF CONTRACT	Director General, LDA
20	WHETHER PROCUREMENT WAS INCLUDED IN ANNUAL PROCUREMENT PLAN	Yes
21	ADVERTISEMENT SPPRA WEBSITE	The News, Daily Jang, Kawish dated 11 th May 2012. 8260/2012
22	NEWSPAPERS	Domestic/Local
23	NATURE OF CONTRACT WHETHER QUALIFICATION CRITERIA WAS INCLUDED IN BIDDING DOCUMENTS?	Yes
24	WHETHER EVALUATION CRITERIA BID WAS INCLUDED IN BIDDING DOCUMENTS?	Open competition bidding method was used.
25	WHETHER APPROVAL OF COMPETENT AUTHORITY WAS OBTAINED FOR USING A METHOD OTHER THAN COMPETITIVE BIDDING?	Yes
26	WAS BID SECURITY OBTAINED FROM ALL THE BIDDERS?	Yes
27	WHETHER THE SUCCESSFUL BID WAS LOWEST EVALUATED BID/BEST EVALUATED BID?	Yes
28	WHETHER THE SUCCESSFUL BIDDER WAS TECHNICALLY COMPLAINT?	
29	WHETHER THE NAMES OF THE BIDDERS AND THEIR QUOTED PRICES WERE READ OUT AT THE TIME OF OPENING OF BIDS?	Yes
30	WHETHER EVALUATION REPORT WAS GIVEN TO BIDDERS BEFORE THE AWARD OF CONTRACT?	
31	ANY COMPLAINT RECEIVED	No
32	ANY DEVIATION FROM SPECIFICATIONS GIVEN IN THE TENDER NOTICE/DOCUMENTS	No
33	WAS THE EXTENSION MADE IN RESPONSE TIME?	No
34	ANY DEVIATION FROM QUALIFICATION CRITERIA	No

35

WAS IT ASSURED BY THE PROCURING AGENCY THAT THE SELECTED FIRM IS NOT BLACK LISTED?

Yes

36

WAS A VISIT MADE BY ANY OFFICER/OFFICIAL OF THE PROCURING AGENCY TO THE SUPPLIERS PREMISES IN CONNECTION WITH THE PROCUREMENT? DETAILS TO BE ASCERTAINED REGARDING FINANCES OF VISIT IF ABROAD

No

37

WERE PROPER SAFEGUARD PROVIDED ON MOBILIZATION ADVANCE PAYMENT IN THE CONTRACT (BANK GUARANTEE ETC)

Yes

38

SPECIAL CONDITIONS IF ANY

No

39

DATE OF AWARD OF CONTRACT

29th June 2012

40

SIGNATURE & OFFICIAL STAMP OF AUTHORIZED OFFICER


EXECUTIVE ENGINEER
 Hawksbay Division
 Lyari Development Authority

BID EVALUATION REPORT

1. Name of Agency : Lyari Development Authority
2. Tender Reference No : Infra-006
3. Tender description/Name of : Rehabilitation of Infrastructure works in sector 3 & 3-A in Hawksbay, Scheme 42
4. Method of Procurement : Single Envelop procedure
5. Tender published : The News, Daily Jang, Kawish dated 11th May 2012.
6. Total Bid sold : 04 Nos
7. total bid received : 04 Nos
8. Technical Bid Opening date : 04th June 2012.
9. No of Bid technically qualified : 04 Nos
10. Bid(s) Rejected : NA
11. Financial bid opening date : 04th June 2012.
12. **Bid Evaluation Report :**

S.#	Name of Firm/Bidder	Cost offered by Bidder	Ranking in term of cost	Comparasion of Estimated Cost	Reasons for acceptance /rejection	Remarks
1	2	3	4	5	6	7
01	M/s Ziaul Haq & sons	Rs. 7,32,69,468/-	1 st Lowest		Accepted being 1 st lowest	
02	M/s. Malik Zaheer Khan	Rs. 7,43,22,110/-	2 nd Lowest			
03	M/s. Abdul Sattar & company	Rs. 7,49,51,328/-				
04	M/s. Kaim Khani Competition International	Not quoted				

Deputy Director (F&A)
Member

Deputy Director (F&A)
Lyari Development Authority

Consultant
Member

Executive Engineer
Member

Executive Engineer
Chairman

EXECUTIVE ENGINEER
Hawksbay Division
Lyari Development Authority



LYARI DEVELOPMENT AUTHORITY
OFFICE OF THE EXECUTIVE ENGINEER, HAWKS BAY-III

No. EE/HBD-III/LDA/Infra-006/2012/227

Dated 21st June, 2012

M/s. S. Ziaul Haq & Sons,
A-103, Block 'N',
North Nazimabad,
Karachi.

WORK ORDER

Sub: REHABILITATION OF INFRASTRUCTURE WORKS IN SECTOR 3 & 3-A IN HAWKS BAY, SCHEME 42 (CONTRACT NO: INFRA-006)

With reference to letter of acceptance for the subject work amounting to Rs. 7,32,69,468/- (Rupees Seven Crore Thirty Two Lacs Sixty Nine thousand Four hundred Sixty Eight only) issued vide this office letter No. EE/HBD-III/Infra-006/110 dated 26th June, 2012, you are requested to make immediate arrangements to start the work within (14) Fourteen days from the date of issue of this letter and complete the same within the period stipulated for completion of work in the tender documents i.e (06) Six months. The time allowed for completion of work shall be considered as the essence of contract.

Please note that the work should be carried out strictly in accordance with the drawing, design, specification, terms & conditions agreed to as per contract agreement of above mentioned work. In this connection please get in touch with the Resident Engineer of the consultant M/s. Osmani & Company (Pvt) Ltd. and Assistant Executive Engineer of this division.


The execution of work and quality control shall be supervised by the consultant M/s. Osmani & Co (Pvt) Ltd and payment towards work done shall be released after verification of bills by the consultant.

In case you failed, to commence the work within 14 (fourteen) days from the date of issue of this letter, action under the relevant clauses of the contract agreement shall be initiated against you.


Executive Engineer
Hawks Bay Division-III

Copy for information to:

1. The Director (F&A), LDA
2. The Chief Engineer, LDA
3. The Superintending Engineer, LDA
4. M/s. Osmani & Company (Pvt) Ltd.
5. The Resident Engineer, M/s. OCL
6. The PS to Director General, LDA



STAMP OFFICE KARACHI

S. Ziaul Haq & Sons


29.6.2012
29.6.2012
29.6.2012

S. Ziaul Haq & Sons
29/6/12

CONTRACT AGREEMENT

THIS CONTRACT AGREEMENT (Hereinafter called the "Agreement") made on the 29th day of the June, 2012 between LYARI DEVELOPMENT AUTHORITY (LDA), 4th Floor, Civic Center, Sir Shah Suleman Road, Gulshan-e-Iqbal, Karachi, (hereafter called the "Employer") of the one Part and M/s. S. Ziaul Haq & Sons, A-103, Block N, North Nazimabad, Karachi. (Hereafter called the Contractor) of the other part.

WHERE AS The employer is desirous that certain works, viz REHABILITATION OF INFRASTRUCTURE WORKS IN SECTOR 3 & 3-A IN HAWKS BAY, SCHEME 42, (CONTRACT NO INFRA-001) should be executed by the Contractor and has accepted a Bid by the Contractor for the execution and completion of such works and remedying of any defects therein




TAMR C
 S. Zaad Has 25m

27.6.2012
 27.6.2012
 No. 27.6.2012

NOW this agreement witnessed as follows:


1. In this agreement, words and expressions shall have the same meanings as are respectively assigned to them in the Conditions of Contract hereinafter referred to.
2. The following documents after incorporating addenda, if any, except those parts relating to instructions to Bidders shall be deemed to form and be read and construed as part of this agreement, viz:
 - a) The Contract Agreement (if completed);
 - b) The Letter of Acceptance;
 - c) The Completed Form of Bid;
 - d) Special Stipulations (Appendix-A to Bid);
 - e) The Particular Conditions of Contract, Part-II;
 - f) Specifications-Special Provisions;
 - g) Specifications-Technical Provisions;
 - h) The General Conditions-Part-I;



STAMP
 S. Zawal / H 995803
 27.6.2012
 29.6.2012
 27.6.2012
 E. No.
 [Signature]

3. In consideration of the payments to be made by the Employer to the Contractor as hereinafter mentioned, the Contractor hereby covenants with the Employer to execute and complete the Works and remedy defects therein in conformity and in all respects with the provisions of the Contract.

4. The Employer hereby covenants to pay the Contractor, in consideration of the execution and completion of the works as per provisions of the Contract, the Contract price or such other sum as may become payable under the provisions of the Contract at the times and in the manner prescribed by the Contract.



STAMP
 3.200/1/1/2501
 27.6.2012
 27.6.2012
 E.No. 27.6.2012

IN WITNESS WHEREOF, the parties hereto have caused this agreement to be executed on the 27th day of June and year first before written in accordance with their respective laws.

Signature of the Contractor



H. SIRAJUDDIN & BROTHERS
 Proprietor
 (Seal)

Signature of the Employer


 EXECUTIVE ENGINEER
 Hawksbay Division
 Lyari Development Authority

Signed, Sealed and Delivered in the presence of:

Witness:


HAJI SIRAJUDDIN & BROTHERS
 (Name, Title and Address)

Witness:


 (Name, Title and Address)

STAMP OF
DATE
M. No.
V.
D.C.
E. No.

Signature
20/10/11

CONTRACT AGREEMENT

"REHABILITATION OF INFRASTRUCTURE WORKS IN SECTOR 3 & 3-A IN HAWKS BAY,
SCHEME 42"
(CONTRACT NO: INFRA-00C)

Signature

Signature

STAMP
No. 1000
Date: 10/10/11
By: [Signature]

[Handwritten Signature]
2/16/11

CONTRACT AGREEMENT

"REHABILITATION OF INFRASTRUCTURE WORKS IN SECTOR 3 & 3-A IN HAWKS BAY,
SCHEME 42"
(CONTRACT NO: INFRA-000)

[Handwritten Signature]

[Handwritten Signature]

STAMP
Date: 2.12.2011
No. _____
No. _____
No. _____
E.No. _____

Signature
21/12

CONTRACT AGREEMENT

REHABILITATION OF INFRASTRUCTURE WORKS IN SECTOR 3 & 3-A IN HAWKS BAY,
SCHEME 42"
(CONTRACT NO: INFRA-005)

Signature

Signature

STAMP OF
MUNICIPALITY
NO.
OFFICE
E. No.

[Handwritten signature]

CONTRACT AGREEMENT

"REHABILITATION OF INFRASTRUCTURE WORKS IN SECTOR 3 & 3-A IN HAWKS BAY,
SCHEME 42"
(CONTRACT NO: INFRA-000)

[Handwritten signature]

[Handwritten signature]

STAMP

Mr. [unclear] [unclear]
[unclear]
[unclear]
[unclear]
[unclear]

Mr. [unclear] [unclear]
[unclear]

CONTRACT AGREEMENT

"REHABILITATION OF INFRASTRUCTURE WORKS IN SECTOR 3 & 3-A IN HAWKS BAY,
SCHEME 42"
(CONTRACT NO: INFRA-006)

[Handwritten signature]

[Handwritten signature]

STAMP OF

No.

M/s

Dist.

Office

S. No.

Signature
6/5/12

CONTRACT AGREEMENT

"REHABILITATION OF INFRASTRUCTURE WORKS IN SECTOR 3 & 3-A IN HAWKS BAY,
SCHEME 42"
(CONTRACT NO: INFRA-005)

Signature

Signature

STAMP
Date: 10/10/2011
Time: 11:30 AM
E. No. 10/10/2011

[Signature]

CONTRACT AGREEMENT

"REHABILITATION OF INFRASTRUCTURE WORKS IN SECTOR 3 & 3-A IN HAWKS BAY,
SCHEME 42"
(CONTRACT NO: INFRA-000)

[Signature]

[Signature]

STAMP
No. _____
Date _____
E. No. _____

Dr. Gyanendra
12/6/11

CONTRACT AGREEMENT

"REHABILITATION OF INFRASTRUCTURE WORKS IN SECTOR 3 & 3-A IN HAWKS BAY,
SCHEME 42"
(CONTRACT NO: INFRA-000)



STAMP ON
Date: 21/11/10
By: [Signature]
E. No. [Blank]

[Signature]
21/11/10

CONTRACT AGREEMENT

"REHABILITATION OF INFRASTRUCTURE WORKS IN SECTOR 3 & 3-A IN HAWKS BAY,
SCHEME 42"
(CONTRACT NO: INFRA-005)

[Signature]

[Signature]

STAMP
No. _____
Date _____
Name _____
Signature _____

Signature
15/6/11

CONTRACT AGREEMENT

"REHABILITATION OF INFRASTRUCTURE WORKS IN SECTOR 3 & 3-A IN HAWKS BAY,
SCHEME 42"
(CONTRACT NO: INFRA-000)

Signature

Signature

STAMP
No. 2
Date 10/10/2014
E. No.

[Handwritten signature]

CONTRACT AGREEMENT

"REHABILITATION OF INFRASTRUCTURE WORKS IN SECTOR 3 & 3-A IN HAWKS BAY,
SCHEME 42"
(CONTRACT NO. INFRA-006)

[Handwritten signature]

[Handwritten signature]

STAMP

to
M
on
E No.

Signature
05/11/11

CONTRACT AGREEMENT

" REHABILITATION OF INFRASTRUCTURE WORKS IN SECTOR 3 & 3-A IN HAWKS BAY,
SCHEME 42"
(CONTRACT NO: INFRA-00C)

Signature

Signature

STATE OF NEW SOUTH WALES
M...
P...
V...
D...
E. No. ...

in Office Tenders
2/6/11

CONTRACT AGREEMENT

"REHABILITATION OF INFRASTRUCTURE WORKS IN SECTOR 3 & 3-A IN HAWKSBAY,
SCHEME 42"
(CONTRACT NO: INFRA-005)



STAMP OF
H
M
U
SEC
E NO

in Office Handwritten
2/6/12

CONTRACT AGREEMENT

"REHABILITATION OF INFRASTRUCTURE WORKS IN SECTOR 3 & 3-A IN HAWKS BAY"
SCHEME 42"
(CONTRACT NO: INFRA-008)



STAMP OF THE
[Faint stamp text]
[Faint signature]
[Faint date]

CONTRACT AGREEMENT

"REHABILITATION OF INFRASTRUCTURE WORKS IN SECTOR 3 & 3-A IN HAWKSBAY,
SCHEME 42"
(CONTRACT NO: INFRA-006)

[Handwritten signature]

[Handwritten signature]

STAMP
No. 1
Date: 1/1/2000
M:
M:
SEC:
E. 110


Dr. [Signature]
1/1/00

CONTRACT AGREEMENT

"REHABILITATION OF INFRASTRUCTURE WORKS IN SECTOR 3 & 3-A IN HAWKS BAY,
SCHEME 42"
(CONTRACT NO: INFRA-000)

[Signature]

[Signature]



STAMP
Name: S. S. A. Hossain
M:
V:
G:
E. No:

S. S. A. Hossain
5/16/11

CONTRACT AGREEMENT

"REHABILITATION OF INFRASTRUCTURE WORKS IN SECTOR 3 & 3-A IN HAWKSBAY,
SCHEME 42"
(CONTRACT NO: INFRA-006)

STAMP OF THE CONTRACTOR
Name: _____
Address: _____
City: _____
State: _____
E. No. _____

Signature
2/6/10

CONTRACT AGREEMENT

"REHABILITATION OF INFRASTRUCTURE WORKS IN SECTOR 3 & 3-A IN HAWKS BAY,
SCHEME 42"
(CONTRACT NO: INFRA-000)

Signature

Signature

STATE OF
No. 1
No. 2
No. 3
No. 4
No. 5
No. 6
No. 7
No. 8
No. 9
No. 10
No. 11
No. 12
No. 13
No. 14
No. 15
No. 16
No. 17
No. 18
No. 19
No. 20
No. 21
No. 22
No. 23
No. 24
No. 25
No. 26
No. 27
No. 28
No. 29
No. 30
No. 31
No. 32
No. 33
No. 34
No. 35
No. 36
No. 37
No. 38
No. 39
No. 40
No. 41
No. 42
No. 43
No. 44
No. 45
No. 46
No. 47
No. 48
No. 49
No. 50
No. 51
No. 52
No. 53
No. 54
No. 55
No. 56
No. 57
No. 58
No. 59
No. 60
No. 61
No. 62
No. 63
No. 64
No. 65
No. 66
No. 67
No. 68
No. 69
No. 70
No. 71
No. 72
No. 73
No. 74
No. 75
No. 76
No. 77
No. 78
No. 79
No. 80
No. 81
No. 82
No. 83
No. 84
No. 85
No. 86
No. 87
No. 88
No. 89
No. 90
No. 91
No. 92
No. 93
No. 94
No. 95
No. 96
No. 97
No. 98
No. 99
No. 100

Dr. Brijendra Kumar
28/6/11

CONTRACT AGREEMENT

"REHABILITATION OF INFRASTRUCTURE WORKS IN SECTOR 3 & 3-A IN HAWKS BAY,
SCHEME 42"
(CONTRACT NO: INFRA-006)

[Handwritten signature]

[Handwritten signature]

STAMP
No. 9
dt.
V.
at
E. No.

Sanjiv Kumar
2/6/11

CONTRACT AGREEMENT

"REHABILITATION OF INFRASTRUCTURE WORKS IN SECTOR 3 & 3-A IN HAWKS BAY,
SCHEME 42"
(CONTRACT NO: INFRA-680)

STAMP OF
No.
No.
No.
DCS
E. No.

Signature
20/10

CONTRACT AGREEMENT

"REHABILITATION OF INFRASTRUCTURE WORKS IN SECTOR 3 & 3-A IN HAWKS BAY,
SCHEME 42"
(CONTRACT NO: INFRA-005)

Signature

Signature

STAMP OF
No. 250 - 250 1/2
No.
No.
No. C.
E. No.

Sanjiv Kumar
2/1/11

CONTRACT AGREEMENT

REHABILITATION OF INFRASTRUCTURE WORKS IN SECTOR 3 & 3-A IN HAWKS BAY
SCHEME 42"
(CONTRACT NO: INFRA-005)

[Handwritten signature]

[Handwritten signature]

STATE OF
No. 100
No. 100
No. 100
No. 100
No. 100

Handwritten signature
2/16/12

CONTRACT AGREEMENT

"REHABILITATION OF INFRASTRUCTURE WORKS IN SECTOR 3 & 3-A IN HAWKS BAY,
SCHEME 42"
(CONTRACT NO: INFRA-006)

Handwritten signature

Handwritten signature

STAMP OF THE...
No. ...
V. ...
V. ...
GR. ...
E. No. ...

the Office Director
2/16/11

CONTRACT AGREEMENT

"REHABILITATION OF INFRASTRUCTURE WORKS IN SECTOR 3 & 3-A IN HAWKS BAY"
SCHEME 42"
(CONTRACT NO: INFRA-005)



STAMP OF
M. No. _____
V. No. _____
S. No. _____
Sanjay Kumar
15/6/11

CONTRACT AGREEMENT

"REHABILITATION OF INFRASTRUCTURE WORKS IN SECTOR 3 & 3-A IN HAWKS BAY,
SCHEME 42"
(CONTRACT NO. INFRA-606)

[Handwritten signature]

[Handwritten signature]

STAMP
No.
M.
D.
C.
E. No.

[Handwritten signature]

CONTRACT AGREEMENT

"REHABILITATION OF INFRASTRUCTURE WORKS IN SECTOR 3 & 3-A IN HAWKS BAY,
SCHEME 42"
(CONTRACT NO. INFRA-000)

[Handwritten mark]

[Handwritten mark]

STAMP OF
No. 2
Date
No.
Date
E. No.

[Handwritten signature]

CONTRACT AGREEMENT

"REHABILITATION OF INFRASTRUCTURE WORKS IN SECTOR 3 & 3-A IN HAWKS BAY,
SCHEME 42"
(CONTRACT NO: INFRA-000)

[Handwritten mark]

[Handwritten mark]

STAMP

No.

Mo.

Y.

Price

C. No.

[Handwritten signature]
15/6/11

CONTRACT AGREEMENT

"REHABILITATION OF INFRASTRUCTURE WORKS IN SECTOR 3 & 3-A IN HAWKS BAY,
SCHEME 42"
(CONTRACT NO: INFRA-006)

[Handwritten signature]

[Handwritten signature]

STAMP
M...
ME...
M...
D...
E. No. →

via Office London
2/6/12

CONTRACT AGREEMENT

"REHABILITATION OF INFRASTRUCTURE WORKS IN SECTOR 3 & 3-A IN HAWKS BAY,
SCHEME 42"
(CONTRACT NO: INFRA-000)



STAMP
NO.
E. No.

Signature

CONTRACT AGREEMENT

"REHABILITATION OF INFRASTRUCTURE WORKS IN SECTOR 3 & 3-A IN HAWKSBAY,
SCHEME 42"
(CONTRACT NO: INFRA-005)

Signature

Signature

STAMP OF
No. 2
No.
No.
No.
L.No.

Signature
2/6/12

CONTRACT AGREEMENT

"REHABILITATION OF INFRASTRUCTURE WORKS IN SECTOR 3 & 3-A IN HAWKS BAY,
SCHEME 42"
(CONTRACT NO: INFRA-000)

Signature

Signature

STAMP
No. 1000
Date 25/6/11
E. No. 1000
[Signature]

CONTRACT AGREEMENT

"REHABILITATION OF INFRASTRUCTURE WORKS IN SECTOR 3 & 3-A IN HAWKS BAY,
SCHEME 42"
(CONTRACT NO: INFRA-005)

[Signature]

[Signature]

STAMP
Date: _____
By: _____
E. No. _____

[Handwritten signature]
2/16/10

CONTRACT AGREEMENT

"REHABILITATION OF INFRASTRUCTURE WORKS IN SECTOR 3 & 3-A IN HAWKS BAY,
SCHEME 42"
(CONTRACT NO: INFRA-006)

[Handwritten signature]

[Handwritten signature]

STAMP OF
[Faint stamp text]
E. No. _____

Dr. Brijendra Kishore
27/6/12

CONTRACT AGREEMENT

"REHABILITATION OF INFRASTRUCTURE WORKS IN SECTOR 3 & 3-A IN HAWKS BAY,
SCHEME 42"
(CONTRACT NO: INFRA-000)



STAMP
No.
Date
U
D
E. No.

Sanjiv Kumar
5/14/11

CONTRACT AGREEMENT

"REHABILITATION OF INFRASTRUCTURE WORKS IN SECTOR 3 & 3-A IN HAWKS BAY,
SCHEME 42"
(CONTRACT NO: INFRA-000)



STAMP
No. _____
Date _____
By _____
For _____
E. No. _____

Office Number
2/16/11

CONTRACT AGREEMENT

"REHABILITATION OF INFRASTRUCTURE WORKS IN SECTOR 3 & 3-A IN HAWKS BAY"
SCHEME 42"
(CONTRACT NO: INFRA-000)



STAMP
No. _____
Date _____
Office _____
E. No. _____

[Handwritten Signature]
5/16/12

CONTRACT AGREEMENT

"REHABILITATION OF INFRASTRUCTURE WORKS IN SECTOR 3 & 3-A IN HAWKS BAY,
SCHEME 42"
(CONTRACT NO: INFRA-005)

[Handwritten Signature]

[Handwritten Signature]

STAMP
No.
No.
No.
No.
No.

[Faint handwritten text and lines]

[Signature]
2/16/11

CONTRACT AGREEMENT

"REHABILITATION OF INFRASTRUCTURE WORKS IN SECTOR 3 & 3-A IN HAWKS BAY,
SCHEME 42"
(CONTRACT NO: INFRA-006)

[Handwritten mark]

[Handwritten mark]

STAMP

No.

Date

By

Official

E. No.

Signature
3/16/11

CONTRACT AGREEMENT

"REHABILITATION OF INFRASTRUCTURE WORKS IN SECTOR 3 & 3-A IN HAWKS BAY,
SCHEME 42"
(CONTRACT NO: INFRA-000)

Signature

Signature

STAMP
to
W/
V/
OFF
E. No.


Mr. [Signature]
2/6/77

CONTRACT AGREEMENT

"REHABILITATION OF INFRASTRUCTURE WORKS IN SECTOR 3 & 3-A IN HAWKS BAY"
SCHEME 42"
(CONTRACT NO: INFRA-003)

[Signature]

[Signature]



STAMP OF THE OFFICE OF THE CHIEF EXECUTIVE OFFICER
 Date: 25/04/12
 No. 25/04/12
 City: Islamabad
 E. No. 25/04/12


Signature
 25/4/12

CONTRACT AGREEMENT

"REHABILITATION OF INFRASTRUCTURE WORKS IN SECTOR 3 & 3-A IN HAWKS BAY,
 SCHEME 42"
(CONTRACT NO: INFRA-800)

Signature

Signature



STAMP OF THE GOVERNMENT OF PAKISTAN
Date: 20/06/2012
No. _____
W. _____
OF _____
E. No. _____


Signature
20/6/12

CONTRACT AGREEMENT

**"REHABILITATION OF INFRASTRUCTURE WORKS IN SECTOR 3 & 3-A IN HAWKS BAY,
SCHEME 42"**
(CONTRACT NO: INFRA-000)

Signature

Signature



STAMP OFFICE DISTRICT HEADQUARTERS KARACHI

Issued to S. Zia ul Haq Sar

NR/No. 276/2012

Via 276/2012

E. No. 276/2012


S. Zia ul Haq Sar
27/6/12

CONTRACT AGREEMENT

"REHABILITATION OF INFRASTRUCTURE WORKS IN SECTOR 3 & 3-A IN HAWKS BAY,
SCHEME 42"
(CONTRACT NO: INFRA-006)

[Handwritten signature]

[Handwritten signature]



STAMP OFFICE KARACHI

Issued to S. Zia ul Haq Sars

REC-5

Via

on 25/6/2012

E. No.

25/6/2012

25/6/2012

25/6/2012


S. Zia ul Haq Sars
25/6/12

CONTRACT AGREEMENT

"REHABILITATION OF INFRASTRUCTURE WORKS IN SECTOR 3 & 3-A IN HAWKS BAY,
SCHEME 42"
(CONTRACT NO: INFRA-003)

[Handwritten mark]

[Handwritten mark]



STAMP OFFICE DISTRICT OFFICE KARACHI

Invoice No. S-2/a of 16/02/2012

MR. / 27.6.2012

FOR / 27.6.2012

E.No. 27.6.2012


 Mr. [Name]

CONTRACT AGREEMENT

"REHABILITATION OF INFRASTRUCTURE WORKS IN SECTOR 3 & 3-A IN HAWKS BAY,
SCHEME 42"
(CONTRACT NO: INFRA-000)







STAMP OFFICE KARACHI

For: S. Zahid Sar

NIC: 276-2012


Via: 276-2012

E. No. 276-2012

Car. Office Karachi
27/6/12

CONTRACT AGREEMENT

"REHABILITATION OF INFRASTRUCTURE WORKS IN SECTOR 3 & 3-A IN HAWKS BAY,
SCHEME 42"
(CONTRACT NO: INFRA-006)



STAMP OFFICE DIRECTOR GENERAL KARACHI

For: S. S. A. al-Hariri Sar

NIC: 27.6.2012

Via: 27.6.2012

on: 27.6.2012

E. No. 27.6.2012


S. S. A. al-Hariri Sar
27/6/12

CONTRACT AGREEMENT

**"REHABILITATION OF INFRASTRUCTURE WORKS IN SECTOR 3 & 3-A IN HAWKS BAY,
SCHEME 42"
(CONTRACT NO: INFRA-006)**

[Handwritten signature]

[Handwritten signature]
S. S. A. al-Hariri Sar
27/6/12



STAMP OFFICE KARACHI

Issued to S. Zia ul Haq Saeed

NI: 29.6.2012

VI: 29.6.2012

E. No. 29.6.2012

S. Zia ul Haq Saeed
29/6/12

CONTRACT AGREEMENT

**"REHABILITATION OF INFRASTRUCTURE WORKS IN SECTOR 3 & 3-A IN HAWKS BAY,
SCHEME 42"**
(CONTRACT NO: INFRA-006)

[Handwritten signature]

[Handwritten signature]
LDA



STAMP OFFICE OF KARACHI

Issued to S. Zahid Hussain

Value 2776-2012

or Bawal 2776-2012

E. No. 2776-2012

For Officer-in-Charge
S. Zahid Hussain

CONTRACT AGREEMENT

"REHABILITATION OF INFRASTRUCTURE WORKS IN SECTOR 3 & 3-A IN HAWKS BAY,
SCHEME 42"
(CONTRACT NO: INFRA-006)



STAMP OFFICE KARACHI

Serial No. S-214/16/2012

NO. 276/2012

on Date 22/6/2012

E. No. 276/2012


Stamp Office Karachi
[Signature]

CONTRACT AGREEMENT

**"REHABILITATION OF INFRASTRUCTURE WORKS IN SECTOR 3 & 3-A IN HAWKS BAY,
SCHEME 42"**
(CONTRACT NO: INFRA-008)

[Signature]

[Signature]



STAMP OFFICE KARACHI

Issue No. S. 22/1/1052502

NIC No. 29.6.2012

OR No. 29.6.2012

E. No. 29.6.2012

Signature
29/6/12

CONTRACT AGREEMENT

**"REHABILITATION OF INFRASTRUCTURE WORKS IN SECTOR 3 & 3-A IN HAWKS BAY,
SCHEME 42"**
(CONTRACT NO: INFRA-006)

Signature

Signature



STAMP OFFICE KARACHI

Issued to S. Zahid Hussain

NIC No. _____
Vid. No. 276/2017
on Date 29.6.2017
E. No. 296/2017

Official Stamp
29/6/17

CONTRACT AGREEMENT


"REHABILITATION OF INFRASTRUCTURE WORKS IN SECTOR 3 & 3-A IN HAWKS BAY,
SCHEME 42"
(CONTRACT NO: INFRA-006)

[Handwritten Signature]

[Handwritten Signature]

CONTRACT AGREEMENT


REHABILITATION OF INFRASTRUCTURE WORKS IN THE ...
...
CONTRACT NO. ...



Handwritten notes and signatures in Urdu script, including a signature that appears to read "محمد رفیق" (Muhammad Rafiq).

CONTRACT AGREEMENT

"REHABILITATION OF INFRASTRUCTURE WORKS IN SECTOR 3 & 3-A IN HAWKSBAY,
SCHEME 42"
(CONTRACT NO. INFRA-005)




STAMP
No. 10 20 30 40 50
M. 1000
N. 1000
S. 1000
E. NO. 1000
(Faint handwritten text and a signature are visible below the stamp.)

CONTRACT AGREEMENT

"REHABILITATION OF INFRASTRUCTURE WORKS IN SECTOR 3 & 3-A IN HAWKSBAY"
SCHEME 42"
(CONTRACT NO. INFRA-603)

(Handwritten signature)

(Handwritten signature)



STAMP OF _____
No. _____
Date _____
E. No. _____


Signature
28/6/12

CONTRACT AGREEMENT

"REHABILITATION OF INFRASTRUCTURE WORKS IN SECTOR 3 & 3-A IN HAWKS BAY,
SCHEME 42"
(CONTRACT NO. INFRA-003)

Signature

Signature




STAMP OF THE GOVERNMENT OF PUNJAB
No. 22 of 1999
Date: 12/11/99
E. NO. 12/11/99

The Chief Engineer
12/11/99

CONTRACT AGREEMENT

"REHABILITATION OF INFRASTRUCTURE WORKS IN SECTOR 3 & 3-A IN HAWKS BAY,
SCHEME 42"
(CONTRACT NO: INFRA-006)




STAMP OFFICE
Date: 22/04/2011
No. _____
U. _____
D.P. _____
E. NO. _____

Signature
22/4/11

CONTRACT AGREEMENT

"REHABILITATION OF INFRASTRUCTURE WORKS IN SECTOR 3 & 3-A IN HAWKS BAY,
SCHEME 42"
(CONTRACT NO: INFRA-000)




STAMP OFFICE GENERAL (COMMERCIAL)
No. 1000/1000
N. 1000
V. 1000
D.D. 1000
E. No. 1000

Official Stamp
2/6/11

CONTRACT AGREEMENT

"REHABILITATION OF INFRASTRUCTURE WORKS IN SECTOR 3 & 3-A IN HAWKS BAY,
SCHEME 42"
(CONTRACT NO: INFRA-905)



STAMP OFFICE
Date: 22/04/2012
HT: _____
V: _____
DR: _____
E. No. _____


Signature
22/4/12

CONTRACT AGREEMENT

"REHABILITATION OF INFRASTRUCTURE WORKS IN SECTOR 3 & 3-A IN HAWKS BAY,
SCHEME 42"
(CONTRACT NO. INFRA-008)

Signature


Signature



STAMP OF THE STATE BANK OF INDIA
No. 3000
Date: 12/11/12
E. No. 12/11/12
Sd/-
12/11/12

CONTRACT AGREEMENT

"REHABILITATION OF INFRASTRUCTURE WORKS IN SECTOR 3 & 3-A IN HAWKS BAY,
SCHEME 42"
(CONTRACT NO: INFRA-000)

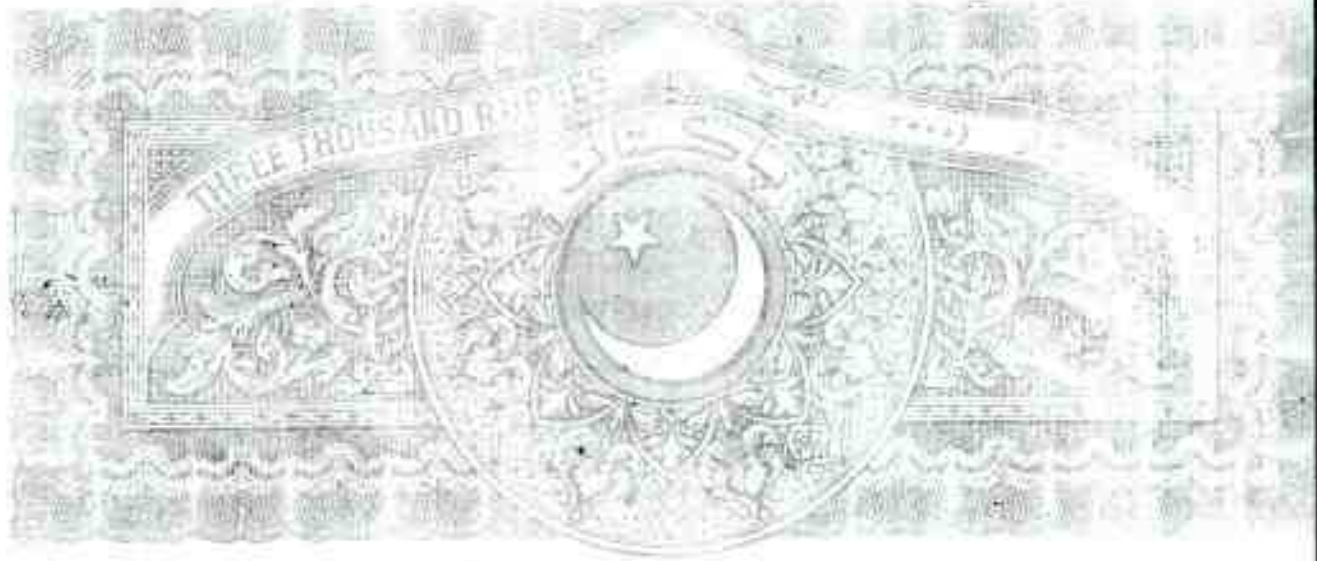

STAMP OF THE OFFICE OF THE
DIRECTOR OF THE
OFFICE OF THE
DIRECTOR OF THE
OFFICE OF THE
E. No. _____

*in Office Director
2/16/11*

CONTRACT AGREEMENT

**"REHABILITATION OF INFRASTRUCTURE WORKS IN SECTOR 3 & 3-A IN HAWKS BAY,
SCHEME 42"**
(CONTRACT NO. INFRA-006)

SUMMARY BILL OF QUANTITIES


/ Owner : Lyari Development Authority
 e of Project : Infrastructure Development Works at Hawksbay Scheme -42
 e of Work : Rehabilitation of Infrastructure Works in Sector 3 & 3A. (Hawksbay Scheme - 42)
 on : Hawksbay
 ract No. : INFRA - 06


Sr. No.	Description	Amount
1	Roads Work	5,00,85,641. ¹²
2	Laying Sewer Lines	40,80,542. ⁰⁰
2	Laying Water Supply Lines	1,91,03,285. ⁰⁰
Total (Rs.)		7,32,69,468. ¹²


Seventy Three Millions Two Hundred Sixty
 Nine Thousands In Words Four Hundred Sixty Eight Only


 CONTRACTOR




 04/6/2012


 4/6/2012



 4/6

Pay Order
 Mafzari Bank
 PO: 016.0022477

BILL OF QUANTITIES

Owner : Lyari Development Authority
 Project : Infrastructure Development Works at Hawksbay Scheme - 42
 Work : Rehabilitation of Infrastructure Works in Sector 3 & 3A (Hawksbay Scheme - 42)
 Road : Rehabilitation of Road
 Location : Hawksbay
 Project No. : INFRA - 06

Particulars	Qty.	Unit	Rate		Amount (Rs.)
			In Figure	In Words	
<i>All Cement Concrete in contact with earth to be carried out with S.R. Cement</i> <i>Surface steel formwork is to be used in all the items of R.C.C</i>					
MAIN CARRIAGE WAY					
Jungle clearance and removing with 100ft: Thin jungle	1,411,180	Sq. Ft.	4.00	(Four)	56,44,720. ⁰⁰
Earth work for embankment from borrow pits including laying in 6 inch layers, clod breaking, ramming, dressing & compaction by sheep foot / power roller with optimum moisture content 95-100% of modified A.A.S.H.T.O dry density complete, upto an average lead of 5 miles and lift upto 5 ft (in ordinary soil). (Compacted depth will be considered for payment)	4,105,858	Cft.	7.00	(Seven)	28,741,006. ⁰⁰
Preparing base course including supplying and spreading metal of approved quality, properly graded to maximum size of 1-1/2" in required thickness to proper camber and grade including supplying and spreading 150ft. screening and non plastic quarry fine, filling depressions with stone metal after initial rolling & watering and compacting the same so as to achieve 100% density as per modified AASHTO specification (compacted thickness will be considered for payment). Rate includes providing and using templates, camber plates, screens, forms as directed also cost of material T & P and carriage upto site of work.	46,236	Cft.	55.00	(Fifty Five)	25,42,987. ⁰⁰
Providing surface dressing two coats on new or existing surface: 1st coat with 30lbs. bitumen and 4.00 Cft of bajri of required size per %Sft, cleaning the road surface & rolling etc., 2nd coat with 25lbs. bitumen and 3.50 Cft of bajri of required size %Sft including cleaning the road surface, rolling etc., complete. Rate includes all cost of materials T&P and cartage of material upto site of work.	185,217	Sft.	55.00	(Fifty Five)	103,51,985. ⁰⁰


ASIA-HIL-HAC & SONS
 Proprietor



Executive Engineer
 Hawksbay Division II
 Lyari Development Authority


Particulars	Qty.	Unit	Rate		Amount (Rs.)
			In Figure	In Words	
Providing and laying edge stone 12" (305 mm) long, 4" (229 mm) deep and 6" (152 mm) wide obtained from approved quarry, chisel dressed on top and sides, laid in cement mortar 1:4 ruled cement pointing in cement mortar 1:3, including cost of excavation, back filling of excavated stuff and its disposal within one chain (30.5 m) lead as desired.	11,220	Rt	250.00	(Two hundred Fifty)	28,05,000.00
Total Rs.					

500,85,641.00

Five Millions Eighty Five Thousands Six hundred and forty Seven One Only.

TRACTOR

[Handwritten signatures]



Proprietor

Executive Engineer
Hawkesnab

[Handwritten signature]

BILL OF QUANTITIES

Owner : Lyari Development Authority
 Project : Infrastructure Development Works at Hawksbay Scheme - 42
 Work : Rehabilitation of Infrastructure Works in Sector 3 & 3A. (Hawksbay Scheme - 42)
 Item : Laying Sewer Line
 Location : Hawksbay
 Contract No : INFRA - 06

Particulars	Qty.	Unit	Rate		Amount (Rs.)
			In Figure	In Words	
At Cement Concrete in contact with earth to be carried out with S.R. Cement Surface steel formwork is to be used in all the items of R.C.C.					
ITEMS					
Excavation for pipe lines in trenches, and pits in all kind of soils i/c trimming and dressing sides to true alignment and shape levelling of beds of trenches to correct level and grade, cutting joint holes and disposal of surplus earth after backfilling in trenches, in the depression or as directed by the engineer with in the boundaries of the scheme, providing fence guard, lights, flags and temporary crossings for non vehicular traffic where ever required including all lead & lift upto 5 ft.	11,735	Cft	7.0	(Seven)	82,145. ⁰⁰
Excavation for pipe lines in trenches, and pits in soft rock by hammering and chiselling where blasting is not practicable or prohibited i/c trimming and dressing sides to true alignment and shape levelling of beds of trenches to correct level and grade, cutting joint holes and disposal of surplus earth after backfilling in trenches, in the depression or as directed by the engineer with in the boundaries of the scheme, providing fence guard, lights, flags and temporary crossings for non vehicular traffic where ever required including all lead & lift upto 5 ft.	1,467	Cft	8.0	(Eight)	11,736. ⁰⁰
Excavation for pipe lines in trenches, and pits in hard rock by hammering and chiselling where blasting is not practicable or prohibited i/c trimming and dressing sides to true alignment and shape levelling of beds of trenches to correct level and grade, cutting joint holes and disposal of surplus earth after backfilling in trenches, in the depression or as directed by the engineer with in the boundaries of the scheme, providing fence guard, lights, flags and temporary crossings for non vehicular traffic where ever required including all lead & lift upto 5 ft.	1,467	Cft	8.0	(Eight)	11,736. ⁰⁰
Refilling the excavated stuff in trenches in 6" thick layer including watering, ramming, to full compaction etc complete.	12,433	Cft	10.0	(Ten)	124,330. ⁰⁰
Cement concrete plain including placing compacting, finishing and curing, complete (including screening and washing of stone aggregate without shuttering, Ratio 1:4:8, (for Manhole)	205	Cft	10.0	(One Hundred & Ten)	2050 2,250. ⁰⁰


Executive Engineer
 Hawksbay Division
 Lyari Development Authority


(Handwritten signature)

Particulars	Qty.	Unit	Rate		Amount (Rs.)
			In Figure	In Words	
Reinforced cement concrete work using S.R. Cement including all labour and material except the cost of steel reinforcement and its labour for bending and binding which will be paid separately. This rate also includes all kinds of forms moulds, lifting shuttering curing rendering and finishing the exposed surface (including screening and washing of shingle). (Ratio 1:1-1/2:3) For Manhole Wall & Bed Wall	5,451	Cft.	275.0	(Two Hundred Seventy Five)	14,99,025.00
Cement Plaster 1:4 upto 20' height (3/4" thick) (Outer Surface of Existing Manhole)	6,375	Sft	55.0	(Fifty Five)	3,50,625.00
Providing and laying (Fiber Cement) FC Sewerage pipe (internally coated with epilax paint) i/c transportation, loading, unloading at the site of work stacking, cutting and fitting in trenches with comet joint and a pair of rubber rings. 10' Dia Pipe	978	Rft	978.0 540.0	(Five Hundred Forty)	5,28,120.00
Providing & laying Deformed steel reinforcement bars having minimum yield stress of 60,000 psi with and including the cost of straightening, cutting, bending, binding, wastage, and such overlaps as are not shown over the drawings, placing in position on cement concrete 1:2:4 precast or m.s.chairs, tying with binding wire, cost of chair and wires etc. in all kinds of RCC work in foundation, basement, plinth and ground floor of building including septic tank and under ground tank and in projections for future extension. (For Manhole)	248	Cwt.	5730.0	(Five Thousand Seven Hundred)	14,13,600.00
Providing & filling coarse sand in trenches in 6" thick layers, watering and compacting to required level etc.	1,467	Cft.	25.0	(Twenty five)	36,675.00
Total Rs.					40,80,542.00


Rupees Forty Lacs Eighty Thousands Five Hundreds
In Words Forty Two ONLY.


CONTRACTOR



 ASLA-UL-HAQ & SONS

Proprietor

Executive Engineer
Hawksbay Division
Urban Development


BILL OF QUANTITIES

OWNER : LYARI DEVELOPMENT AUTHORITY
 PROJECT : INFRASTRUCTURE DEVELOPMENT WORKS AT HAWKS BAY SCHEME-42
 WORK : REHABILITATION OF INFRASTRUCTURE WORKS IN SECTOR 3 & 3A
 (HAWKS BAY SCHEME - 42)
 : LAYING WATER SUPPLY LINES
 : HAWKS BAY, KARACHI
 CT NO : INFRA - 05

Particulars	Qty.	Unit	Rate		Amount (Rs.)
			In Figure	In Words	
Concrete in contact with earth to be carried out Cement					
Steel formwork to be used in all the items of R.C.C.					
PLY LINES					
Excavation for pipe lines in trenches, and pits in hard of soil i/c trimming and dressing sides to alignment and shape leveling of beds of trenches to correct level and grade, cutting joint and disposal of surplus earth (after backfilling in trenches, in the depression or as directed by Engineer with in the boundaries of the scheme), providing fence guard, lights, flags and temporary crossing for non vehicular traffic where ever required i/c all lead and lift upto 5 ft.	289,775	Cft	6.0	(Six)	1738,650. ⁰⁰
Plain concrete plain 1:4:8 including placing, compacting, finishing and curing, complete (including screening and washing of stone aggregate without shuttering.) (For Chamber)	5,438	Cft	100.0	(Hundred)	5,43,800. ⁰⁰
Backfilling the excavated stuff in trenches 6" thick layers including watering, ramming to full compaction, etc, complete	230,807	Cft	5.0	(Five)	11,54,035. ⁰⁰
Plain concrete 1:2:4 plain including placing, compacting, finishing and curing, complete (including screening and washing of stone aggregate) including shuttering etc., complete. (For Chamber)	1,440	Cft	250.0	(Two Hundred Fifty)	360,000. ⁰⁰
Reinforced cement concrete work including all labour and material except the cost of steel reinforcement and its labour for bending and fixing which will be paid separately. This rate also includes all kinds of forms moulds, lifting shuttering curing rendering and finishing the exposed surface (including screening and washing of shingle). (Ratio 1:2:4 for Chamber and Slabs)	6,986	Cft	300. ⁰⁰	(Three Hundred)	20,95,800. ⁰⁰
Fabrication of mild steel reinforcement for plain concrete including cutting bending, fixing in position, making joints and fastenings including cost of binding wire (also includes removal of rust from bars.) (For Chamber)	318	Cwt	5500. ⁰⁰	(Five Thousand Five hundred)	17,49,000. ⁰⁰
Providing and fixing C.I Manhole cover with same i/c cost of material etc. (For Chamber)	160	Cwt	5500. ⁰⁰	(")	880,000. ⁰⁰

Executive Engineer
Hawksbay Division

Particulars	Qty.	Unit	Rate		Amount (Rs.)
			In Figure	In Words	
Providing G.I. Pipe & special etc. including fixing, cutting and fitting complete with and inc the cost of cutting trench upto 2-1/2 ft deep refilling, watering, ramming and disposal of surplus earth within 1 chain and painting two coats of bitumen paint to pipe and specials after cleaning, plumber insulation tape wrapped tightly round pipes and testing to a pressure head of 200ft - 1/2" (15mm) medium grade.	1,600	Rft.	500.0	(Five Hundred)	800,000. ⁰⁰
Providing G.I. Pipe & special etc. including fixing, cutting and fitting complete with and inc the cost of cutting trench upto 2-1/2 ft deep refilling, watering, ramming and disposal of surplus earth within 1 chain and painting two coats of bitumen paint to pipe and specials after cleaning, plumber insulation tape wrapped tightly round pipes and testing to a pressure head of 200ft - 3/4" (20mm) medium grade.	800	Rft.	500.0	(Five Hundred)	400,000. ⁰⁰
Supplying Polyethylene (P.E) pressure pipe and fittings conforming to AWWA-C-906-99 and pressure rating PN-8 with and including the cost of laying in proper position, fitting, jointing (Butt Fusion Joint), testing, disinfecting and commissioning complete including cartage upto site of work, etc. complete.	22,100	Rft.	250.0	(Two Hundred Fifty)	5525000. ⁰⁰
P.E Pipe dia 90mm PN-08	5,600	Rft.	250.0	(")	14,00,000. ⁰⁰
P.E Pipe dia 160mm PN-08	2,000	Rft.	250.0	(")	5,00,000. ⁰⁰
Making connection with Butt Fusion of compression fitting for PE Pipes & Fittings. (PN-10)					
EQUAL / UNEQUAL TEES (PN-10)					
Equal Tee (90 x 90 x 90)	47	No.	500.0		23,500. ⁰⁰
Equal Tee (200 x 200 x 200)	1	No.	500.0		500. ⁰⁰
Un Equal Tee (160 x 90 x 160)	7	Nos.	500.0		3,500. ⁰⁰
Un Equal Tee (200 x 90 x 200)	5	Nos.	500.0		2,500. ⁰⁰
Un Equal Tee (200 x 160 x 200)	1	Nos.	500.0		500. ⁰⁰
ELBOWS / BENDS (PN-10)					
Elbow 90° (90 x 90)	4	Nos.	500.0		2,000. ⁰⁰
Elbow 45° (90 x 90)	3	Nos.	500.0		1,500. ⁰⁰
REDUCERS (PN-10)					
Reducer (200 x 90)	1	Nos.	500.0		500. ⁰⁰
Reducer (200 x 25)	1	Nos.	500.0		500. ⁰⁰
Supplying & stacking river bed sand of approved quality and grading & filling in trenches under pipe as per drawing & direction of Engineer.	29,700	Cft	10.0		297,000. ⁰⁰
Providing and fixing Cast Iron Sluice Valves of approved quality (Local Made) with flanged ends & short pieces if required to each valve, of approved quality and make, complete with bolts and nuts, including the cost of insertion rubber washers, valves to stand specified test pressure, the sluice valve is to be removed after fixing/checking and handing over to department's store. Opening of pipe ends to be closed with ordinary Flanges of required dia, as directed by the Engineer.					
For 160mm dia pipe			5000.0		10,000. ⁰⁰
			500.0		500. ⁰⁰

Particulars	Qty.	Unit	Rate		Amount (Rs.)
			In Figure	In Words	
Supply & fixing 2" dia Double action Air valve (heavy quality Local Made) made according to RWA on 6" dia PE pipe line, fixing in position, testing and commissioning in manhole chambers as per design, drawing & as per direction of the Engineer etc., complete For 2" dia	2	Nos.	5000.00		13,000.00
Making 3/4" dia GI Pipe Service connection from 2" dia PE pipe line with and i/c. cost of PE Topping saddle for 3/4" connection (female end) suitable for PE pressure pipe with Galvanized nuts and bolts., 3/4" dia ferrule along with 3/4" dia GI Service pipe with compressor fittings with 3" including cost of fitting, cutting, trench, backfilling the trench after making connection complete as per the direction and approval of the Engineer.	160	Nos.	10000.00		1600,000.00
Total Rs.					

(Nineteen Million One Hundred Three Thousand Two Hundred Eighty Five ONLY) 19,103,285.
 One Million Ninety One Thousand

In Words

[Handwritten Signature]

TRACTOR

S.S.A. - III - HAO & SONS
 Proprietor

Executive Engineer
 Hawksbay District
 Lyari Development Authority

[Handwritten Signature]

BID EVALUATION REPORT

1. Name of Agency : Lyari Development Authority
2. Tender Reference No : Infra-001
3. Tender description/Name of work : Construction of 60' wide Road in Sector 12 in Hawksbay, Scheme 42
4. Method of Procurement : Single Envelop procedure
5. Tender published : The News, Daily Jang, Kawish dated 11th May 2012.
6. Total Bid sold : 04 Nos
7. Total bid received : 04 Nos
8. Technical Bid Opening date : 04th June 2012.
9. No of Bid technically qualified : 04 Nos
10. Bid(s) Rejected : NA
11. Financial bid opening date : 04th June 2012.
12. Bid Evaluation Report :

S.#	Name of Firm/Bidder	Cost offered by Bidder	Ranking in term of cost	Comparasion of Estimated Cost	Reasons for acceptance /rejection	Remarks
1	2	3	4	5	6	7
01	M/s. Riasat Brothers	Rs 7,96,04,975/-	1 st Lowest	2.26%	Accepted being 1 st lowest	
02	M/s. Samad Khan Baber & Company	Rs 8,46,86,506/-	2 nd Lowest	6.55%	-	
03.	M/s. Abdul sattar & Sons	Rs 8,16,26,378/-			-	
04	M/s. Kamran & Kampany	Not quoted				

Deputy Director (F&A)
Member

Deputy Director (F&A)
Lyari Development Authority

Consultant
Member

Executive Engineer
Member

Executive Engineer
Chairman

EXECUTIVE ENGINEER
Head Office Division
Lyari Development Authority

BID EVALUATION REPORT

1. Name of Agency : Lyari Development Authority
2. Tender Reference No : Infra-006
3. Tender description/Name of : Rehabilitation of Infrastructure works in sector 3 & 3-A in Hawksbay, Scheme 42
4. Method of Procurement : Single Envelop procedure
5. Tender published : The News, Daily Jang, Kawish dated 11th May 2012.
6. Total Bid sold : 04 Nos
7. total bid received : 04 Nos
8. Technical Bid Opening date : 04th June 2012.
9. No of Bid technically qualified : 04 Nos
10. Bid(s) Rejected : NA
11. Financial bid opening date : 04th June 2012.
12. **Bid Evaluation Report :**

S.#	Name of Firm/Bidder	Cost offered by Bidder	Ranking in term of cost	Comparasion of Estimated Cost	Reasons for acceptance /rejection	Remarks
1	2	3	4	5	6	7
01	M/sZiaul Haq & sons	Rs.7,32,69,468/-	1 st Lowest		Accepted being 1 st lowest	
02	M/s. Malik Zaheer Khan	Rs. 7,43,22,110/-	2 nd Lowest			
03.	M/s. Abdul Sattar & company	Rs.7,49,51,328/-				
04	M/s. Kaim Khani Competition International	Not quoted				

Deputy Director (F&A)
Member

Consultant
Member

Executive Engineer
Member

Executive Engineer
Chairman

Deputy Director (F&A)
Lyari Development Authority

EXECUTIVE ENGINEER
Lyari Development Authority
